WEBCENTER SUPPLEMENTAL GUIDE

Back to View

The materials presented in this technical guideline provide specific supplemental information into OUM for the purposes of WebCenter delivery work.The WebCenter Supplemental Guide contains the following components:

WebCenter Overview

This Overview provides a summary of the WebCenter platform:

- Oracle WebCenter Sites
- Oracle WebCenter Portal
- Oracle WebCenter Content
- Oracle WebCenter Social

WebCenter Supplemental Activity Guidelines

The Supplemental Activity Guidelines should be used in conjunction with the standard OUM activity guidelines in order to accomplish WebCenter project delivery work at the activity level.

WebCenter Supplemental Task Guidelines - Inception Phase

The Supplemental Task Guidelines for the Inception phase should be used in conjunction with the standard OUM Task guidelines in order to accomplish WebCenter project delivery work at the task level.

WebCenter Supplemental Task Guidelines - Elaboration Phase

The Supplemental Task Guidelines for the Elaboration phase should be used in conjunction with the standard OUM Task guidelines in order to accomplish WebCenter project delivery work at the task level.

WebCenter Supplemental Task Guidelines - Construction Phase

The Supplemental Task Guidelines for the Construction phase should be used in conjunction with the standard OUM Task guidelines in order to accomplish WebCenter project delivery work at the task level.

WebCenter Supplemental Task Guidelines - Transition Phase

The Supplemental Task Guidelines for the Transition phase should be used in conjunction with the standard OUM Task guidelines in order to accomplish WebCenter project delivery work at the task level.

WebCenter Supplemental Task Guidelines - Production Phase

The Supplemental Task Guidelines for the Production phase should be used in conjunction with the standard OUM Task guidelines in order to accomplish WebCenter project delivery work at the task level.

WebCenter Definitions and Terms

The WebCenter Definition and Terms should be used in conjunction with the standard OUM Definitions and Terms in order to understand terms referenced in this Supplemental Guide.

WebCenter Projects and OUM

WebCenter projects require only a subset of the full list of activities and tasks included within OUM.

When using OUM on your project, it is important to **let the method serve you**, that is, only select the appropriate activities and tasks that you need.

WebCenter Project Workplan (MPP)

OUM provides a generic Project Workplan, in Microsoft Project format, that can be quickly tailored for WebCenter projects.

PDF View

You may also prefer to access this information through the **WebCenter Supplemental Guide (PDF View)** located in the Supplemental Guides section of the Supplemental Guidance page.

Back to Top

PURPOSE

The purpose of this document is to provide an overview of WebCenter use for providing WebCenter solutions, and to provide implementation teams with *supplemental guidance* for the successful planning and execution of WebCenter implementations.

Back to Top

AUDIENCE

This document is intended for practitioners who will be designing and implementing WebCenter solutions based on the OUM (Oracle Unified Method) approach.

Back to Top

HOW TO USE THIS DOCUMENT

This document contains supplemental guidance for planning and executing WebCenter implementations and should be used in conjunction with and not instead of the OUM base method content.

Back to Top

LIMITATIONS TO THIS DOCUMENT

This document does not describe OUM in detail – the reader must review the documentation and training materials referenced below to gain a basic understanding of each.

Back to Top

RELATED DOCUMENTATION AND TRAINING

The following related documentation and training provide additional detailed guidance related to OUM implementations and are prerequisites to this document:

- OUM Method Pack – Desktop Installable or Hosted version
- OUM Training and Accreditation Program

Back to Top

CONTRIBUTORS

Erin Smith, Stephen Hamilton, David Steed, Michael Yehle

Back to Top

Copyright © 2006, 2016, Oracle and/or its affiliates. All rights reserved.

WebCenter OVERVIEW

Back to View

WHAT IS WebCenter?

Oracle WebCenter is the user engagement platform for social businesses, connecting people and information. It brings together a portfolio of portal, web experience management, content, social and collaboration technologies into a single product suite.

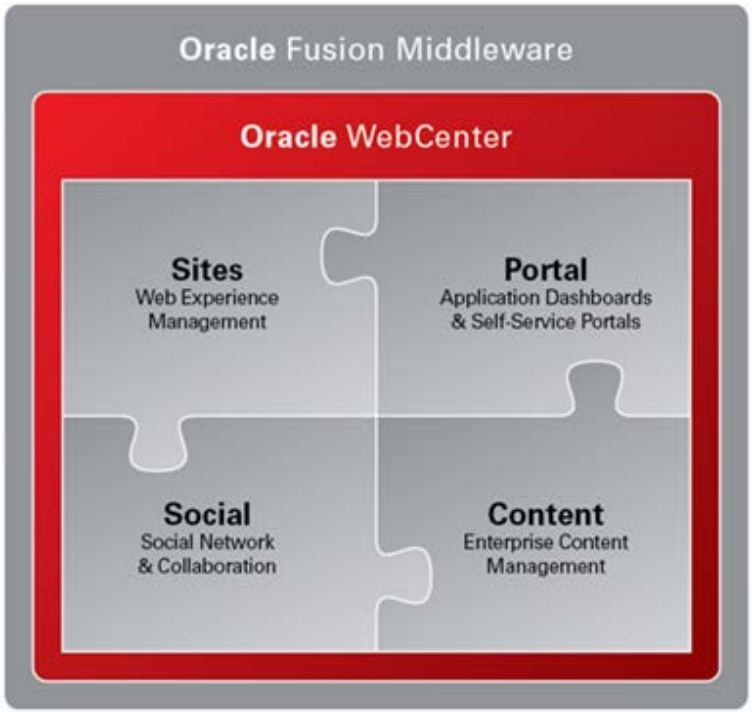

Oracle WebCenter improves customer loyalty and sales by helping marketing-driven organizations deliver contextual and targeted web experiences to users and gives employees anytime, anywhere access to information and applications in context of an interaction and business process through portals and composite applications.

Oracle WebCenter helps people work together more efficiently through contextual collaboration tools that optimizing connections between people, information and applications while managing the complete content lifecycle for the entire organization in a single repository to ensure compliance.

Oracle WebCenter delivers 4 main components:

Oracle WebCenter Sites

- Increase customer sales and loyalty with online engagement optimization by creating, managing, and moderating contextually relevant, targeted and interactive online experiences.
- Optimize customer engagement across Web, mobile, and social channels and manage your large-scale, multi-channel global online presence with integration to enterprise applications.

Oracle WebCenter Portal

- Provide users with intuitive portals and Websites with integrated application content.
- Easily assemble new composite applications using a prebuilt library of reusable components, and access relevant content faster with personalized solutions and integrated social tools.

Oracle WebCenter Social

- Drive enterprise collaboration through natural Conversations using fully integrated social tools including blogs, wikis, ratings, tagging, reviews, polls, and forums.
- Leverage social enterprise building blocks to enable end users to build effective and collaborative communities.

Oracle WebCenter Content

- Remove content silos and update most current documents, images, and rich media files.
- Manage end-to-end content lifecycle from creation to archiving and automate business processes with pre-built enterprise application integrations.

Back to Top

WebCenter RELATED INFORMATION

Additional information about Oracle WebCenter can be found online:

External Websites

- Oracle.com
- Oracle Technology Network

Social Media

- LinkedIn - Oracle Social Enterprise group
- Facebook - Oracle WebCenter

Back to Top

ORACLE

Copyright © 2006, 2016, Oracle and/or its affiliates. All rights reserved.

WebCenter Sites OVERVIEW

Back to View

WHAT IS WebCenter Sites?

Web Experience Management

Enables marketers and business users to easily create and manage contextually relevant, social, and interactive online experiences across multiple channels on a global scale.

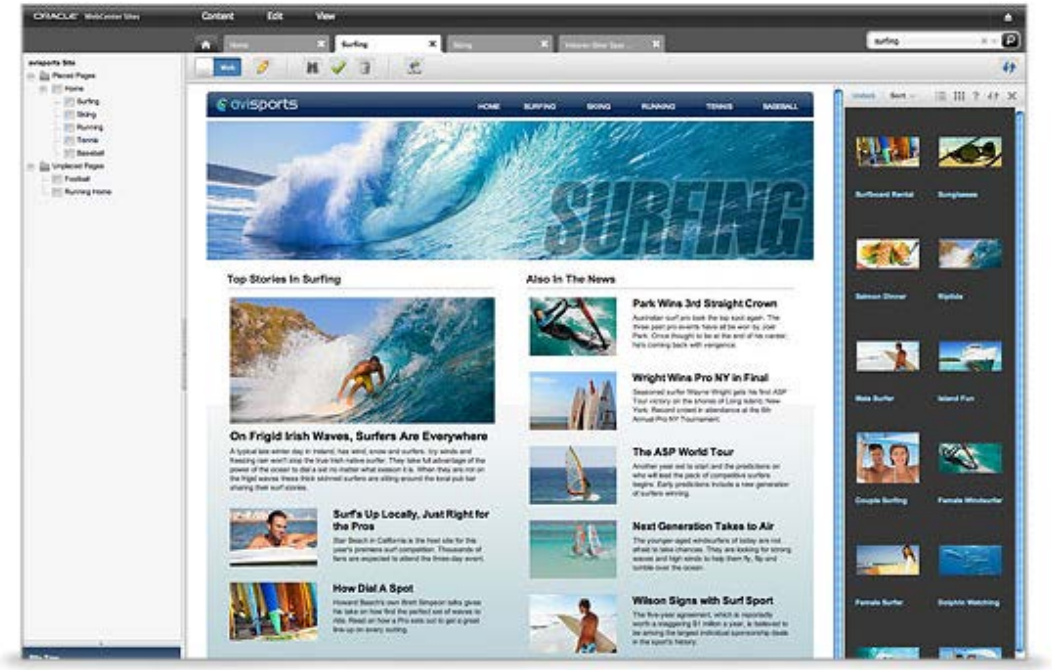

Back to Top

WHAT DOES WebCenter Sites PROVIDE?

WebCenter Sites - Enables marketers and business users to easily create and manage contextually relevant, social, and interactive online experiences across multiple channels on a global scale.

WebCenter Sites Satellite Server - Enables organizations to deliver segmented, targeted, and dynamically assembled content across global Web properties with rapid

response times and intelligent edge caching to optimize and speed the delivery of dynamic Web experiences.

WebCenter Sites Mobility Server - Easily extend your Web presence to mobile devices and deliver multi-channel marketing and customer experience initiatives while saving significant time, money, and effort in managing mobile sites.

Back to Top

RELATED DOCUMENTATION AND TRAINING

The following related documentation and training provide additional detailed guidance related to OUM and WebCenter Content implementations and are prerequisites to this document:

- OUM Method Pack – Desktop Installable or Hosted version

Back to Top

ORACLE

Copyright © 2006, 2016, Oracle and/or its affiliates. All rights reserved.

WebCenter Portal OVERVIEW

Back to View

WHAT IS WebCenter Portal?

Oracle **WebCenter Portal** consolidates the user experience capabilities from a significant portfolio of portal products and related technologies to deliver intuitive user experiences for the enterprise that are seamlessly integrated with enterprise applications.

- Prebuilt library of rich components for enhancing existing enterprise or creating new composite applications
- Flexible application integration tooling for extending application or back-office capabilities and services into portals, websites, and composite applications
- Innovative social tools enable contextual access to content and dynamic personalization of solutions

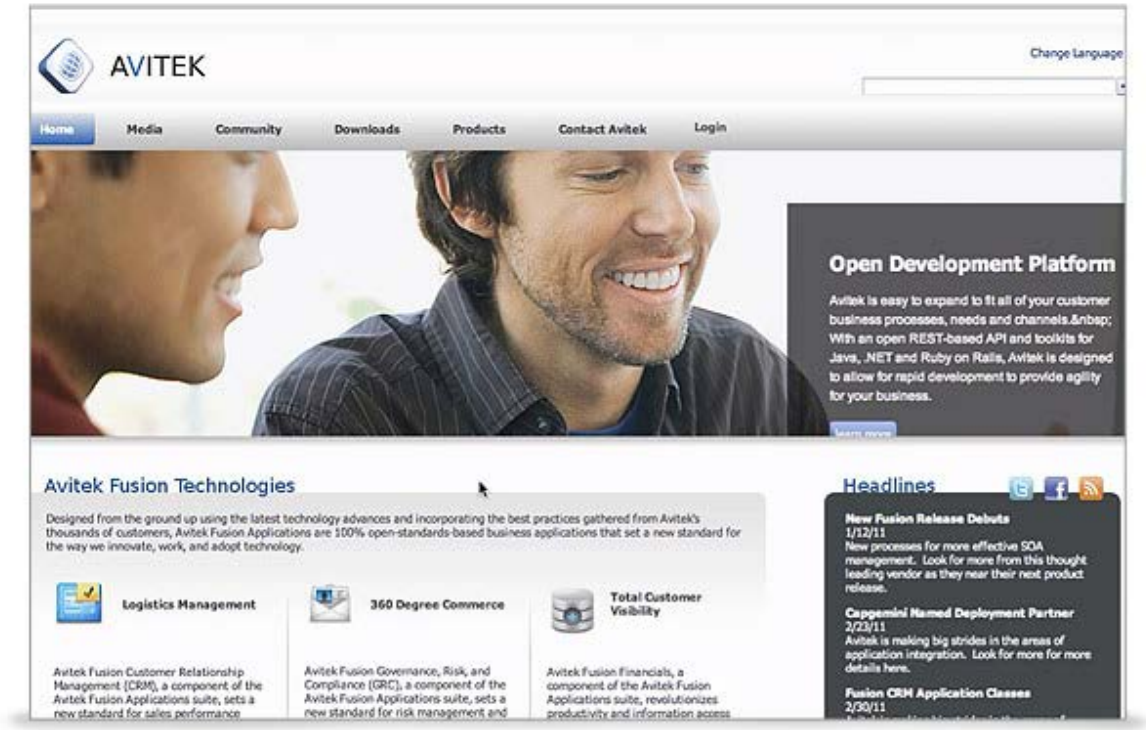

Back to Top

WHAT DOES WebCenter Portal PROVIDE?

Framework - The next generation of portal building platform that enables developers to create pixel perfect internet sites and composite portal applications with a radically

reduced effort. Building portal resources such as navigation, page templates, skins and other portal artifacts are centrally managed in a single resource management tool optimized for team development.

Spaces - Out-of-the-box social and collaborative portal application for business users to collaborate in teams, build business social networks, manage personal information, build departmental portals, intranets, and dynamic online communities without relying on IT.

Services - Enterprise-ready social computing services such as wikis, blogs, RSS, activity stream, activity graph, content management and publishing, discussion forums, tags, links, social networking, polls, comments, ratings, BPEL workflows, and analytics can be embedded directly into applications. The out-of-the-box UIs can be easily customized at run time and development of new UI components on top of these services is easy by using our complete set of REST APIs.

Document Capture - Streamlines the capture process of paper and electronic documents.

Back to Top

RELATED DOCUMENTATION AND TRAINING

The following related documentation and training provide additional detailed guidance related to OUM and WebCenter Content implementations and are prerequisites to this document:

- OUM Method Pack – Desktop Installable or Hosted version
- WebCenter Portal Product Documentation

Back to Top

ORACLE

Copyright © 2006, 2016, Oracle and/or its affiliates. All rights reserved.

WebCenter Content OVERVIEW

Back to View

WHAT IS WebCenter Content?

Oracle **WebCenter Content** provides the most complete, open, and unified enterprise content management (ECM) platform – enabling customers to integrate and implement a solution with the lowest total cost of ownership.

Key features of WebCenter Content are:

- Single, unified Web-based repository
- Core content services – version control, security, indexing & search, metadata, subscription, replication, etc.
- Conversion of 500+ file formats to Web-viewable formats
- Archiving & file store management
- Document management
- Content publishing
- Digital asset management
- Document imaging
- Business process management & workflow
- DoD5015.2 v. 3 certified records & retention management
- Information rights management

Back to Top

WHAT DOES WebCenter Content PROVIDE?

Document Management

- Effectively and efficiently capture, secure, share and distribute digital and paper-based documents and reports.
- Save money and improve operational efficiencies by streamlining communications, automating routine tasks.
- Lower costs related to the printing, shipping, and storage of business documents.

Capture and Imaging

- End-to-end management of document images within enterprise business processes.
- Intelligent data capture, and provides annotation and markup of images, automates routing and approvals.
- Scalable repository supporting enterprise-wide applications.
- Quickly automate business processes in Oracle E-Business Suite, PeopleSoft Enterprise, and JD Edwards EnterpriseOne.

Content Publishing

- Enables documents and web pages to be published as Web sites.
- Maintain accurate, timely, and current Web content with consistent branding and presentation.
- Provides role-based tools to ensure high-productivity and fast updates to critical content.

Digital Asset Management

- Provides industry-leading digital asset management to store, find, and access your brand assets.
- Allows users to automate the creation of thumbnails and renditions, convert high-resolution assets into Web-friendly formats.
- Storyboard video to help you select key scenes.

Records Management

- Manage both electronic and physical records.
- Apply your records management policies and practices on both records and non-records content
- Apply policies and actions on content in remote repositories such as file systems, content management systems, and email archives, enabling you to place holds from a single console.

Back to Top

WHAT IS WebCenter Content: CORE CAPABILITIES?

Core Capabilities is a WebCenter Content platform that enables customers to utilize document management, Web content management, and digital asset management functionality to build and complement their business applications. Building a strategic WebCenter Content infrastructure for content and applications helps customers to reduce their costs, easily share content across the enterprise, minimize risk, automate expensive, time-intensive and manual processes, and consolidate multiple Web sites onto a single platform for centralized management. Through user-friendly interfaces, roles-based authentication and security models, Core Capabilities empowers users throughout the enterprise to view, collaborate on, or retire content, ensuring that all accessible distributed or published information is secure, accurate and up-to-date.

Web Content Management

- in-context Web site contribution, preview, updates, and approvals
- e-mail notifications during workflow
- library services, including full-text search, check-in or check-out, and version control
- flexible metadata and security
- template-based pages
- libraries of reusable components and XML-based fragments

native content conversion to Web-viewable formats, including HTML, XML, and PDF
- dynamic delivery and scheduled publishing models
- personalized content delivery
- content release and expiration
- full digital asset and records management

Digital Asset Management

- automatically create thumbnails for easy search and retrieval of assets
- convert high-resolution legacy images and videos to Web-friendly format
- pinpoint specific video scenes using story board
- automatically create multiple rendition sets for multiple uses
- select assets and download in one operation
- automatically format images to appropriate size, shape, resolution, and aspect ratio

Back to Top

RELATED DOCUMENTATION AND TRAINING

The following related documentation and training provide additional detailed guidance related to OUM and WebCenter Content implementations and are prerequisites to this document:

- OUM Method Pack – Desktop Installable or Hosted version
- WebCenter Content Product Documentation

Back to Top

ORACLE

Copyright © 2006, 2016, Oracle and/or its affiliates. All rights reserved.

WebCenter Social OVERVIEW

Back to View

WHAT IS WebCenter Social ?

Oracle **WebCenter Social**, which includes Oracle Social Network and Oracle WebCenter Real-Time Collaboration, delivers secure social networking and enterprise collaboration tools for the enterprise.

- Enable enterprise collaboration through contextual Conversations and real-time updates.
- Drive productivity with activity streams, content annotation, and business application integration.
- Offer simple and rapid means to set up collaborative communities and start working together.

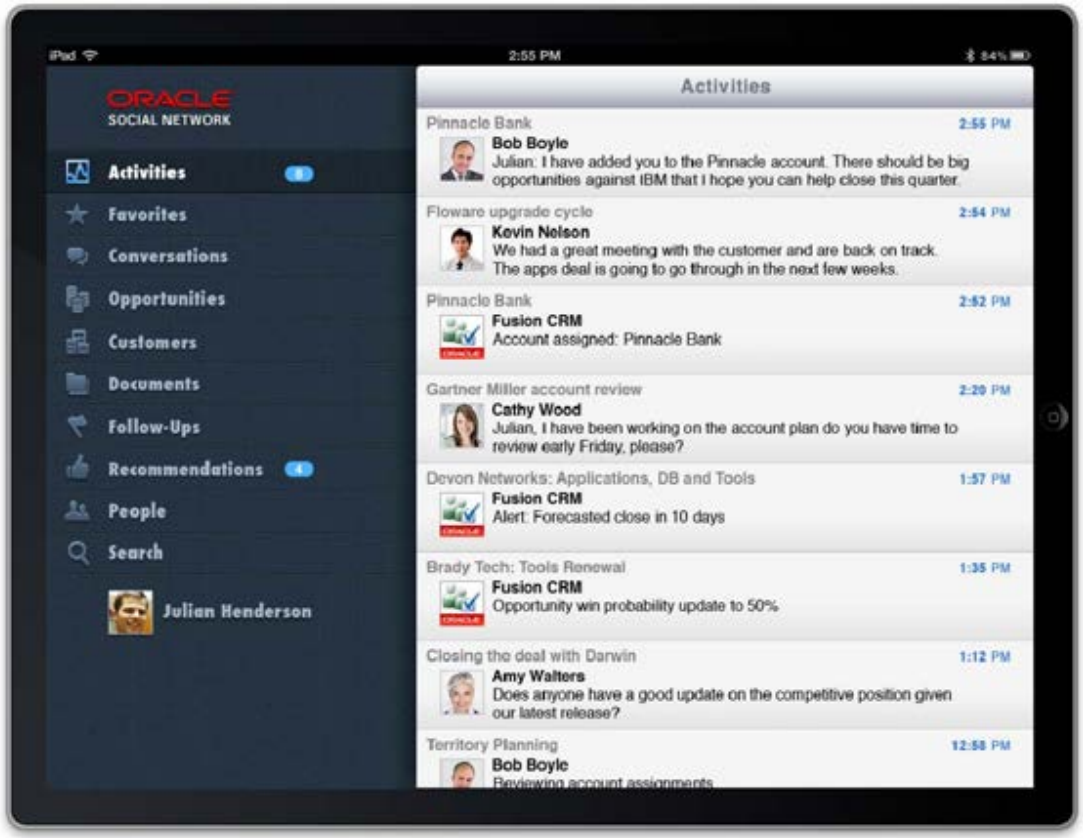

Back to Top

ORACLE SOCIAL NETWORK

Oracle Social Network is a secure private network that provides a broad range of social tools designed to capture and preserve information flowing between people, enterprise applications, and business processes. By connecting users with their most critical applications, Oracle Social Network provides contextual, real-time communication within and across enterprises. With Oracle Social Network, the users have the tools they need to collaborate quickly and efficiently, while leveraging the organization's collective expertise to make informed decisions and drive business forward.

Back to Top

ORACLE WebCenter REAL-TIME COLLABORATION SOCIAL NETWORK

Oracle WebCenter Real-Time Collaboration improves efficiency and productivity by enabling users to connect and collaborate with others via instant messaging, presence, chat rooms, and web and voice conferencing. It complements other Enterprise 2.0 services available in Oracle WebCenter by offering real-time collaboration capabilities to users who require direct interaction and immediate response. It can be deployed standalone or with Oracle WebCenter.

Back to Top

RELATED DOCUMENTATION AND TRAINING

The following related documentation and training provide additional detailed guidance related to OUM and WebCenter Connect implementations and are prerequisites to this document:

- OUM Method Pack – Desktop Installable or Hosted version

Back to Top

Copyright © 2006, 2016, Oracle and/or its affiliates. All rights reserved.

Oracle
Unified Method

Cloud
Home Page

OUM WebCenter Supplemental Guide

Resources | PDF View

Method Navigation | Current Page Navigation

WEBCENTER SUPPLEMENTAL ACTIVITY GUIDELINES

Back to View

The Activity Guidelines are provided to assist the project team in performing certain key tasks in an OUM-based WebCenter project. OUM defines an activity as "a set of tasks related either by topic, dependencies, data, common skills or work products."

Use the WebCenter supplemental activity guidance provided on the left side of this table, in conjunction with the standard OUM Activity overview on the right side of the table, in order to understand how WebCenter impacts specific OUM activities.

Activity ID	WebCenter Supplemental Activity Guidelines	OUM Activity Overview (Links in this column refer to the OUM Activity Guidelines files)
Inception		
A.ACT.GBRI	Gather Business Requirements - Inception	Gather Business Requirements - Inception
A.ACT.ECBB	Establish Current Business Baseline	Establish Current Business Baseline
A.ACT.GR	Gather Solution Requirements	Gather Solution Requirements
A.ACT.CR	Consolidate Solution Requirements	Consolidate Solution Requirements
A.ACT.CCPI	Create Conceptual Prototype - Inception	Create Conceptual Prototype - Inception
A.ACT.GSP	Gather Supporting Requirements	Gather Supporting Requirements
A.ACT.TPT	Train Project Team	Train Project Team
A.ACT.LCOB	Lifecycle Objective Milestone	Lifecycle Objective Milestone
Elaboration		
B.ACT.DPS	Define Project Strategy	Define Project Strategy
B.ACT.DI	Define Infrastructure	Define Infrastructure
B.ACT.PEE	Prepare Environments - Elaboration	Prepare Environments - Elaboration
B.ACT.GBRE	Gather Business Requirements - Elaboration	Gather Business Requirements - Elaboration
B.ACT.DTP	Develop Test Plans	Develop Test Plans
B.ACT.SSC	Specify Software Configuration	Specify Software Configuration
B.ACT.PVC	Prototype and Validate Configuration	Prototype and Validate Configuration
B.ACT.PGA	Perform Gap Analysis	Perform Gap Analysis

B.ACT.DUCM	Develop Use Case Model	Develop Use Case Model
B.ACT.CCPE	Create Conceptual Prototype - Elaboration	Create Conceptual Prototype - Elaboration
B.ACT.CS	Consolidate Specification	Consolidate Specification
B.ACT.BSA	Baseline Software Architecture	Baseline Software Architecture
B.ACT.DUCD	Develop Use Case Details	Develop Use Case Details
B.ACT.AE	Analyze - Elaboration	Analyze - Elaboration
B.ACT.DE	Design - Elaboration	Design - Elaboration
B.ACT.DCCTSE	Develop Custom Component Test Scripts - Elaboration	Develop Custom Component Test Scripts - Elaboration
B.ACT.DSTSE	Develop System Test Scenarios - Elaboration	Develop System Test Scenarios - Elaboration
B.ACT.DVCSP	Develop and Validate Custom Software Prototypes	Develop and Validate Custom Software Prototypes
B.ACT.PCCTE	Perform Custom Component Testing - Elaboration	Perform Custom Component Testing - Elaboration
B.ACT.PSTE	Perform System Test - Elaboration	Perform System Test - Elaboration
B.ACT.PPM	Plan Performance Management	Plan Performance Management
B.ACT.PACDE	Prepare to Acquire and Convert Data - Elaboration	Prepare to Acquire and Convert Data - Elaboration
B.ACT.LCAR	Lifecycle Architecture Milestone	Lifecycle Architecture Milestone
Construction		
C.ACT.FR	Finalize Requirements	Finalize Requirements
C.ACT.AC	Analyze - Construction	Analyze - Construction
C.ACT.DC	Design - Construction	Design - Construction
C.ACT.PTP	Perform Test Planning	Perform Test Planning
C.ACT.PEC	Prepare Environments - Construction	Prepare Environments - Construction
C.ACT.DCCTSC	Develop Custom Component Test Scripts - Construction	Develop Custom Component Test Scripts - Construction
C.ACT.DSTSC	Develop System Test Scenarios - Construction	Develop System Test Scenarios - Construction
C.ACT.DSITS	Develop Systems Integration Test Scenarios	Develop Systems Integration Test Scenarios
C.ACT.ICC	Implement Custom Components	Implement Custom Components
C.ACT.PCCTC	Perform Custom Component Testing - Construction	Perform Custom Component Testing - Construction
C.ACT.PST	Prepare for System Test	Perform for System Test
C.ACT.PSTC	Perform System Test - Construction	Perform System Test - Construction
C.ACT.PSIT	Perform Systems Integration Test	Perform Systems Integration Test
C.ACT.PPT	Prepare for Performance Testing	Prepare for Performance Testing
C.ACT.PT	Prepare for Transition	Prepare for Transition
C.ACT.PCO	Prepare for Cutover	Prepare for Cut over
C.ACT.TI	Test Infrastructure	Test Infrastructure
C.ACT.PACDC	Prepare to Acquire and Convert Data - Construction	Prepare to Acquire and Convert Data - Construction
C.ACT.ACDC	Acquire and Convert Data - Construction	Acquire and Convert Data - Construction
C.ACT.PD	Produce Documentation	Produce Documentation
C.ACT.DEUT	Design End-User Training	Design End-User Training

C.ACT.BEUT	Build End-User Training	Build End-User Training
C.ACT.TEUC	Train End Users - Construction	Train End Users - Construction
C.ACT.IOCM	Initial Operational Capability Milestone	Initial Operational Capability Milestone
Transition		
D.ACT.SUAT	Support User Acceptance Test	Support User Acceptance Test
D.ACT.CPTST	Conduct Performance Test	Conduct Performance Test
D.ACT.PPE	Prepare Production Environment	Prepare Production Environment
D.ACT.CDT	Convert Data - Transition	Convert Data - Transition
D.ACT.TEUT	Train End Users - Transition	Train End Users - Transition
D.ACT.FD	Finalize Documentation	Finalize Documentation
D.ACT.GP	Go Production	Go Production
D.ACT.SIP	System in Production Milestone	System in Production Milestone
Production		
E.ACT.MPSP	Manage Production System Performance	Manage Production System Performance
E.ACT.EPS	Evaluate Production System	Evaluate Production System
E.ACT.RPP	Resolve Production Problems	Resolve Production Problems
E.ACT.PF	Plan for Future	Plan for Future
E.ACT.SO	Sign Off Milestone	Sign Off Milestone

Back to Top

INCEPTION

A.ACT.GBRI Gather Business Requirement- Inception

The business requirements for the WebCenter system or new enhancements are identified, refined and prioritized as outlined in the OUM process. The main work products of this process are the business objectives and goals, the list of functional requirements and the supplemental requirements.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
RD.001	Detail Business and System Objectives	This is a highly recommended task as it outlines the objectives for any project implementing WebCenter. Upon completion of this task, you should have identified all of the organization's business and system objectives which you can review at various stages of the implementation.	R	R	R	R
RD.005	Create System Context Diagram	This task is recommended for all WebCenter projects as it provides the business and the project team with the context of	R	R	R	R

		the full system indicating the various inputs and outputs.				
RD.011.1	Develop Future Process Model	This task is recommended if you have the information available at the start of the Inception phase. Otherwise, it is recommended that this task is delivered within the Elaboration phase. This task can be very time consuming and must be accounted for within the workplan.	O	O	O	O
RD.020	Obtain High-Level Business Descriptions	This task is recommended if the organization is complex or if the project is an enterprise-level implementation.	O	O	O	O
RA.015	Develop Business Use Case Model	This task is only recommended if you do not have a Future Process Model. In most cases, the system Use Case Model is sufficient.	O	O	O	O
RD.065	Develop Domain Model (Business Entities)	This task requires more than one iteration for WebCenter Content projects in order to capture the metadata and security information using class diagramming techniques.	O	O	R	O
RD.012	Document Present and Future Organizational Structures	This task is recommended if the organization is complex or if the project is an enterprise-level implementation.	O	O	O	O
RD.015	Determine KPI Collection and Reporting Strategy	This task is optional unless there is a project requirement.	O	O	O	O

Back to Top

A.ACT.ECBB Establish Current Business Baseline

This activity is required for WebCenter projects if an analysis of the organization's current business processes and functions is required.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
RD.030	Develop Current Business Process Model	This task is recommended if the organization is complex or if the project is an enterprise-level implementation.	O	O	O	O
RD.034	Document Current Business Baseline Metrics	This task is optional unless there is a project requirement.	O	O	O	O

Back to Top

A.ACT.GR Gather Solution Requirements

This activity includes the gathering of other requirements that are not related to the business and system objectives. For WebCenter projects, you should ensure that the recommended tasks are completed.

Task ID (Link to WebCenter	Task Name					

Supplemental Task Guidance)	(Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
RD.042.1	Develop Glossary	This task is highly recommended for all WebCenter projects. It is essential that a project glossary be developed as it avoids misinterpretation of WebCenter and business terms.	R	R	R	R
RD.045.1	Prioritize Requirements (MoSCoW)	The MoSCoW List is one of the most important work products for any WebCenter project. It must identify all of the use cases (functional requirements) for the project and their prioritization. Consider combining with the Supplemental Requirements (RD.055).	R	R	R	R
RD.055	Detail Supplemental Requirements	Detailing the Supplemental Requirements is one of the most important tasks for any WebCenter project. The objective is to identify all of the non-functional requirements for the project and their prioritization. Consider combining with the MoSCoW List (RD.045).	R	R	R	R
RD.130.1	Develop Baseline Architecture Description	This task is optional for WebCenter projects; however, it can prove useful in the early stages of any project. It helps provide understanding of factors that will influence the architecture of the system. It also allows the opportunity to develop strategies to address the identified factors and, if a product specialist is available, this can ease concerns over certain product related factors.	O	O	O	O
RA.023.1	Develop Use Case Model	It is recommended that Use Case Specification (RA.024) documents are produced for all functional requirements that are not present within the packaged software. This task should be completed regardless of the type of WebCenter project.	R	R	R	R
RA.027.1	Identify Candidate Business Rules	This task is recommended if you need to include WebCenter Records retention lifecycle type of rules, i.e., taking the customers records policy and making a concise set of rules.	O	O	O	O

Back to Top

A.ACT.CR Consolidate Solution Requirements

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
RD.140.1	Create Requirements Specification	The Requirements Specification is recommended for every WebCenter project as it captures all of the requirement information for the project.	R	R	R	R
RD.150.1	Review Requirements Specification	The Requirements Specification is recommended for every	R	R	R	R

		WebCenter project as it captures all of the requirement information for the project.				

Back to Top

A.ACT.CCPI Create Conceptual Prototype - Inception

In this activity, you create the Conceptual Prototype. The purpose of this prototype is to show the users your understanding of an agreed on set of requirements. If the WebCenter implementation project requires the use of such a prototype, then the following tasks are recommended.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
IM.005.1	Develop Conceptual Prototype	During the Inception phase, this task is recommended for clarification of the system objectives.	O	O	O	O
RA.030.1	Validate Conceptual Prototype	This task is executed if a Conceptual Prototype has been produced and the validation should be undertaken in the format of a small workshop/meeting.	O	O	O	O

Back to Top

A.ACT.GSP Gather Supporting Requirements

This activity includes the gathering of supporting requirements that are not related to the business and system objectives. For WebCenter projects, you should ensure that the recommended tasks are completed. The optional tasks depend on the requirements for the project (for example, if there is any data migration or is Performance Management required).

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
CV.010	Define Data Acquisition and Conversion Requirements	This task is recommended if you are providing data migration as part of the project. It is not necessary to complete the template for this task – you may wish to provide the migration requirements in the Supplemental Requirements (RD.055).	O	O	O	O
TE.005.1	Determine Testing Requirements	This task is recommended as testing is an important part of any WebCenter project. It is not necessary to complete the template for this task – you may wish to provide the testing requirements in the Supplemental Requirements (RD.055).	R	R	R	R
PT.010	Conduct Performance Management Workshop	This task is recommended if performance is a key	O	O	O	O

		requirement. It is not necessary to complete the template for this task – you may wish to provide the performance requirements within the Supplemental Requirements (RD.055).				
TA.010	Conduct Technical Architecture Workshop	This task is highly recommended for all WebCenter projects. It is essential that a Technical Architecture Requirements and Strategy document (TA.020) be produced as it aids understanding for the project team. You may also wish to provide the technical architecture requirements within the Supplemental Requirements (RD.055).	R	R	R	R
DO.010	Define Documentation Requirements and Strategy	This task is recommended as documentation is an important part of most WebCenter projects. It is not necessary to complete the template for this task – you may wish to provide the documentation requirements within the DO.010 tab of the MoSCoW List.	R	R	R	R
RD.070	Determine Audit and Control Requirements	This task is optional unless there is a project requirement.	O	O	O	O

Back to Top

A.ACT.TPT Train Project Team

This activity can be used to prepare a learning plan for the project team, as well as establishing the learning environment and lastly, put the plan into action by conducting the team learning events. Many WebCenter projects may have an internal team of developers who need training before configuration and customization commences.

Although these tasks are listed as optional, it is recommended that they are taken into consideration during the early stages of the project.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TR.010.1	Define Training Strategy	This task should not just address the project team. It should also be used to define a strategy for the end users (business). This task should also not just address product training, but also awareness/understanding of the organization's business (project team).	R	R	R	R
TR.020	Prepare Project Team Learning Plan	This task is recommended if the project team requires product or business process awareness training.	O	O	O	O
TR.030	Prepare Project Team Learning Environment	This task is recommended if it is a large multi-functional project. An example would include installing a sandbox/VM for training purposes.	O	O	O	O
TR.040	Develop Project Team Learningware	This task is recommended if the project team requires product or business process awareness training.	O	O	O	O
TR.050	Conduct Project Team Learning Events	This task is recommended if the project team requires product or business process awareness training.	O	O	O	O

Back to Top

A.ACT.LCOB Lifecycle Objective Milestone

For WebCenter projects, the recommended activities should be completed in order to achieve this milestone in the project. It is also recommended that the optional activities, if applicable to the project, be completed as part of this milestone.

Activity ID	Activity Name	Sites	Social	Content	Portal
A.ACT.GBRI	Gather Business Requirements - Inception	R	R	R	R
A.ACT.ECBB	Establish Current Business Baseline	O	O	O	O
A.ACT.GR	Gather Solution Requirements	R	R	R	R
A.ACT.CR	Consolidate Solution Requirements	R	R	R	R
A.ACT.CCPI	Create Conceptual Prototype - Inception	O	O	O	O
A.ACT.GSP	Gather Supporting Requirements	R	R	R	R
A.ACT.TPT	Train Project Team	R	R	R	R

Back to Top

ELABORATION

B.ACT.DPS Define Project Strategy

The WebCenter objective for this activity is to develop project strategies for the application extension, Testing, Data Acquisition and Conversion, Documentation, and Transition of the solution. Some tasks have been marked as optional; however, it is recommended that each task is reviewed to confirm if it is applicable.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TE.005.2	Determine Testing Requirements	This task is recommended to ensure that the Testing Requirements are reviewed during the Elaboration phase as there may be changes required based on the Analysis and Design.	R	R	R	R
TE.010	Develop Testing Strategy	This task is recommended in order to identify how testing should be performed at various stages of the project. It is also important that the strategy should also define the acceptance	R	R	R	R

		criteria of the solution.				
CV.020	Define Data Acquisition, Conversion and Data Quality Strategy	This task is recommended if you are providing data migration as part of the project.	O	O	O	O
DO.020	Define Documentation Standards and Procedures	This task is recommended to be undertaken as early as possible within any project as to ensure that you have the correct documentation format and structure, i.e., some customers may require their logo or a different page structure. The earlier this task is undertaken, the less chance of having to reformat, or even rewrite the material. Documentation Standards and Procedures (DO.020) for WebCenter projects largely depend on the project requirements. However, it is recommended to use the OUM template.	R	R	R	R
TR.010.2	Define Training Strategy	This task is recommended to ensure that the strategy is reviewed during the Elaboration phase as there may be changes required based on the Analysis and Design.	O	O	O	O
TS.020.1	Define Cutover Strategy	This task is recommended when you have a complex transition with a significant impact on business.	O	O	O	O

Back to Top

B.ACT.DI Define Infrastructure

The Define Infrastructure activity consists of producing the requirements for the Technical Architecture infrastructure for the WebCenter system. All tasks in this activity are recommended when implementing a WebCenter system.

It is highly recommended that the Develop Security and Control Strategy task is completed for this activity. This task focuses on the security and control requirements for the WebCenter system.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TA.020	Define Technical Architecture Requirements and Strategy	This task is highly recommended for all WebCenter projects.	R	R	R	R
TA.030	Define Integration Requirements and Strategy	It is strongly recommended that this task is documented in one combined TA.020 work product.	R	R	R	R
TA.040	Define Reporting and Information Access Strategy	It is strongly recommended that this task is documented in one combined TA.020 work product.	R	R	R	R
TA.050	Define Disaster Recovery Strategy	It is strongly recommended that this task is documented in one combined TA.020 work product.	R	R	R	R
TA.060	Define System Operations and Management	It is strongly recommended that this task is documented in one	R	R	R	R

	Strategy	combined TA.020 work product.				
TA.070	Define Initial Architecture and Application Mapping	It is strongly recommended that this task is documented in one combined TA.020 work product.	R	R	R	R
TA.080	Define Backup and Recovery Strategy	It is strongly recommended that this task is documented in one combined TA.020 work product.	R	R	R	R
TA.090	Develop Security and Control Strategy	It is strongly recommended that this task is documented in one combined TA.020 work product.	R	R	R	R

Back to Top

B.ACT.PEE Prepare Environments - Elaboration

In this activity, you create the Development Environment that you will need during the development stage of the WebCenter implementation project. You should also prepare appropriate test data within this activity.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
IM.090.1	Create Installation Routines	This task is recommended to be undertaken in the Elaboration phase for all WebCenter projects and is typically delivered together with the system design. The initial iteration of this work product could be delivered with the physical prototype if required	R	R	R	R
IM.007.1	Prepare Development Environment	This task is recommended for all WebCenter projects and typically requires one central Development Environment plus any customer-based Development Environments depending on the project.	R	R	R	R
TE.018.1	Prepare Static Test Data	This task is recommended for all WebCenter projects because of the complexity in developing and unit testing without any data. This task should immediately follow the preparation of the Development Environment (IM.007.1). Note that this does not include full test data – such data should be identified in the various test plans.	R	R	R	R
TE.038.1	Prepare Integration Test Environment	This optional task requires you to install the Integration Test Environment based on the recorded configuration details in MC.050 and TA.020, and the installation routines in IM.090.	O	O	O	O
TE.060.1	Prepare System Test Environment	This optional task requires you to install the System Test Environment based on the recorded configuration details in MC.050 and TA.020, and the installation routines in IM.090.	O	O	O	O
CV.030.1	Prepare Conversion Environment (Initial Load)	This optional task requires you to install the Conversion Environment based on the recorded configuration details in MV.030 and TA.020, and the installation routines in IM.090.	O	O	O	O

Back to Top

B.ACT.GBRE Gather Business Requirements - Elaboration

The Future Process Model (RD.011.2) includes process flow diagrams of the events and business processes that the applications and the associated functions of the business area will support with regards to WebCenter. In some cases, business processes will be affected by the introduction of the WebCenter system.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
RD.011.2	Develop Future Process Model	This task is recommended for WebCenter Content and Portal engagements. This task can be very time consuming and must be accounted for within the workplan.	O	O	R	R
RA.055.1	Document Business Procedures	This task is recommended when you are not documenting requirements within use cases. Note that this is a narrative of the process (RD.011) as opposed to formal procedures.	O	O	O	O
MC.030	Map Business Requirements	This task is highly recommended in order to identify if the WebCenter system can satisfy the project requirements. If the system cannot satisfy a requirement then this is a gap and must be recorded. It is important that the alternative solutions to resolve the gap are proposed during this task. It is strongly recommended that this task is documented in the Analysis Specification (AN.100) work product together with MC.100 and MC.110.	R	R	R	R
RD.065.3	Develop Domain Model (Business Entities	This is an additional iteration of this task for WebCenter projects.	R	R	R	R

Back to Top

B.ACT.DTP Develop Test Plans

The WebCenter objective for this activity is to develop the test plans. Testing is highly recommended and is most significant for WCM implementation projects.

Note: Test plans can be combined into a single work product.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal

TE.015.1	Develop Integration Test Plan	This task is recommended for all WebCenter projects in order to plan for the testing of component integration in the system. For WebCenter products, this task is performed only for custom-built components.	O	O	O	O
TE.050.1	Develop System Test Plan	This task is recommended to plan the testing of the operation and integration of all business system flows within the WebCenter system, including the integration of application extensions.	O	O	O	O
TE.080	Develop Systems Integration Test Plan	This task is recommended for most WebCenter projects in order to plan the testing for the system's integration with other application systems, i.e., external security, external providers.	O	O	O	O

Back to Top

B.ACT.SSC Specify Software Configuration

This activity allows for the definition and documentation of all setup information, including business data structures, rules, profiles, contribution folders, etc., not previously addressed in the Specify Key Structure Definition activity. Configuration file parameter values should also be specified within this activity.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
MC.040	Gather Setup Information		R	R	R	R
MC.050.1	Define Application Setups	This task is highly recommended for all WebCenter projects. Within this iteration, you should ensure that you capture the system configuration in order to support the Design Specification (DS.140) and Software Component Design(s) (DS.080). You can also refine this work product during the Prototype and Validate Configuration activity. For WebCenter Content projects, this task involves the development of a Security Model and Metadata Model based on the Domain Model (RD.065). For WebCenter Records, you may require additional child documents such as a Retention Schedule, Archive Locations, etc.	R	R	R	R
MC.060	Document Functional Security		R	R	R	R

Back to Top

B.ACT.PVC Prototype and Validate Configuration

This activity is used to validate the standard application functionality.. It also includes validation of the standard reports and forms provided with the WebCenter system

functionality being implemented. It involves conducting a prototyping workshop(s) to validate the standard application functionality (i.e., configured application environment) for the purpose of validating that the packaged application functionality as configured based on the results of the Specify Software Configuration activity, meets the requirements.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TE.025.1	Create System Test Scenarios	In a WebCenter implementation project, the System Test Scenarios created during this activity are used to validate a prototype of the standard WebCenter system functionality.	R	R	R	R
MC.070	Prepare Configuration Prototype Environment		R	R	R	R
MC.080	Conduct Configuration Prototyping Workshop		R	R	R	R
MC.090.2	Conduct Reporting Fit Analysis	This task is recommended if the organization is complex, if the project is an enterprise-level implementation, or if it is a specific project requirement.	O	O	O	O

Back to Top

B.ACT.PGA Perform Gap Analysis

Within this activity the project team reviews any proposed business process changes and other modifications (setups, interfaces, custom components, etc.) identified during the Validate Prototypes activity. Alternative ways to address open requirements are determined and estimates for each alternative prepared. As a final step the alternative solutions are reviewed with the organization and the best alternative is determined based on the their preference.

This activity should be completed if prototypes have been developed and validated.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
MC.100	Define and Estimate Application Extensions	This task is highly recommended in order to estimate the amount of effort to deliver the different gap solutions identified in MC.030. This will allow the reviewers and approvers to make an educated decision when it comes to choosing the right solution (MC.110). It is strongly recommended that this task is documented in the Analysis Specification (AN.100) work product together with MC.030 and MC.110.	R	R	R	R
MC.110	Define Gap Resolutions	This task is highly recommended as this where the alternative solutions for satisfying gaps are reviewed with the customer	R	R	R	R

		and the best alternative is identified and documented, based on the customer's preference. It is strongly recommended that this task is documented in the Analysis Specification (AN.100) work product together with MC.030 and MC.100.				

Back to Top

B.ACT.DUC Develop Use Case Model

In this activity, the Use Case Model (RA.023) should be created for all WebCenter projects that require customization, or enhancement to the system. If the organization has provided a functional specification then that may be sufficient. It is recommended that the Use Case Model is created at the same time as the MoSCoW List as they are very closely linked. The Use Case Model should show a structured representation of all of the project use cases with the gaps identified as appropriate.

During Elaboration, all use cases should be reviewed and the appropriate updates made to the Use Case Model (see also RA.180 Review Use Case Model).

A Use Case Specification must be developed for all use cases defined as a 'Gap' for all WebCenter projects.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
RA.023.2	Develop Use Case Model	A Use Case Model (RA.023) should be created for all WebCenter projects that require customization, or enhancement to the system.	R	R	R	R

Back to Top

B.ACT.CCPE Create Conceptual Prototype - Elaboration

In this activity, you review and modify the Conceptual Prototype. The purpose of this prototype is to show the users your understanding of an agreed on set of requirements. If the WebCenter implementation project requires the use of such a prototype, then the following tasks are recommended.

If you are working on a WCM project, then these tasks are essential in order to show:

- storyboards - to understand the flow from one screen to the next
- wireframes - identification of data to be input, viewed or changed by a user

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal

IM.005.2	Develop Conceptual Prototype	During the Elaboration phase, this task is recommended for clarification of the use case gaps.	R	R	R	R
RA.030.2	Validate Conceptual Prototype	This task is undertaken if a Conceptual Prototype has been produced and the validation should be undertaken in the format of a small workshop/meeting.	R	R	R	R

Back to Top

B.ACT.CS Consolidate Specification

The objective for this activity is to refine the software requirements and review the Use Case Model and Use Case Specifications (RA.023 and RA.024) and prepare for detailed design of the WebCenter solution.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
RD.042.2	Develop Glossary	This task is highly recommended for all WebCenter projects. It is essential that a project glossary be continuously refined throughout the project as it avoids misinterpretation of WebCenter and business terms.	R	R	R	R
RD.045.2	Prioritize Requirements (MosCoW)	The MoSCoW List is one of the most important work products for any WebCenter project. It is essential that the MoSCoW List be continuously reviewed and refined throughout the project. It may also be necessary to review/refine the Supplemental Requirements (RD.055).	R	R	R	R
RD.140.2	Create Requirements Specification	The Requirements Specification is recommended for every WebCenter project as it captures all of the requirement information for the project. You should ensure that the document is refined during the Elaboration phase as there may be changes required based on the Analysis and Design.	R	R	R	R
RD.150.2	Review Requirements Specification	The Requirements Specification is recommended for every WebCenter project as it captures all of the requirement information for the project. You should ensure that the document is reviewed during the Elaboration phase as there may have been changes applied based on the Analysis and Design.	R	R	R	R
RA.027.2	Identify Candidate Business Rules	This task is recommended if you need to include WebCenter Records retention lifecycle type of rules, i.e., taking the customers records policy and making a concise set of rules.	O	O	O	O
RA.180.1	Review Use Case Model	This task is recommended to ensure that the model is reviewed during the Elaboration phase as there may be changes required based on the Analysis and Design.	R	R	R	R

Back to Top

B.ACT.BSA Baseline Software Architecture

This activity is used to produce the Architecture Description (RD.130, RA.035) for the WebCenter solution. These tasks are recommended for all types of WebCenter projects.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
RA.035	Develop High-Level Software Architecture Description	This task is recommended in order to prioritize and group the use cases / processes. Ensure that critical requirements are grouped together, i.e., Foundation Package, Package #1, Package #2. This grouping allows the project team to focus on the critical packages first.	R	R	R	R
AN.040.1	Develop Analysis Architecture Description	This task is recommended if the organization is complex or if the project is an enterprise-level implementation.	O	O	O	O
DS.040.1	Develop Design Architecture Description	This task is recommended if the organization is complex or if the project is an enterprise-level implementation.	O	O	O	O

Back to Top

B.ACT.DUC Develop Use Case Details

Now that use cases have been prioritized, you can begin to develop the Use Case Specifications.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
RA.024.1	Develop Use Case Details	It is recommended that Use Case Specification documents are produced for all functional requirements that are not present within the packaged software. This task should be completed regardless of the type of WebCenter project.	R	O	R	R

Back to Top

B.ACT.AE Analyze - Elaboration

This activity allows for analyzing the captured requirements by refining and structuring them via various conceptual object models, ultimately organized into the Analysis Specification.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
AN.050.1	Analyze Data	It is strongly recommended that this task is documented in the Analysis Specification (AN.100).	R	R	R	R
AN.060.1	Analyze Behavior	It is strongly recommended that this task is documented in the Analysis Specification (AN.100).	R	R	R	R
AN.070.1	Analyze Business Rules	It is strongly recommended that this task is documented in the Analysis Specification (AN.100).	R	R	R	R
AN.090.1	Analyze User Interface	It is strongly recommended that this task is documented in the Analysis Specification (AN.100).	R	R	R	R
AN.100.1	Prepare Analysis Specification	This task is highly recommended and can be in the form of 1 or more documents each representing the analysis of a system component. There are three approaches to this task for WebCenter projects: 1. Master AN.100 – Use this approach if there is only one system component, i.e., 1 process. 2. Various AN.100s by some grouping (for example, process) – Use this approach if you have multiple system components, i.e., 2+ process. 3. Include the analysis within the Use Case Specification document(s) (RA.024) – Use this approach if you have a small number of use cases and no high level grouping.	R	R	R	R
AN.110.1	Review Analysis Model	Reviewing the Analysis Model is highly recommended prior to commencing with Design. However, it is possible to approve components of the Analysis (AN.100) in iterations therefore allowing design to start for certain components while the Analysis continues – be careful with dependencies.	R	R	R	R

Back to Top

B.ACT.DE Design - Elaboration

This activity allows for shaping the system to meet all functional and supplemental requirements.

The optional tasks are generally performed when there is a need to gain further clarification of the business requirements represented in the use cases. This typically applies to those requirements that can only be satisfied by custom-built components, which extend the functionality of the Webcenter system and/or integrate the WebCenter system with another system or legacy systems.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
DS.050	Determine Design and Build Standards	It is recommended that this task is documented in the Design Specification (DS.140).	O	O	O	O
DS.060	Define Business Rules Implementation Strategy	It is recommended that this task is documented in the Design Specification (DS.140).	O	O	O	O
DS.080.1	Design Software Components	This task is highly recommended and can be in the form of 1 or more documents each representing the design of a system component. It is recommended to add a reference in the Design Specification (DS.140) to each DS.080 document produced.	R	R	R	R
DS.090.1	Design Data	It is strongly recommended that this task is documented in Software Component Design document(s) (DS.080) or in the Design Specification (DS.140).	O	O	O	O
DS.100.1		It is strongly recommended that this task is documented in Software Component Design document(s) (DS.080) or in the Design Specification (DS.140).	O	O	O	O
DS.110.1		It is strongly recommended that this task is documented in Software Component Design document(s) (DS.080) or in the Design Specification (DS.140).	O	O	O	O
DS.130.1		It is strongly recommended that this task is documented in Software Component Design document(s) (DS.080) or in the Design Specification (DS.140).	R	R	R	R
DS.140.1	Prepare Design Specification	This task is highly recommended as it is the parent Design document. It is recommended that this document references the Software Component Design documents (DS.080), plus the Application Setups (DS.030).	R	R	R	R
DS.160.1	Review Design Model	Reviewing the Design Model is highly recommended prior to commencing with the Construction phase. However, it is possible to approve components of the Design (DS.080) in iterations; therefore, allowing Construction to start on certain components while the Design continues – be careful with dependencies.	R	R	R	R

Back to Top

B.ACT.DCCTSE Develop Custom Component Test Scripts - Elaboration

This activity is performed for custom-built components that extend the functionality of the WebCenter system.

These tasks should be completed if custom components have been developed.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TE.020.1	Develop Unit Test Scripts	This task is recommended if it is a specific project requirement. The scripts can be used at a later stage for Integration and User Acceptance Testing.	O	O	O	O
TE.035.1	Create Integration Test Scenarios	This task is recommended if it is a specific project requirement.	O	O	O	O

Back to Top

B.ACT.DSTSE Develop System Test Scenarios - Elaboration

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TE.025.2	Create System Test Scenarios	This task is recommended if it is a specific project requirement.	O	O	O	O
TE.070.1	Perform System Test	This task is recommended if it is a specific project requirement.	O	O	O	O

Back to Top

B.ACT.DVCSP Develop and Validate Custom Software Prototypes

This activity allows for development and validation of the various prototypes of custom components for the WebCenter system and performing a component review.

This activity also serves to address the creation of a User Interface Standards Prototype (IM.085) for validation of any revisions made to the out-of-the-box application system user interface in order to meet the implementing organization's requirements. This is generally applicable to those WebCenter systems that require tailoring/revision of the standard user interface.

This activity is used to validate the Functional Prototype (IM.010) of the custom components.

Validation of functional prototypes for custom extensions is generally limited to custom components that warrant development of a prototype at this stage of the project due to the technical complexity, or other risks associated with them.

Task ID (Link to WebCenter	Task Name					

Supplemental Task Guidance)	(Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
IM.010	Develop Functional Prototype	This task is recommended if the organization is complex, if the project is an enterprise-level implementation, or if it is a specific project requirement.	O	O	O	O
RA.085	Validate Functional Prototype	This task is recommended if the organization is complex, if the project is an enterprise-level implementation, or if it is a specific project requirement.	O	O	O	O
IM.020	Develop Architectural Foundation	This task is recommended if the organization is complex, if the project is an enterprise-level implementation, or if it is a specific project requirement.	O	O	O	O
IM.085	Develop User Interface Standards Prototype	This task is recommended if the organization is complex, if the project is an enterprise-level implementation, or if it is a specific project requirement.	O	O	O	O
RA.095	Validate User Interface Standards Prototype	This task is recommended if the organization is complex, if the project is an enterprise-level implementation, or if it is a specific project requirement.	O	O	O	O
IM.060.1	Perform Component Review	This task is recommended if the organization is complex, if the project is an enterprise-level implementation, or if it is a specific project requirement.	O	O	O	O

Back to Top

B.ACT.PCCTE Perform Custom Component Testing - Elaboration

This activity is performed for custom-built components that extend the functionality of the WebCenter system.

In a WebCenter implementation project, unit testing is generally performed in the Construction phase. However, it may be performed in the Elaboration phase for complex, higher risk custom extensions that have been identified during the pre-sales cycle and/or during the Inception phase, and where the prototypes of those complex custom extensions that have been developed during the Elaboration phase, will continue to be enhanced during the Construction phase.

In a WebCenter implementation project, integration testing is generally performed in the Construction phase. However, it may be performed in the Elaboration phase for complex, higher risk custom extensions that have been identified during the pre-sales cycle and/or during the Inception phase, and where the prototypes of those complex custom extensions that have been developed during the Elaboration phase, will continue to be enhanced during the Construction phase.

These tasks should be completed if custom components have been developed.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TE.030.1	Perform Unit Test	In a WebCenter implementation, it is recommended that this task is performed only for custom-built components that	O	O	O	O

		extend the functionality of the system.				
TE.040.1	Perform Integration Test	This task is recommended if it is a specific project requirement.	O	O	O	O

Back to Top

B.ACT.PSTE Perform System Test - Elaboration

In a WebCenter system implementation, you perform the System Test to test the operation and integration of all business system flows within the system, including the integration of application extensions (Content Server components).

In a WebCenter implementation project, the System Test Scenarios created during this activity are used to validate a prototype of the standard WebCenter system functionality during Validate Functional Prototype (RA.085). System testing involving the integration of application extensions (Content Server components) is generally performed in the Construction phase in a WebCenter implementation project. However, it may be performed in the Elaboration phase for complex, higher risk custom extensions that have been identified during the pre-sales cycle and/or during the Inception phase, and where the prototypes of those complex custom extensions that have been developed during the Elaboration phase, will continue to be enhanced during the Construction phase.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TE.070.1	Perform System Test	This task is recommended if it is a specific project requirement.	O	O	O	O

Back to Top

B.ACT.PPM Plan Performance Management

This activity consists of producing the requirements, strategy, testing models, scenarios, test scripts, and program designs for Performance Management and Testing.

For a WebCenter implementation project, this could be identified as planning an OAT (Operational Acceptance Testing) environment. This type of environment is important to organizations in order to address issues such as website performance

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
PT.020	Define Performance Management Requirements and Strategy	This task is recommended if performance is a specific project requirement / objective.	O	O	O	O
PT.030	Identify Performance Testing Strategy	This task is recommended if performance is a specific project requirement / objective.	O	O	O	O

PT.040	Identify Performance Testing Models and Scenarios	This task is recommended if performance is a specific project requirement / objective.	O	O	O	O
PT.050	Design Performance Test Scripts and Programs	This task is recommended if performance is a specific project requirement / objective.	O	O	O	O
PT.060	Design Performance Test data and Load Programs	This task is recommended if performance is a specific project requirement / objective.	O	O	O	O

Back to Top

B.ACT.PACDE Prepare to Acquire and Convert Data - Elaboration

In a WebCenter implementation project, this activity consists of producing the standards and completing the high-level (business object level) data mapping needed to confirm that the application software supports the organization's business processes and legacy data requirements. Conversion component design and development tasks are executed in a similarly named activity in the Construction phase.

For WebCenter implementation projects, it is recommended that an adequate Security Model and Metadata Model have been developed before starting the task, Perfrom Data Mapping (CV.027.1).

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
CV.025	Define Data Acquisition and Conversion Standards	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
RA.160	Conduct Business Data Source Gap Analysis	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
CV.027.1	Perform Data Mapping	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
RA.170.1	Conduct Data Quality Assessment	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
CV.035.1	Define Manual Conversion Procedures (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
CV.040.1	Design Conversion Components (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
CV.050.1	Prepare Conversion Test Plans (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
CV.055.1	Implement Conversion Components (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
CV.060.1	Perform Conversion Component Unit Test (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
CV.062.1	Perform Conversion Component Business Object Test (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O

CV.063.1	Perform Conversion Component Validation Test (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O

Back to Top

B.ACT.LCAR Lifecycle Architecture Milestone

For WebCenter projects, the recommended activities should be completed in order to achieve this milestone in the project. It is also recommended that the optional activities, if applicable to the project, be completed as part of this milestone.

Activity ID	Activity Name	Site	Social	Content	Portal
B.ACT.DPS	Define Project Strategy	R	R	R	R
B.ACT.DI	Define Infrastructure	R	R	R	R
B.ACT.PEE	Prepare Environments - Elaboration	R	R	R	R
B.ACT.GBRE	Gather Business Requirements - Elaboration	R	R	R	R
B.ACT.DTP	Develop Test Plans	O	O	O	O
B.ACT.SSC	Specify Software Configuration	R	R	R	R
B.ACT.PVC	Prototype and Validate Configuration	R	R	R	R
B.ACT.PGA	Perform Gap Analysis	R	R	R	R
B.ACT.DUCM	Develop Use Case Model	R	R	R	R
B.ACT.CCPE	Create Conceptual Prototype - Elaboration	R	R	R	R
B.ACT.CS	Consolidate Specification	R	R	R	R
B.ACT.BSA	Baseline Software Architecture	R	R	R	R
B.ACT.DUCD	Develop Use Case Details	R	O	R	R
B.ACT.AE	Analyze - Elaboration	R	R	R	R
B.ACT.DE	Design - Elaboration	R	R	R	R
B.ACT.DCCTSE	Develop Custom Component Test Scripts - Elaboration	O	O	O	O
B.ACT.DSTSE	Develop System Test Scenarios - Elaboration	O	O	O	O
B.ACT.DVCSP	Develop and Validate Custom Software Prototypes	O	O	O	O
B.ACT.PCCTE	Perform Custom Component Testing - Elaboration	O	O	O	O
B.ACT.PSTE	Perform System Test - Elaboration	O	O	O	O
B.ACT.PPM	Plan Performance Management	O	O	O	O
B.ACT.PACDE	Prepare to Acquire and Convert Data - Elaboration	O	O	O	O

Back to Top

CONSTRUCTION

C.ACT.FR Finalize Requirements

This activity is generally performed when multiple iterations are planned for the Construction phase. In such cases, this activity is included in the second, and subsequent, iterations

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
RD.042.3	Develop Glossary	This task is highly recommended for all WebCenter projects. It is essential that a project glossary be continuously refined throughout the project as it avoids misinterpretation of WebCenter and business terms.	O	O	O	O
RD.045.3	Prioritize Requirements (MoSCoW)	The MoSCoW List is one of the most important work products for any WebCenter project. It is essential that the MoSCoW List be continuously reviewed and refined throughout the project. It may also be necessary to review/refine the Supplemental Requirements (RD.055).	O	O	O	O
RD.130.2	Develop Baseline Architecture Description	This task is optional for WebCenter projects; however, it can prove useful in the early stages of any project. It helps provide understanding of factors that influence the architecture of the system. It also allows the opportunity to develop strategies to address the identified factors and, if a product specialist is available, this can ease concerns over certain product related factors.	O	O	O	O
RA.023.3	Develop Use Case Model	A Use Case Model (RA.023) should be created for all WebCenter projects that require customization, or enhancement to the system.	O	O	O	O
RA.024.2	Develop Use Case Details	It is recommended that Use Case Specification documents be produced for all functional requirements that are not present within the packaged software. This task should be completed regardless of the type of WebCenter project.	O	O	O	O
RA.180.2	Review Use Case Model	This task is recommended to ensure that the model is reviewed during the Construction phase as there may be changes required based on the Analysis and Design.	O	O	O	O

Back to Top

C.ACT.AC Analyze - Construction

This activity is generally performed when there is a need to gain further clarification of the business requirements represented in the use cases or there are multiple iterations groups of use cases being developed for custom components. This typically applies to those requirements that can only be satisfied by custom-built components, which extend the functionality of the WebCenter system and/or integrate the WebCenter system with other WebCenter or legacy systems.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
AN.040.2	Develop Analysis Architecture Description	This task is recommended if the organization is complex or if the project is an enterprise-level implementation.	O	O	O	O
AN.070.2	Analyze Business Rules	If business rules are available, it is recommended that they are reviewed. Reviewing the Business Rules is recommended prior to commencing with the Construction phase as may be changes required based on the Analysis and Design.	O	O	O	O
AN.110.2	Review Analysis Model	Reviewing the Analysis Model is recommended prior to commencing with the Construction phase as there may be changes required based on the Analysis and Design.	R	R	R	R

Back to Top

C.ACT.DC Design - Construction

This activity is generally performed when there is a need to gain further clarification of the business requirements represented in the use cases or there are multiple iterations groups of use cases being developed for custom components. This typically applies to those requirements that can only be satisfied by custom-built components, which extend the functionality of the WebCenter system and/or integrate the WebCenter system with other WebCenter or legacy systems.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
DS.040.2	Develop Design Architecture Description	This task is recommended if the organization is complex or if the project is an enterprise-level implementation.	O	O	O	O
DS.080.2	Design Software Components	Reviewing the Design Model is recommended prior to commencing with the Construction phase as further changes may be required.	O	O	O	O
DS.090.2	Design Data	Reviewing the Design Model is recommended prior to commencing with the Construction phase as further changes may be required.	O	O	O	O
DS.100.2	Design Behavior	Reviewing the Design Model is recommended prior to commencing with the Construction phase as further changes may be required.	O	O	O	O
DS.110.2	Design Business Rules	Reviewing the Design Model is recommended prior to commencing with the Construction phase as further changes may be required.	O	O	O	O

DS.130.2	Design User Interface	Reviewing the Design Model is recommended prior to commencing with the Construction phase as further changes may be required.	O	O	O	O
DS.140.2	Prepare Design Specification	Reviewing the Design Model is recommended prior to commencing with the Construction phase as further changes may be required.	O	O	O	O
DS.150.2	Develop Database Design	Reviewing the Design Model is recommended prior to commencing with the Construction phase as further changes may be required.	O	O	O	O
DS.160.2	Review Design Model	Reviewing the Design Model is recommended prior to commencing with the Construction phase as further changes may be required.	O	O	O	O

Back to Top

C.ACT.PTP Perform Test Planning

The Perform Test Planning activity allows for updating and refining (iterating) the Integration and System Test Plans.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TE.015.2	Develop Integration Test Plan	This optional task allows for updating and refining the Integration Test Plan.	O	O	O	O
TE.050.2	Develop System Test Plan	This optional task allows for updating and refining the System Test Plan.	O	O	O	O

Back to Top

C.ACT.PEC Prepare Environments - Construction

This activity addresses the installation of software environments for various purposes; testing, development, training and production environments (purposes). In this activity the “out of the box” software is installed.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
IM.007.2	Prepare Development Environment	In a WebCenter implementation, this task is recommended	R	R	R	R

		only when there are requirements that can only be satisfied through custom-built components that extend the functionality of the system.				
TE.018.2	Prepare Static Test Data	In a WebCenter implementation, this task is recommended only when there are requirements that can only be satisfied through custom-built components that extend the functionality of the system.	R	R	R	R
TE.038.2	Prepare Integration Test Environment	In a WebCenter implementation, these tasks are recommended only when there are requirements that can only be satisfied through custom-built components that extend the functionality of the system. An Integration Test verifies that application extension components are properly linked and no coding errors are generated when related components are linked together.	O	O	O	O

Back to Top

C.ACT.DCCTSC Develop Custom Component Test Scripts - Construction

This activity is performed for custom-built components that extend the functionality of the WebCenter system.

In a WebCenter implementation project, unit testing is generally performed in the Construction phase. However, it may be performed in the Elaboration phase for complex, higher risk custom extensions that have been identified during the pre-sales cycle and/or during the Inception phase, and where the prototypes of those complex custom extensions that have been developed during the Elaboration phase, will continue to be enhanced during the Construction phase.

In a WebCenter implementation project, integration testing is generally performed in the Construction phase. However, it may be performed in the Elaboration phase for complex, higher risk custom extensions that have been identified during the pre-sales cycle and/or during the Inception phase, and where the prototypes of those complex custom extensions that have been developed during the Elaboration phase, will continue to be enhanced during the Construction phase.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TE.020.2	Develop Unit Test Scripts		R	R	R	R
TE.035.2	Create Integration Test Scenarios	This task is recommended if it is a specific project requirement.	R	R	R	R

Back to Top

C.ACT.DSTSC Develop System Test Scenarios - Elaboration

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TE.025.3	Create System Test Scenarios		R	R	R	R

Back to Top

C.ACT.DSITS Develop Systems Integration Test Scenarios

This activity is performed if the WebCenter system interacts with other WebCenter or legacy systems.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TE.090	Develop Systems Integration Test Scenarios	This optional task allows for developing the Systems Integration Test Scenarios.	O	O	O	O

Back to Top

C.ACT.ICC Implement Custom Components

This activity allows for implementing (i.e., building) the custom components and custom services needed to extend the capabilities of the application system. It also provides for updating/finalizing the application setup parameters in preparation for Perform System Test (TE.070).

The Perform Component Review task is often completed for WebCenter projects. In this activity, you make all of the product parts (out-of-box and custom) communicate with each other. The technical staff conducts an end-to-end test.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
IM.050	Implement Components	In a WebCenter implementation, this task is highly recommended for those requirements that can only be satisfied through custom-built components that extend the functionality of the system.	R	R	R	R
IM.060.2	Perform Component Review	In a WebCenter implementation, this task is recommended only for custom-built components that extend the functionality of the system.	O	O	O	O

IM.070	Assemble Components	In a WebCenter implementation, this task is recommended only for custom-built components that extend the functionality of the system.	R	R	R	R
IM.090.2	Create Installation Routines	This task iteration is recommended to be undertaken in the Construction phase for all WebCenter projects in order to refine the installation routines based on the implemented components.	R	R	R	R

Back to Top

C.ACT.PCCTC Perform Custom Component Testing - Construction

This activity is performed for custom-built components that extend the functionality of the WebCenter system.

In a WebCenter implementation project, unit testing is generally performed in the Construction phase. However, it may be performed in the Elaboration phase for complex, higher risk custom extensions that have been identified during the pre-sales cycle and/or during the Inception phase, and where the prototypes of those complex custom extensions that have been developed during the Elaboration phase, will continue to be enhanced during the Construction phase.

In a WebCenter implementation project, integration testing is generally performed in the Construction phase. However, it may be performed in the Elaboration phase for complex, higher risk custom extensions that have been identified during the pre-sales cycle and/or during the Inception phase, and where the prototypes of those complex custom extensions that have been developed during the Elaboration phase, will continue to be enhanced during the Construction phase.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TE.030.2	Perform Unit Test	This recommended task can be undertaken by the developer as part of the implementation (IM.050).	R	R	R	R
TE.040.2	Perform Integration Test		R	R	R	R

Back to Top

C.ACT.PST Prepare for System Test

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
MC.030.2	Define Application Setups	For WebCenter Content projects, this task involves the refinement of the Security Model and Metadata Model. For WebCenter Records, you may be required to refine additional	R	R	R	R

		child documents such as a Retention Schedule, Archive Locations, etc.				
TE.060.2	Prepare System Test Environment	In a WebCenter implementation, this task addresses the installation of software environments for various testing, development and documentation purposes.	O	O	O	O

Back to Top

C.ACT.PSTC Perform System Test – Construction

This activity consists of performing the system test and finalizing the Business Procedure Documentation.

The tasks in this activity are recommended if a System Test Environment exists for the WebCenter implementation.

For the optional tasks in this activity, it is recommended that they are completed when there are custom-built components that extend the functionality of the WebCenter system.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TE.070.2	Perform System Test		R	R	R	R
RA.055.2	Document Business Procedures	This task is recommended if it is a specific project requirement.	O	O	O	O
TE.019.1	Collect, Assess, and Refine KPI Measurements	This task is recommended if it is a specific project requirement.	O	O	O	O

Back to Top

C.ACT.PSIT Perform Systems Integration Test

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TE.085	Prepare Systems Integration Test Environment	In a WebCenter implementation, this task addresses the installation of software environments for various testing, development and documentation purposes.	O	O	O	O
TE.100	Perform Systems Integration Test	In a WebCenter implementation, this task validates the integration between the target application system and other systems and verifies that the new system meets defined	R	R	R	R

		interface requirements and supports execution of business processes that cross system boundaries. Examples include external security systems, staff directory systems, etc.				

Back to Top

C.ACT.PPT Prepare for Performance Testing

The Prepare for Performance Testing activity consists of building the test scripts and programs, constructing the environment and database and conducting a dress rehearsal.

Although the tasks in this activity are optional, it is recommended that they are completed on projects when there are custom-built components that extend the functionality of the WebCenter system and/or integrate the WebCenter system with other WebCenter or legacy systems.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
PT.080	Construct Performance Test Environment and Database	This task is recommended if performance is a specific project requirement / objective.	O	O	O	O
PT.090	Conduct Performance Test Dress Rehearsal	This task is recommended if performance is a specific project requirement / objective.	O	O	O	O

Back to Top

C.ACT.PT Prepare for Transition

This activity consists of defining the System Management Procedures, Operational Test Plan, and the Final Platform and Network Architecture and the Capacity Plan.

It is recommended that the Define Final Platform and Network Architecture task is completed for this activity for WebCenter implementation projects.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TA.100	Define System Management Procedures	This task is recommended if it is a specific project requirement.	O	O	O	O
TA.110	Define Operational Testing Plan	This task is recommended if it is a specific project requirement.	O	O	O	O
TA.150	Define Final Platform and Network Architecture	This task is highly recommended for WebCenter projects. It requires the update of the work done in the Initial Architecture	R	R	R	R

		and Application Mapping (TA.070), incorporating any changes, additions or enhancements that have occurred due to subsequent Architecture Design work. This task focuses on the future Production Environment and any supporting environments such as training or production support. It does not address interim project environments that will not be retained after production cutover.				
TA.160	Define System Capacity Plan	This task is recommended if it is a specific project requirement.	O	O	O	O

Back to Top

C.ACT.PCO Prepare for Cutover

This activity consists of defining the Cutover Strategy, developing the Installation Plan, and designing the Production Support Infrastructure.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TS.020.2	Define Cutover Strategy	This task is recommended for WebCenter projects if you need to transition from a legacy system to the new system.	R	R	R	R
TS.030	Develop Installation Plan	In a WebCenter implementation, you should develop a detailed Transition Plan for moving onto the production system, as well as an Implementation Contingency Plan.	R	R	R	R
TS.040	Design Production Support Infrastructure	This task is highly recommended for WebCenter projects. In this task, you identify the operational infrastructure for managing and maintaining the application environment, servers, and network infrastructure in production.	R	R	R	R

Back to Top

C.ACT.TI Test Infrastructure

This activity consists of conducting operational, backup and recovery and disaster recovery testing.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal

TA.120	Conduct Operational Testing	This task is recommended if your WebCenter project includes complex architecture changes.	O	O	O	O
TA.130	Conduct Backup and Recovery Test	This task is recommended if it is a specific project requirement.	O	O	O	O
TA.140	Conduct Disaster Recovery Test	This task is recommended if it is a specific project requirement.	O	O	O	O

Back to Top

C.ACT.PACDC Prepare to Acquire and Convert Data – Construction

All tasks within this activity are recommended for WebCenter implementation projects if data is to be migrated from a legacy system.

The work of this activity evolves during the development of a project. It begins in Elaboration with the identification of the source systems and evolves into the actual data source of the attributes needed in the target system. In many cases, some type of transformation is needed to conform to the target system's architecture. Some data elements needed in the target system may not be available. These elements may be entered manually through the application or in some cases, a new function is required to maintain the "missing" source data elements. The final source to target mappings with the transformations should be documented for WebCenter implementation projects.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
CV.027.2	Perform Data Mapping	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
RA.170.2	Conduct Data Quality Assessment	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
CV.035.2	Define Manual Conversion Procedures (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
CV.040.2	Design Conversion Components (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
CV.050.2	Prepare Conversion Test Plans (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O

Back to Top

C.ACT.ACDC Acquire and Convert Data – Construction

All tasks within this activity are recommended for WebCenter implementation projects if data is to be migrated from a legacy system.

Task ID (Link to WebCenter	Task Name					

Supplemental Task Guidance)	(Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
CV.030.2	Prepare Conversion Environment (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
CV.055.2	Implement Conversion Components (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
CV.060.2	Perform Conversion Component Unit Test (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
CV.063.2	Perform Conversion Component Validation Test (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
CV.064.1	Install Conversion Components (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
CV.065.1	Convert and Verify Data (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O

Back to Top

C.ACT.PD Produce Documentation

This activity consists of publishing the appropriate documentation and producing the Online Help. During the Transition phase, you will have an opportunity to review all implemented system changes and system defects for any impact on the Documentation work products and finalize these work products.

Documentation is often requested for WebCenter WCM projects – If documentation has been requested all tasks in this activity should be completed.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
DO.060	Publish User Reference Manual	This task is recommended if it is a specific project requirement.	O	O	O	O

Back to Top

C.ACT.DEUT Design End-User Training

The Design End-User Training activity consists of executing the Training tasks to design the training for the users of the new WebCenter system.

In a WebCenter system implementation, user learning events are typically conducted in the Transition phase.

Task ID (Link to						

WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TR.060	Conduct User Learning Needs Analysis	This task is recommended if it is a specific project requirement.	O	O	O	O
TR.070	Develop User Learning Plan	This task is recommended if it is a specific project requirement.	O	O	O	O

Back to Top

C.ACT.BEUT Build End-User Training

The Build End-User Training activity consists of executing the Training tasks to build the training for the users of the new WebCenter system.

In a WebCenter system implementation, user learning events are typically conducted in the Transition phase.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TR.080	Develop User Learningware	This task is recommended if it is a specific project requirement.	O	O	O	O
TR.090	Prepare User Learning Environment	This task is recommended if it is a specific project requirement.	O	O	O	O

Back to Top

C.ACT.TEUC Train End Users - Construction

The Train End Users activity consists of executing the Training tasks for training the users of the new WebCenter system.

In a WebCenter system implementation, user learning events are typically conducted in the Transition phase.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TR.100.1	Conduct User Learning Events	This task is recommended if it is a specific project requirement.	O	O	O	O

Back to Top

C.ACT.IOCM / C.PMC.IOCM Initial Operational Capability Milestone

For WebCenter projects, the recommended activities should be completed in order to achieve this milestone in the project. It is also recommended that the optional activities, if applicable to the project, be completed as part of this milestone.

Activity ID	Activity Name	Sites	Social	Content	Portal
C.ACT.FR	Finalize Requirements	O	O	O	O
C.ACT.AC	Analyze - Construction	O	O	O	O
C.ACT.DC	Design - Construction	O	O	O	O
C.ACT.PTP	Perform Test Planning	O	O	O	O
C.ACT.PEC	Prepare Environments - Construction	R	R	R	R
C.ACT.DCCTSC	Develop Custom Component Test Scripts - Construction	R	R	R	R
C.ACT.DSTSC	Develop System Test Scenarios - Construction	R	R	R	R
C.ACT.DSITS	Develop Systems Integration Test Scenarios	R	R	R	R
C.ACT.ICC	Implement Custom Components	R	R	R	R
C.ACT.PCCTC	Perform Custom Component Testing - Construction	R	R	R	R
C.ACT.PST	Prepare for System Test	R	R	R	R
C.ACT.PSTC	Perform System Test - Construction	R	R	R	R
C.ACT.PSIT	Perform Systems Integration Test	R	R	R	R
C.ACT.PPT	Prepare for Performance Testing	O	O	O	O
C.ACT.PT	Prepare for Transition	R	R	R	R
C.ACT.PCO	Prepare for Cutover	R	R	R	R
C.ACT.TI	Test Infrastructure	O	O	O	O
C.ACT.PACDC	Prepare to Acquire and Convert Data - Construction	O	O	O	O
C.ACT.ACDC	Acquire and Convert Data - Construction	O	O	O	O
C.ACT.PD	Produce Documentation	O	O	O	O
C.ACT.DEUT	Design End-User Training	O	O	O	O
C.ACT.BEUT	Build End-User Training	O	O	O	O
C.ACT.TEUC	Train End Users - Construction	O	O	O	O

Back to Top

TRANSITION

D.ACT.SUAT Support User Acceptance Test

This activity consists of preparing users for testing, preparing the Acceptance Test Environment and supporting the users in conducting the Acceptance Test.

This environment is commonly known as the User Acceptance Testing (UAT) environment and is used for many WebCenter WCM implementation projects.

Although the tasks in this activity are optional, it is strongly recommended that user acceptance testing is conducted.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TE.105	Prepare Users for Testing	This task is recommended if User Acceptance Testing (UAT) is a specific project requirement. UAT is typically undertaken by the organization with Implementation Team support (TE.120).	O	O	O	O
TE.110	Prepare Acceptance Test Environment	This task is recommended if User Acceptance Testing (UAT) is a specific project requirement. UAT is typically undertaken by the organization with Implementation Team support (TE.120).	O	O	O	O
TE.120	Support Acceptance Test	This task is recommended if User Acceptance Testing (UAT) is a specific project requirement. UAT is typically undertaken by the organization with Implementation Team support (TE.120).	O	O	O	O

Back to Top

D.ACT.CPTST Conduct Performance Test

The Conduct Performance Test activity consists of executing the performance test and creating the Performance Test Results.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
PT.100	Execute Performance Test	This task is recommended if performance is a specific project requirement / objective.	O	O	O	O
PT.110	Create Performance Test Report	This task is recommended if performance is a specific project requirement / objective.	O	O	O	O

Back to Top

D.ACT.PPE Prepare Production Environment

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TS.050	Prepare Production Environment	In a WebCenter implementation, this task includes the implementation of required setups in all of the applications as part of your configuration. It also includes the installation of any custom extensions to the system intended for production use.	R	R	R	R

Back to Top

D.ACT.CDT Convert Data – Transition

The objective for this activity is to convert and cleanse data / content in preparation for the transition of the solution into the Production Environment.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
CV.064.2	Install Conversion Components (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
CV.065.2	Convert and Verify Data (Initial Load)	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O
CV.068.2	Clean Data	This task is recommended if data migration is a specific project requirement / objective.	O	O	O	O

Back to Top

D.ACT.TEUT Train End Users - Transition

The Train End Users activity consists of executing the Training tasks for training the users of the new WebCenter system.

In a WebCenter system implementation, user learning events are typically conducted in the Transition phase.

Task ID						

(Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TR.100.2	Conduct User Learning Events	This task is recommended if it is a specific project requirement.	O	O	O	O

Back to Top

D.ACT.FD Finalize Documentation

The Finalize Documentation activity provides a last opportunity to make any revisions and finalize documentation and Online Help.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
DO.110	Finalize Documentation	All of the WebCenter project documentation should be completed by the end of the Construction phase. However, during the Transition phase, minor revisions or changes to the software system may cause updates to any or all of the documentation work products. This task covers the incorporation of any of those changes into the Documentation work products.	R	R	R	R

Back to Top

D.ACT.GP Go Production

The Go Production activity consists of going production.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TS.052	Implement Production Support Infrastructure	This task is recommended for WebCenter projects in order to activate the support personnel and procedures for the new business system and review requirements for support-related services from software suppliers, contractors, help desks, and other support services.	R	R	R	R

TS.058	Verify Production Readiness	This task is recommended for WebCenter projects to formally verify that the organization's systems, host facilities, local area networks (LANs), wide area networks (WANS), and people are prepared for production. Typically, this task is driven by the organization with Implementation team support.	R	R	R	R
TS.060	Go Production	This task is highly recommended for all WebCenter projects.	R	R	R	R

Back to Top

D.ACT.SIP / D.PMC.SIP System in Production Milestone

For WebCenter projects, the recommended activities should be completed in order to achieve this milestone in the project. It is also recommended that the optional activities, if applicable to the project, be completed as part of this milestone.

Activity ID	Activity Name	Sites	Social	Content	Portal
D.ACT.SUAT	Support User Acceptance Test	O	O	O	O
D.ACT.CPTST	Perform Performance Test	O	O	O	O
D.ACT.PPE	Prepare Production Environment	R	R	R	R
D.ACT.CDT	Convert Data - Transition	O	O	O	O
D.ACT.TEUT	Train End Users - Transition	O	O	O	O
D.ACT.FD	Finalize Documentation	R	R	R	R
D.ACT.GP	Go Production	R	R	R	R

Back to Top

PRODUCTION

E.ACT.MPSP Manage Production System Performance

The Manage Production System Performance activity provides for managing the Production Environment. The objective for this activity is to monitor and adjust the WebCenter system based on production performance.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
PT.120	Conduct Production Performance Management	This task is recommended.	R	R	R	R

Back to Top

E.ACT.EPS Evaluate Production System

The objective for this activity is to audit the WebCenter system after the move to production.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
TE.019.2	Collect, Assess, and Refine KPI Measurements	This task is recommended if it is a specific project requirement.	O	O	O	O
PS.010	Audit System	This task is recommended for WebCenter projects in order to analyze the system against the requirements / objectives identifying any problems.	R	R	R	R

Back to Top

E.ACT.RPP Resolve Production Problems

The Resolve Production Problems activity consists of analyzing and resolving production problems.

The ongoing system maintenance begins during this activity. Maintenance is typically not triggered by technical issues that the support or help desk address; this type of maintenance focuses on necessary and preventative actions.

Ongoing system maintenance should address the following:

- timing of maintenance procedures
- reporting unusual occurrences
- interpreting system indicators
- logging completion of maintenance work
- adjusting the software and hardware for anticipated business changes

Verify that all normal, ongoing activities keep the system protected, purged, and operating as efficiently as possible. Make sure a log is available for recording all change events. Standard checklists can be incorporated for normal, standing tasks that must be performed.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
PS.050	Analyze Problems	recommended	R	R	R	R

PS.060	Monitor and Respond to System Problems	This task is recommended to resolve the problems identified during the problem analysis (PS.050).	R	R	R	R

Back to Top

E.ACT.PF Plan for Future

The Plan for Future activity consists of determining the Future Functional Enhancements and prioritizing them in the Future MoSCoW List as well as measuring the effectiveness of the organizational change effort and making post-Go Live recommendations.

Although the tasks in this activity are optional, it is strongly recommended that some form of enhancement planning takes place.

Task ID (Link to WebCenter Supplemental Task Guidance)	Task Name (Link to OUM Base Task Overview)	Task Notes	Sites	Social	Content	Portal
PS.135	Determine Future Functional Enhancements	This task is recommended if the implementation is part of a multi-stage project, for example, part 1 of 2.	O	O	O	O

Back to Top

E.ACT.SO / E.PMC.SO Sign-Off Milestone

For WebCenter projects, the recommended activities should be completed in order to achieve this milestone in the project. It is also recommended that the optional activities, if applicable to the project, be completed as part of this milestone.

Activity ID	Activity Name	Sites	Social	Content	Portal
E.ACT.MPSP	Manage Production System Performance	R	R	R	R
E.ACT.EPS	Evaluate Production System	R	R	R	R
E.ACT.RPP	Resolve Production Problems	O	O	O	O
E.ACT.PF	Plan For Future	O	O	O	O

Back to Top

ORACLE

Copyright © 2006, 2016, Oracle and/or its affiliates. All rights reserved.

WEBCENTER SUPPLEMENTAL TASK GUIDELINES - INCEPTION PHASE

Back to View

This document contains OUM supplemental task guidance for WebCenter projects.

- The first column of the following table provides a complete list of all tasks in this document for which "supplemental" guidelines are provided as well as a quick link to the "supplemental" task guideline in this document.
- The second column provides a link to the OUM Task Overview.

The task guidelines in this document should be used to supplement the guidelines that appear in the OUM Task Overview.

WebCenter - OUM Supplemental Task Guidelines (this document) collapse table | expand table	OUM Task Overview
A.ACT.GBRI Gather Business Requirements - Inception	
RD.001 Detail Business and System Objectives	RD.001 Detail Business and System Objectives
RD.005 Create System Context Diagram	RD.005 Create System Context Diagram
RD.065 Develop Domain Model (Business Entities)	RD.065 Develop Domain Model (Business Entities)
A.ACT.GR Gather Solution Requirements	
RD.042.1 Develop Glossary	RD.042.1 Develop Glossary
RD.045.1 Prioritize Requirements (MoSCoW)	RD.045.1 Prioritize Requirements (MoSCoW)
RD.055 Detail Supplemental Requirements	RD.055 Detail Supplemental Requirements
RD.130.1 Develop Baseline Architecture Description	RD.130.1 Develop Baseline Architecture Description
RA.023.1 Develop Use Case Model	RA.023.1 Develop Use Case Model
A.ACT.CR Consolidate Solution Requirements	
RD.140.1 Create Requirements Specification	RD.140.1 Create Requirements Specification
RD.150.1 Review Requirements Specification	RD.150.1 Review Requirements Specification

A.ACT.GSP Gather Supporting Requirements	
TE.005.1 Determine Testing Requirements	TE.005.1 Determine Testing Requirements
TA.010 Conduct Technical Architecture Workshop	TA.010 Conduct Technical Architecture Workshop
DO.010 Define Documentation Requirements and Strategy	DO.010 Define Documentation Requirements and Strategy
A.ACT.TPT Train Project Team	
TR.010.1 Define Training Strategy	TR.010.1 Define Training Strategy

Back to Top

A.ACT.GBRI GATHER BUSINESS REQUIREMENTS - INCEPTION GUIDANCE

RD.001 Detail Business and System Objectives

OVERVIEW

This is an extremely important task as it outlines the objectives for any project implementing WebCenter. Upon completion of this task, you should have identified all of the organization 's business and system objectives relevant for your project.

APPROACH

This task should ideally be undertaken as a workshop involving the business, the IT department, and a solution architect. It may also be necessary to involve Project Management at some point in the workshop. Typically, this task could form part of a kick-off event where the business sponsor would provide their goal at the beginning of the workshop in order to get the participants focused. It is recommended that the workshop is undertaken over 2 days, with 1-2 days gap in between – this gap allows the workshop participants to gather additional information and react to topics discussed on the first day. In some cases, various participants may not agree on certain objectives therefore the workshop leader will need to ensure that such discussions should be kept to a minimum and then discussed outside of the workshop. Any decision made outside of the workshop must then be communicated to all workshop participants.

Note: Consider delivering task, Create System Context Diagram (RD.005) within the workshop. This allows the workshop participants to refer to the diagram when reviewing each objective.

Note: It is recommended that the Glossary (RD.042) is completed prior to the workshop. This allows the workshop participants to refer to the definitions and terms when reviewing each objective. It may be necessary to update the Glossary within the workshop as new terms are identified.

Preparation

It is recommended that you request the business to provide a list of specific measurable objectives and ask them to return these to you in order to prepare the schedule for the workshop (not all information has to be completed). The number of objectives identified by the business will impact the length of the workshop and the time allocated to discuss each item. It is also recommended that you send out the workshop agenda and the initial list of objectives to each participant well in advance so that each participant is clear as to the goal of the workshop and what they need to provide.

WORK PRODUCT

The work product format can be any of those recommended within the OUM Method Pack, however, it is recommended to keep the list format simple and understandable. The recommended template for WebCenter is to use the MS Excel version with the following structure:

Tab 1: **Title Page**
- Tab 2: **Document Control**
  - Change Record
  - Reviewers
  - Approvers
- Tab 3: **Additional Information**
  - Relationship to other projects
  - Key drivers and selling points
- Tab 4: **Business Objectives**
  - List of business objectives
- Tab 5: **System Objectives**
  - List of system objectives (for formatting see below)

The formatting of the System Objectives (Tab 5) spreadsheet should clearly identify each objective and the associated information. This will aid in providing the project team with the required information and understanding project scope. The following table indicates the recommended columns for the spreadsheet:

Column	Description
Group / Topic	This value is used to provide a grouping making it easier for the project team to locate a specific objective.
Objective ID	This value is essential so that project members can uniquely identify the objective. The value will ultimately be mapped to the requirements in the MoSCoW list (RD.045).
Objective	This value is the objective description and must be measurable – try to ensure that you meet the quality criteria set out in the RD.001 Method Pack guidelines.
Scope	This value can be used to identify in which part of the project the objective is related i.e. WebCenter Portal or WebCenter Content. This is an optional field and can be used for other purposes. This value can also identify if an objective is moved out-of-scope.
Source	This value identifies the source of the objective such as a specific department within the business. This is useful if you require further information about a specific objective.
Process	In some cases, the customer may have already mapped out the business processes. This value can be used to identify the related process providing more context.
Priority	This value is optional but very useful if the project team needs to provide early prioritization of their objectives. Further prioritization will still be required within the MoSCoW List (RD.045).
Delivery Method	In some cases, the solution architect may be able to provide an early indication as to whether the objective can be met out-of-the-box, or through customization. While this value is optional, it can help the business to decide the prioritization against other objectives.
Complexity	In some cases, the solution architect may be able to provide an early indication as to the complexity involved in delivering the objective. While this value is optional, it can help the business to decide the prioritization against other objectives.
Comments	This column can be used to provide additional information related to the objective, such as, outstanding decisions or further context.

Note: Try to ensure that each objective is numbered as they will be cross referenced within further documentation (i.e., the MoSCoW List). Also, please try to group the objectives into sensible groups to help locate the information at a later stage.

Note: If a Statement of Work has been provided by the organization that responds to the requirements set out in this task, then this can be used as an input into the workshop.

RD.005 Create System Context Diagram

OVERVIEW

This task is recommended for all WebCenter projects as it provides the business and the project team with the context of the full system indicating the various inputs and outputs.

APPROACH

This task should be undertaken as early as possible within the project and reviewed on a regular basis. Ideally, this task should be undertaken prior to, or during, the Business and System Objectives (RD.001) workshop as it will allow the participants to refer to the system context while reviewing the system objectives. The work product of this task will form the basis of the Use Case Model (RA.023) and the MoSCoW List (RD.045) where further revisions may be necessary.

Preparation

Prepare a draft version of the System Context Diagram as soon as you have a basic understanding of the project scope. If you have scheduled an Business and System Objectives (RD.001) workshop, then it is recommended that you have a draft version of this document available in advance.

WORK PRODUCT

- Only document the input and output data on the lines to each actor, i.e., ‘user id and password’ or ‘search request’.
- The border of the “system box” in the middle is the scope of the project. Therefore, your system objectives must relate to what is inside the box, and not what is outside.
- The actor/system interactions are represented by the information flows into and out of the system. The detailed functional requirements are detailed in use cases.

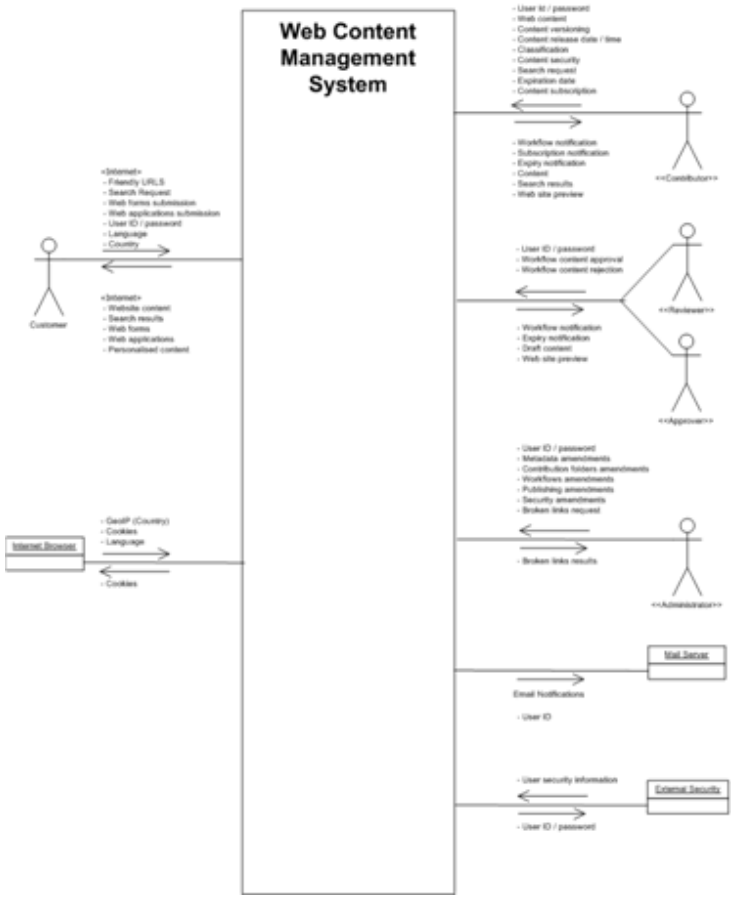

RD.065 (.1 and .2) Develop Domain Model (Business Entities)

OVERVIEW

This task requires more than one iteration for WebCenter Content projects in order to capture the metadata and security information using class diagramming techniques.

APPROACH (WebCenter Content)

For the first iteration of this task in Inception, work with the project team to produce:

- list of basic content objects (content types / content profiles) required for the project
- foundation list of metadata (can be extended as the project progresses)
- list of identified security roles (for users) and security groups (for content) - Typically, this is done in a second iteration of this task in Inception or early Elaboration. For the purposes of this supplemental guidance, iterations 1 and 2 will be in Inception.

For the third iteration of this task in Elaboration, conduct a half day workshop involving the business and a product specialist. During the workshop:

- Create high-level class diagrams to define the associated metadata for each of the basic content objects (content types / content profiles) to be considered in the system.
- Create high-level diagrams to define the associated security groups and permissions for each identified security roles.

Note: It is typically not possible to identify all content types, metadata, security roles, or security groups prior to or during the workshop, however, once this task is started it is easier to refine these models as the project progresses.

Note: The resulting work products from this task will be used to generate the security and metadata model configuration within the Application Setup Documents (DS.030) . Therefore, it is important to undertake this task as early as possible.

Examples

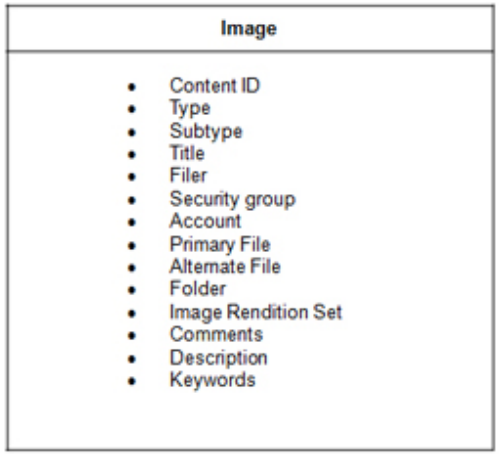

WebCenter Content – Metadata (1st Iteration)

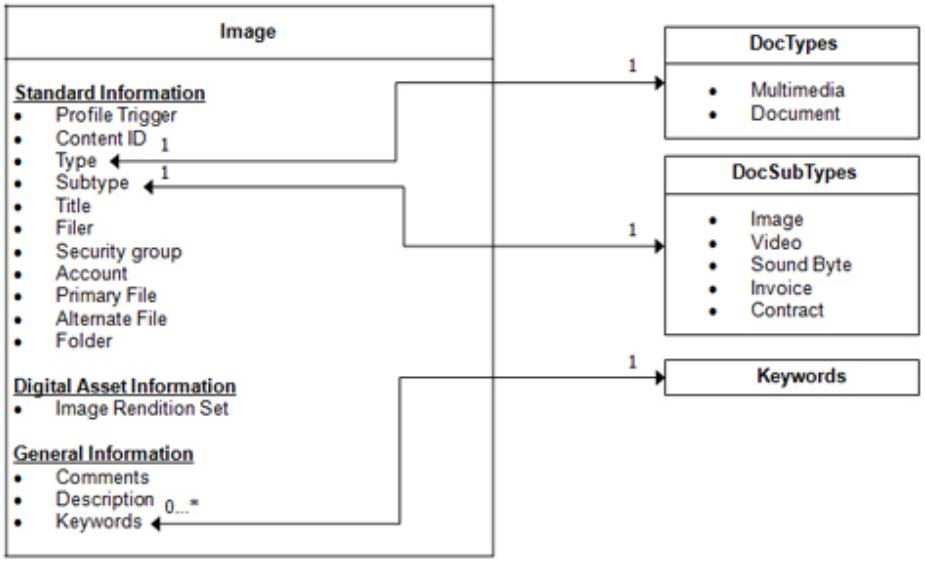

WebCenter Content – Metadata (2nd Iteration)

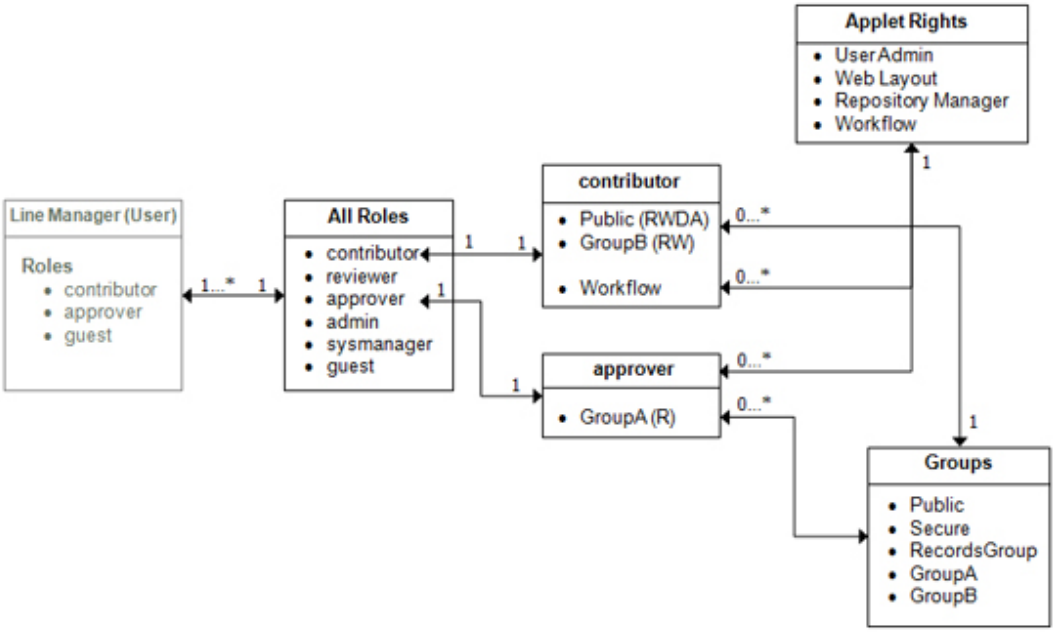

WebCenter Content – Security

Back to Top

A.ACT.GR GATHER SOLUTION REQUIREMENTS GUIDANCE

RD.042.1 Develop Glossary

OVERVIEW

This task is highly recommended for all WebCenter projects. It is essential that a project Glossary be developed as it avoids misinterpretation of WebCenter and business terms.

WORK PRODUCT

It is recommended that the Glossary work product contains the following sections:

- **Project specific definitions and terms** - Provides the definitions and terms used specifically for the project.
- **Definitions and terms used in [Organization Name]** - Provides the definitions and terms used by the organization on a regular basis particularly within the business and IT.
- **Definitions and terms used in [Application]** - Provides the definitions and terms applicable to the WebCenter product(s).
- **Definitions and terms used in Oracle** - Provides the definitions and terms used by Oracle Consulting on a regular basis inclusive of OUM.

Refer to the WebCenter Definitions and Terms for a high-level WebCenter Glossary.

Note: It is recommended that this task is completed prior the Business and System Objectives (RD.001) workshop. This allows the workshop participants to refer to the Glossary when reviewing each objective. It may be necessary to update the Glossary within the workshop as new terms are identified.

RD.045.1 Prioritize Requirements (MoSCoW)

OVERVIEW

The MoSCoW List (RD.045) is one of the most important work products for any WebCenter project. It must identify all of the use cases (functional requirements) for the project and their prioritization.

APPROACH

First, you should take the completed Business and System Objectives (RD.001) work product and then convert the objectives into project requirements. You should find that one or more objectives will map to one requirement in the MoSCoW List (see Mapping Objectives to Use Cases table below). It is recommended that you record the Objective IDs for each use case to ensure that you have no gaps, i.e., you haven't missed any objectives.

Objective	Use Case
The system will allow the full text searching of content, i.e., search of text within the content.	Search for Content
The system will provide search forms based on content type profiles.	

Once you have listed all of the functional requirements for the project, you should also capture the non-functional requirements (RD.055 - Detail Supplemental Requirements). This is essential to ensure that all project requirements are captured in one place.

Finally, the list of requirements should be completed, reviewed, refined, and approved within a workshop involving the business, the IT department, and a solution architect.

WORK PRODUCT

The work product format can be any of those recommended in OUM; however, it is recommended to keep the list format simple and understandable. The recommended template for WebCenter is to use the MS Excel version with the following structure:

- Tab 1: **Title Page**
- Tab 2: **General Instructions** (with content updates)
- Tab 3: **Sheet Definitions** (with content updates)
- Tab 4: **RD.045 MoSCoW List (highly recommended)**
  - List of Functional Requirements
- Tab 5: **RD.055 Supplemental Requirements (highly recommended)**
  - List of Non-Functional Requirements
- Tab 6: **RA.027 Rules Traceability (optional)**
  - List of Business Rules
- Tab 7: **TE.0xx Test Traceability (optional)**
  - List of Test Scripts

The formatting of the RD.045 MoSCoW List tab should clearly identify all functional requirements and the associated information. This will aid in providing the project team with the required prioritization and understanding project scope. The table below indicates the recommended columns for the spreadsheet:

The formatting of the RD.055 Supplemental Requirements tab should clearly identify all non-functional requirements and the associated information. This will aid in providing the project team with the required prioritization and understanding project scope. The table below indicates the recommended columns for the spreadsheet:

Column	MoSCoW List (RD.045) Description	Supplemental Requirements (RD.055) Description
MoSCoW ID	This value is essential so that project members can uniquely identify the **functional requirement**.	This value is essential so that project members can uniquely identify the **non-functional requirement**.
Supplemental Type	This column is not used for the MoSCoW List.	This value is useful to inform the project team of the nature of the non-functional requirement, e.g., Usability, Supportability, Performance, Security, etc.
Requirement Name	This value is essential so that project members can identify the name of the functional requirement.	This value is essential so that project members can identify the name of the non-functional requirement.
Requirement Description	This value provides a brief description of the functional requirement.	This value is essential so that project members can identify the name of the non-functional requirement.
Gap (COTS/Custom)	This value identifies if the functional requirement **cannot** be delivered out of the box, i.e., the required functionality cannot immediately be delivered within the WebCenter product.	This value identifies if the non-functional requirement cannot be delivered out of the box, i.e., the required functionality cannot immediately be delivered within the WebCenter product.
Urgency (Business Criticality)	This value is provided by the business and identifies how urgent the functional requirement perceived to be – take care when assigning this value as it is common for the business to mark everything with high urgency. This value will form part of the priority analysis.	Column heading should only be **Urgency**. This value is provided by the project team and identifies how urgent the non-functional requirement perceived to be. This value will form part of the priority analysis.
Complexity	This value identifies the complexity of the functional requirement as **estimated** by the solution architect. This value will form part of the priority analysis.	This value identifies the complexity of the non-functional requirement as **estimated** by the solution architect. This value will form part of the priority analysis.
Delivery Estimation	This value identifies the delivery **estimation** for the functional requirement as provided by the solution architect. This value will form part of the priority analysis.	This value identifies the delivery **estimation** for the non-functional requirement as provided by the solution architect. This value will form part of the priority analysis.

Delivery Method	This value identifies the anticipated delivery method for the functional requirement as provided by the solution architect. This value will form part of the priority analysis. Recommended values are OOTB (out-of-the-box), Configuration, and Custom – please ensure that you define these values within the project glossary to avoid any confusion.	This value identifies the anticipated delivery method for the non-functional requirement as provided by the solution architect. This value will form part of the priority analysis. Recommended values are OOTB (out-of-the-box), Configuration, and Custom – please ensure that you define these values within the project glossary to avoid any confusion.
Risk / Impact	This value is provided by the project team (including the business) and identifies the risk to both the business and the project. This value will form part of the priority analysis.	This value is provided by the project team (including the business) and identifies the risk to both the business and the project. This value will form part of the priority analysis.
Priority (M/S/C/W)	This value is essential to provide the prioritization of the functional requirement. Prioritization will help the project team to decide what has to be delivered first within the project. The prioritization value is derived from the Urgency, Complexity, Estimation, Delivery Method, and Risk/Impact values. You may also use the associated business objective(s) priority as a guide.	This value is essential to provide the prioritization of the non-functional requirement. Prioritization will help the project team to decide what has to be delivered first within the project. The prioritization value is derived from the Urgency, Complexity, Estimation, Delivery Method, and Risk/Impact values. You may also use the associated business objective(s) priority as a guide.
Scope	This value can be used to identify in which part of the project the functional requirement is related, i.e., WebCenter Portal or WebCenter Content. This is an optional field and can be used for other purposes. It is recommended that out-of-scope requirements are removed from the MoSCoW List, i.e., do not use these column to mark as out-of-scope.	This value can be used to identify in which part of the project the non-functional requirement is related, i.e., WebCenter Portal or WebCenter Content. This is an optional field and can be used for other purposes. It is recommended that out-of-scope requirements are removed from the MoSCoW List, i.e., do not use these column to mark as out-of-scope.
Business Process	This value indicates the process associated with the functional requirement (optional).	This column is not used for the Supplemental Requirements.
Owner	This value is recommended for identifying the current owner of the functional requirement during the project. It can be used in conjunction with the Status, and Comments values.	This value is recommended for identifying the current owner of the non-functional requirement during the project. It can be used in conjunction with the Status, and Comments values.
Status	This value is recommended for identifying the current status of the non-functional requirement during the project. It can be used in conjunction with the Owner, and Comments values.	This value is recommended for identifying the current status of the non-functional requirement during the project. It can be used in conjunction with the Owner, and Comments values.
Comments	This value can be used to provide additional information related to the functional requirement such as decisions or open issues. It can be used in conjunction with the Status, and Comments values.	This value can be used to provide additional information related to the non-functional requirement such as decisions or open issues. It can be used in conjunction with the Status, and Comments values.
Objective(s)	This value identifies the associated objective(s) for the functional requirement. The population of this value is highly recommended for traceability reasons.	This value identifies the associated objective(s) for the non-functional requirement. The population of this value is highly recommended for traceability reasons.

Note: As you can see from the table above, the recommended columns for both the MoSCoW and Supplemental lists are very similar. Therefore, it is typical for these to be merged into one single list or spreadsheet – with AutoFilter functionality enabled for filtering (available in MS Excel only).

RD.055 Detail Supplemental Requirements

OVERVIEW

This task is one of the most important tasks for any WebCenter project. The objective is to identify all of the non-functional requirements for the project and their

prioritization.

WORK PRODUCT

The format of the 'RD.055 Supplemental Requirements' tab or worksheet should clearly identify all non-functional requirements and the associated information. This aids the project team with prioritizing requirements and understanding project scope.

Please see task, Prioritize Requirements (MoSCoW) (RD.045) for further information as both tasks should be developed in parallel.

RD.130.1 Develop Baseline Architecture Description

OVERVIEW

This task is optional for WebCenter projects; however, it can prove useful in the early stages of any project. It helps provide understanding of factors that will influence the architecture of the system. It also allows the opportunity to develop strategies to address the identified factors and, if a product specialist is available, this can ease concerns over certain product related factors.

APPROACH

This task should ideally be undertaken during the Inception phase as a half day workshop involving business analysts, a system architect and ideally a product specialist. The workshop should consist of the following activities:

- Identify the project scope.
- Identify the project overview.
- Undertake project analysis focusing on the following areas:
    - Organizational Factors – Identify resource availability, skills, etc.
    - Technological Factors – Identify infrastructure limitations, standards, etc.
    - Product Factors – Identify performance, suitability concerns etc.

WORK PRODUCT

The standard OUM work product is suitable for WebCenter projects. Only complete the High-Level Software Architecture section if you have time or it is a requirement of the project.

RA.023.1 Develop Use Case Model

OVERVIEW

A Use Case Model (RA.023) should be created for all WebCenter projects that require customization, or enhancement to the system.

APPROACH

If the customer has provided a functional specification then that may be sufficient. It is recommended that the Use Case Model is created at the same time as the MoSCoW List as they are very closely linked.

WORK PRODUCT

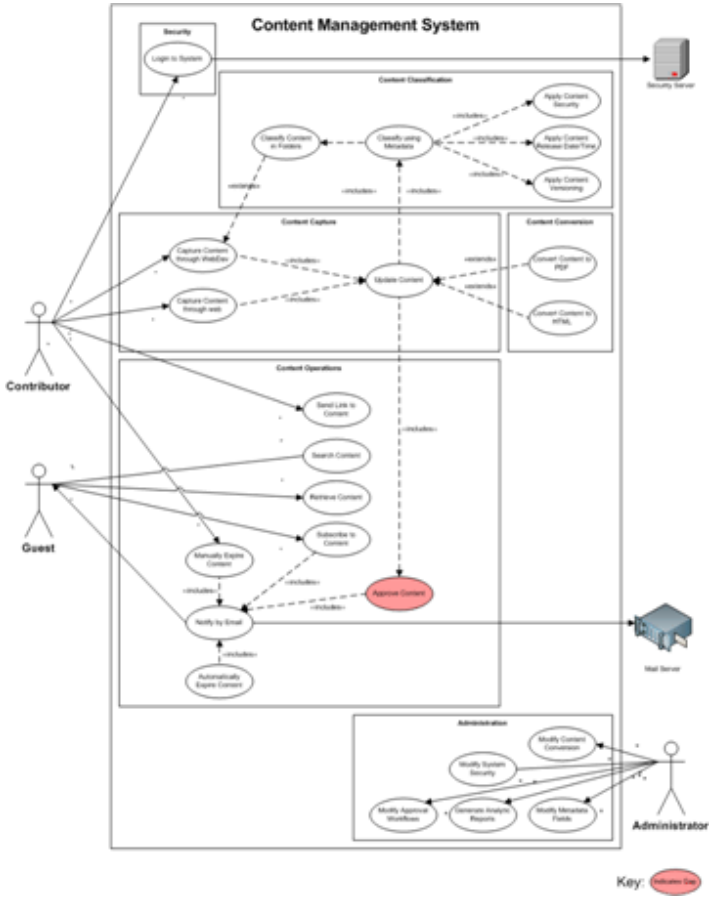

The Use Case Model should show a structured representation of all of the project use cases with the gaps, within scope, identified as appropriate. Ensure that both the diagram and MS Word work product are completed.

It is also very important to briefly describe the use cases and the actors within the provided OUM work product template. This will avoid much confusion when writing the use cases, and when reviewing the model in the requirements approval process.

Review

You should review this model in conjunction with the MoSCoW List (RD.045) in order to ensure that the all use cases are identified and have the correct relationship to each other. In some cases you may not identify all of the use cases at once, therefore the sign off/approval for the use cases, may come one iteration group at any time, or one package at any time.

Note: The use cases for Content Operations are system white box use cases and have been broken down to a very low level of granularity. These use cases are already realized into the UCM software. As such their level of granularity is appropriate for possible GAP resolutions when customization is required.

Note: For custom development, OUM recommends that CRUD (Create, Read, Update, Delete) use cases be generalized into a single ‘Maintain Content’ Use case, where the main success scenario is performing the ‘Create Content’. The ‘Update Content’, and the ‘Delete Content’ use cases would include the ‘Retrieve Content’, and ‘View Content’ steps.

Whenever the individual scenarios become complex, or may require customization, OUM advocates breaking them out into separate use cases as depicted in the diagram.

Back to Top

A.ACT.CR CONSOLIDATE SOLUTION REQUIREMENTS GUIDANCE

RD.140.1 Create Requirements Specification
RD.150.1 Review Requirements Specification

OVERVIEW

The Requirements Specification is recommended for every WebCenter project as it captures all of the requirement information for the project.

RD.140.1 - Create - Consolidate all the requirements into a unique document: the Requirements Specification. This task is only required when it is necessary to have a formal review. it may also be necessary when you must provide it has a major milestone in early iterations of a project. The Requirements Specification can contain both functional and non-functional (i.e., supplemental) requirements.

RD.150.1 - Review - The goal of this task is to remove defects on the requirements via peer review.

WORK PRODUCT

The standard OUM work product template is sufficient for most WebCenter projects. The diagram below indicates the recommended work products in Inception that should be linked to or added to the Requirements Specification.

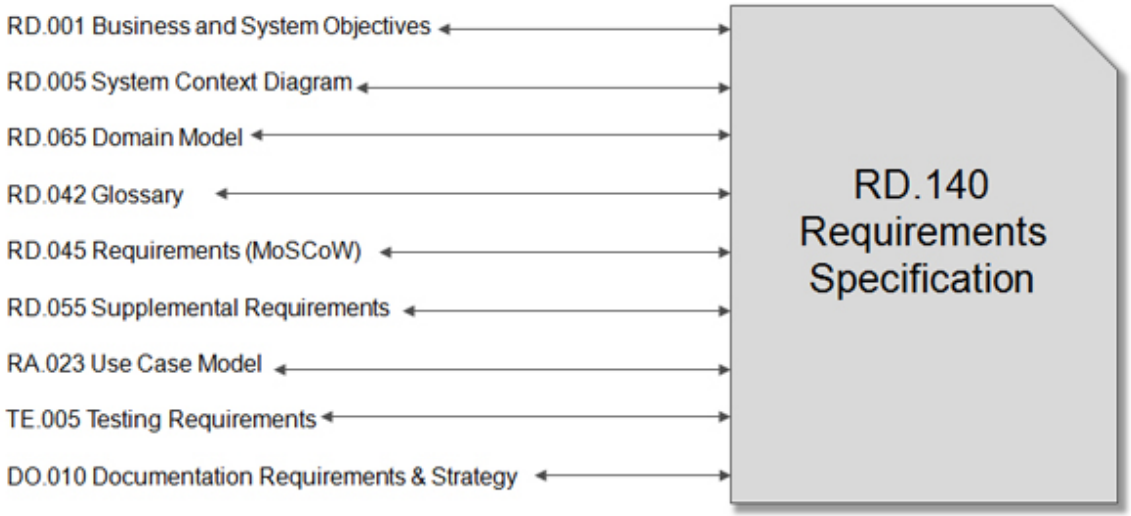

Note: The work products created in other requirement tasks do not need to be duplicated within this document; suitable links to the relevant documents should be placed into the appropriate sections, or insert the other documents as an object.

Note: Although seen as the best way of ensuring that everything is consolidated, inserting work products (children) into other work products (parents) can cause issues with document versioning and document approval. For example, if one of the inserted work products changes, then it will mean updating the revision of not only the child work product but also the parent. Approvers will not want to review a whole parent work product again purely because one of it child work products has changed. However, this can be avoided by identifying revision changes with the parent document.

Note: The requirements specification must be reviewed on a regular basis for all WebCenter projects, as it is common for requirements to change based on new decisions

and design issues. Typically, it is recommended to review the requirements specification work product after creating and updating any of the child tasks identified within task RD.140. Refer to the Elaboration phase iteration for this task to see additional guidance.

Back to Top

A.ACT.GSP GATHER SUPPORTING REQUIREMENTS GUIDANCE

TE.005.1 Determine Testing Requirements

OVERVIEW

In this task, all Testing Requirements for the WebCenter project are defined. This covers the requirements for all tests that should be performed in the project from unit testing to user acceptance testing. Refer to the Elaboration phase iteration for this task to see additional guidance.

APPROACH

Identify Testing Requirements from:

- existing test plans and standards
- testing objectives

WORK PRODUCT

It is not necessary to complete the OUM template for this task. You may wish to provide the Testing Requirements within the Supplemental Requirements (RD.055).

TA.010 Conduct Technical Architecture Workshop

OVERVIEW

This is a core task on WebCenter projects. It is particularly important for projects that have contractually delegated the bulk of the technical architecture responsibility to technical resources (outside the project team) either within the enterprise or to a third-party provider.

The workshop should be conducted as early in the project lifecycle as possible in order to make the enterprise aware of the expectations and requirements associated with their responsibility as well as to share leading practice approaches and experiences for WebCenter implementations.

DO.010 Define Documentation Requirements and Strategy

OVERVIEW

The goal of this task is to outline the overall requirements for creating documentation and specify the work products to be produced. You also identify the strategy you will use in publishing project-specific documentation.

This task is important for all WebCenter projects. It is not necessary to complete the OUM template for this task. You may wish to provide the requirements within the DO.010 tab of the MoSCoW List (RD.045).

Back to Top

A.ACT.TPT TRAIN PROJECT TEAM GUIDANCE

TR.010.1 Define Training Strategy

OVERVIEW

In this task, assess the education and training needs of the project team and user community and plan the delivery of the necessary training based on common areas of responsibility, interests, and skills. This training could be accomplished in classes, through online self-study training, or a combination of both. The types of training needed depend on the requirements of the WebCenter project.

This task is executed in both the Inception and Elaboration phases:

- The first iteration in the Inception phase addresses the education needs and training strategy for the project team.
- The second iteration in the Elaboration phase adds the strategy for training the end-user community.

Back to Top

ORACLE

Copyright © 2006, 2016, Oracle and/or its affiliates. All rights reserved.

WEBCENTER SUPPLEMENTAL TASK GUIDELINES - ELABORATION PHASE

Back to View

This document contains OUM supplemental task guidance for WebCenter projects.

- The first column of the following table provides a complete list of all tasks in this document for which "supplemental" guidelines are provided as well as a quick link to the "supplemental" task guideline in this document.
- The second column provides a link to the OUM Task Overview.

The task guidelines in this document should be used to supplement the guidelines that appear in the OUM Task Overview.

WebCenter - OUM Supplemental Task Guidelines (this document) collapse table | expand table	OUM Task Overview
B.ACT.DPS Define Project Strategy	
TE.005.2 Determine Testing Requirements	TE.005.2 Determine Testing Requirements
TE.010 Develop Testing Strategy	TE.010 Develop Testing Strategy
DO.020 Define Documentation Standards and Procedures	DO.020 Define Documentation Standards and Procedures
B.ACT.DI Define Infrastructure	
TA.020 Define Technical Architecture Requirements and Strategy	TA.020 Define Technical Architecture Requirements and Strategy
B.ACT.PEE Prepare Environments - Elaboration	
IM.090.1 Create Installation Routines	IM.090.1 Create Installation Routines
IM.007.1 Prepare Development Environment	IM.007.1 Prepare Development Environment
TE.018.1 Prepare Static Test Data	TE.018.1 Prepare Static Test Data
B.ACT.GBRE Gather Business Requirements - Elaboration	
RD.011.2 Develop Future Process Model	RD.011.2 Develop Future Process Model
RD.065 Develop Domain Model (Business Entities)	RD.065 Develop Domain Model (Business Entities)

MC.030 Map Business Requirements	MC.030 Map Business Requirements
B.ACT.SSC Specify Software Configuration	
MC.050.1 Define Application Setups	MC.050.1 Define Application Setups
B.ACT.PGA Perform Gap Analysis	
MC.100 Define and Estimate Application Extensions	MC.100 Define and Estimate Application Extensions
MC.110 Define Gap Resolutions	MC.110 Define Gap Resolutions
B.ACT.DUCM Develop Use Case Model	
RA.023.2 Develop Use Case Model	RA.023 Develop Use Case Model
B.ACT.CCPE Create Conceptual Prototype - Elaboration	
IM.005.2 Develop Conceptual Prototype	IM.005.2 Develop Conceptual Prototype
RA.030.2 Validate Conceptual Prototype	RA.030.2 Validate Conceptual Prototype
B.ACT.CS Consolidate Specification	
RD.042.2 Develop Glossary	RD.042.2 Develop Glossary
RD.045.2 Prioritize Requirements (MoSCoW)	RD.045.2 Prioritize Requirements (MoSCoW)
RD.140.2 Create Requirements Specification	RD.140.2 Create Requirements Specification
RD.150.2 Review Requirements Specification	RD.150.2 Review Requirements Specification
RA.027.2 Identify Candidate Business Rules	RA.027.2 Identify Candidate Business Rules
RA.180.1 Review Use Case Model	RA.180.1 Review Use Case Model
B.ACT.BSA Baseline Software Architecture	
RA.035 Develop High-Level Software Architecture Description	RA.035 Develop High-Level Software Architecture Description
B.ACT.DUCD Develop Use Case Details	
RA.024.1 Develop Use Case Details	RA.024 Develop Use Case Details
B.ACT.AE Analyze - Elaboration	
AN.090.1 Analyze User Interface	AN.090.1 Analyze User Interface
AN.100.1 Prepare Analysis Specification	AN.100 Prepare Analysis Specification
AN.110.1 Review Analysis Model	AN.110 Review Analysis Model
B.ACT.DE Design - Elaboration	
DS.080.1 Design Software Components	DS.080.1 Design Software Components
DS.130.1Design User Interface	DS.130.1Design User Interface
DS.140.1 Prepare Design Specification	DS.140.1 Prepare Design Specification
DS.160.1 Review Design Model	DS.160.1 Review Design Model

Back to Top

B.ACT.DPS DEFINE PROJECT STRATEGY GUIDANCE

TE.005.2 Determine Testing Requirements

OVERVIEW

Refine the Testing Requirements for the WebCenter project based on those requirements identified and further detailed in the Elaboration phase.

APPROACH

- Identify any new testing requirements from:
  - Functional Requirements (MoSCoW List – RD.045)
  - Non-Functional Requirements (documented in RD.045, RD.055 Supplemental Requirements tab)
- Review and comment on the Testing Requirements.
- Review and approve the Testing Requirements.

TE.010 Develop Testing Strategy

OVERVIEW

Develop the project direction in relation to testing. At a minimum, the Testing Strategy must address all of the requirements documented in the Testing Requirements (TE.005).

APPROACH

- Review Testing Requirements (TE.005).
- Review existing test plans and standards.
- Determine testing objectives.
- Identify the scope of the testing.
- Develop testing approach.
- Determine required test data.
- Determine constraints.
- Determine testing tools.
- Determine acceptance criteria.
- Document problem management procedure.
- Determine critical success factors.
- Determine risks and contingency.
- Determine testing metrics.

DO.020 Define Documentation Standards and Procedures

OVERVIEW

Specify the standards for all Documentation work products and determine the look and feel of the project documentation.

APPROACH

- Gather existing Documentation standards.
  - Paragraph and Sentence Structure, Usage, Lists, Translations, Numbers and Operations, Preferred Terms, etc.
- Determine Documentation development procedures.
  - Initial Material: Writing and Editing, Translation Procedures, Downloading, Change Control, Hardcopy and Reproduction, Review and Approval, etc.

Back to Top

B.ACT.DI DEFINE INFRASTRUCTURE GUIDANCE

TA.020 Define Technical Architecture Requirements and Strategy

OVERVIEW

This task identifies the application and technical Requirements and documents the strategy to be used for the design and development of the system being implemented.

APPROACH

Address the following types of environments:

-
  - Project Support Environment
  - Development Environment
  - Test Environment
  - Production Environment
- Consider and document the following:
  - Availability Requirements
  - Performance Requirements
  - Service-Level Agreements
  - High-Level Security and Control Requirements

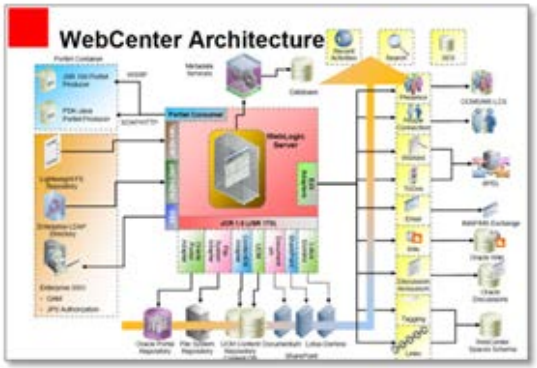

WORK PRODUCT

For WebCenter projects, it is recommended that the TA.020 work product be used as the master work product document for other TA work products by including or referencing the other TA work products.

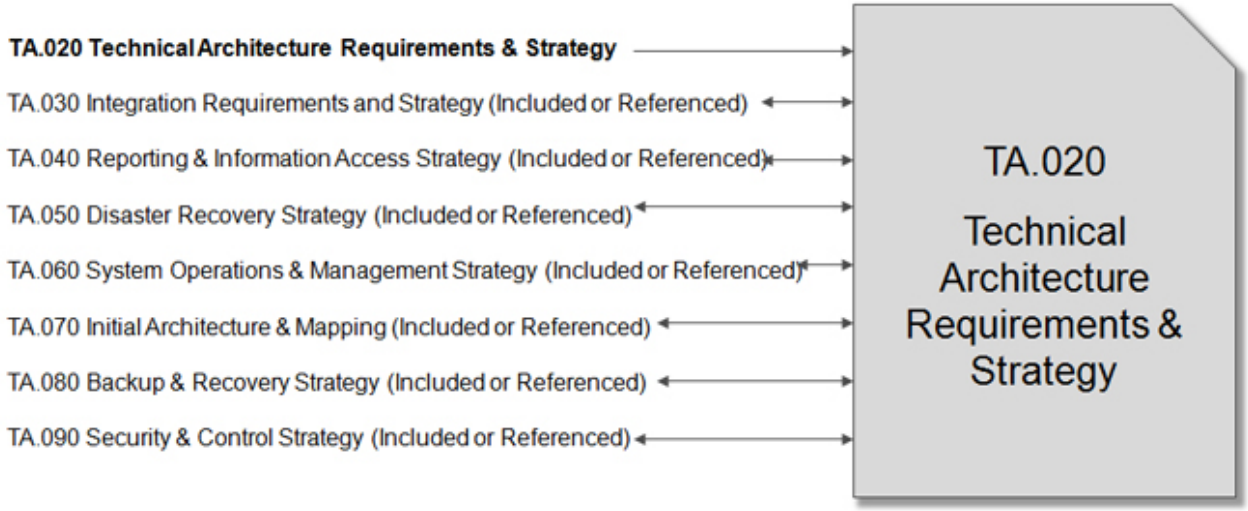

Back to Top

B.ACT.PEE PREPARE ENVIRONMENT - ELABORATION GUIDANCE

IM.090.1 Create Installation Routines

OVERVIEW

In a WebCenter implementation, the main goal of this task is to prepare a work product that can be used by the system administrator in order to install the system. The next iteration of this task in Construction will focus more on the specific system configuration (MC.050) and custom modules (DS.080).

APPROACH

- Identify the standard installation steps for the WebCenter product(s).
- Identify pre-installation steps in the work product.
  - add links to standard documentation and then customize for the implementation.
- Identify installation steps in the work product.
  - Add links to standard documentation and then customize for the implementation.
- Identify a verification checklist in the work product.
- Review the work product.



IM.007.1 Prepare Development Environment

OVERVIEW

Create or verify the Development Environment that you will need during the development effort. It is highly recommended that this task is conducted following, or at the same time as, the initial iteration of the Installation Routines task (IM.090.1). Refer to the Construction phase iteration for this task to see additional guidance.

APPROACH

- Review the Architecture Requirements and Strategy (TA.020).
- Identify and make available any required installation software.
- Identify and make available any required supporting systems, i.e., database, applications.
- Review and deliver steps in the Installation Routines work product (IM.090.1).
- Install and configure, or verify the environment operating system.
- Install and configure, or verify the App. Server / WebCenter product installation.
- Conduct test of the system to ensure validity of installation/configuration.

TE.018.1 Prepare Static Test Data

OVERVIEW

Prepare the required test data you will need throughout the project. This data should support prototypes (if required), unit tests (in the Development Environment), and any other tests. Refer to the Construction phase iteration for this task to see additional guidance.

APPROACH

- Review the Testing Strategy and appropriate test plans to see what data will be required.
- Determine required test data baselines.
- For each required set of test data, identify how it should be produced.
- Identify test data for each baseline.
- Produce test data for baselines.
- Quality check baseline test data.

Back to Top

B.ACT.GBRE GATHER BUSINESS REQUIREMENTS - ELABORATION GUIDANCE

RD.011.2 Develop Future Process Model

OVERVIEW

Define the Future Process Model (Future Business Model) in the form of integrated process flows

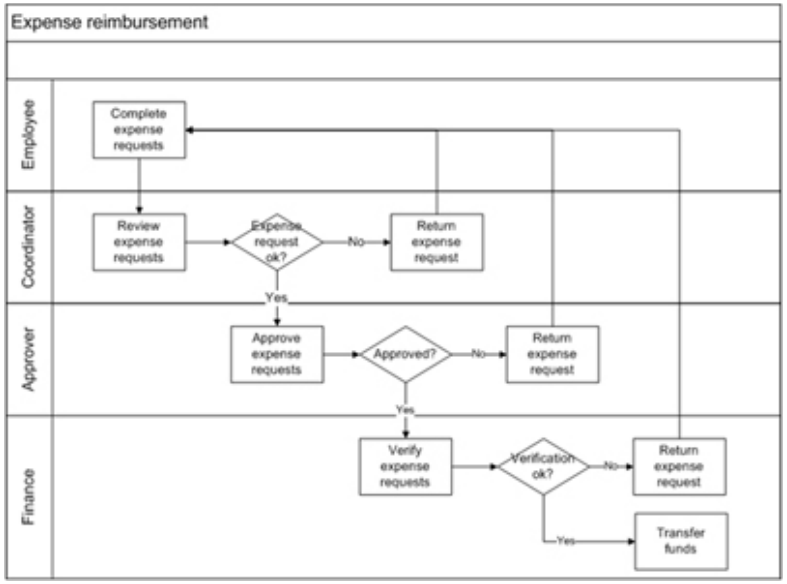

based on the business processes supported by the new WebCenter system. The model is created through iterations, starting with a higher level view in the Inception phase (if available), and progressing into a more detailed view in later iterations.

APPROACH

- Using one or more workshops may be the most appropriate technique for executing this task depending on the size and complexity of the project.
- Confirm and identify new high-level business triggering events to which the business and system must respond.
- Identify business actors.
- List each process and write a summary description for each.

WORK PRODUCT

Document the triggering events that drive the business areas that are to be automated and describe the future business process that the
business executes. The Future Process Model should include:

- a catalog describing all the triggering events
- diagrams of the business processes by which the business responds to those events

---

RD.065.3+ Develop Domain Model (Business Entities)

OVERVIEW

Following the Inception phase iteration(s), you should return to the Domain Model in Elaboration. In the next iteration of this task in Elaboration, add and associated any additional metadata fields or objects. You should also provide further information for each of the fields, such as, format and default values. Execute as many additional iterations of this task as necessary in order to compile the model prior to executing the task, Define Application Setups (MC.050). The following diagram shows a WebCenter Content example for defining the metadata.

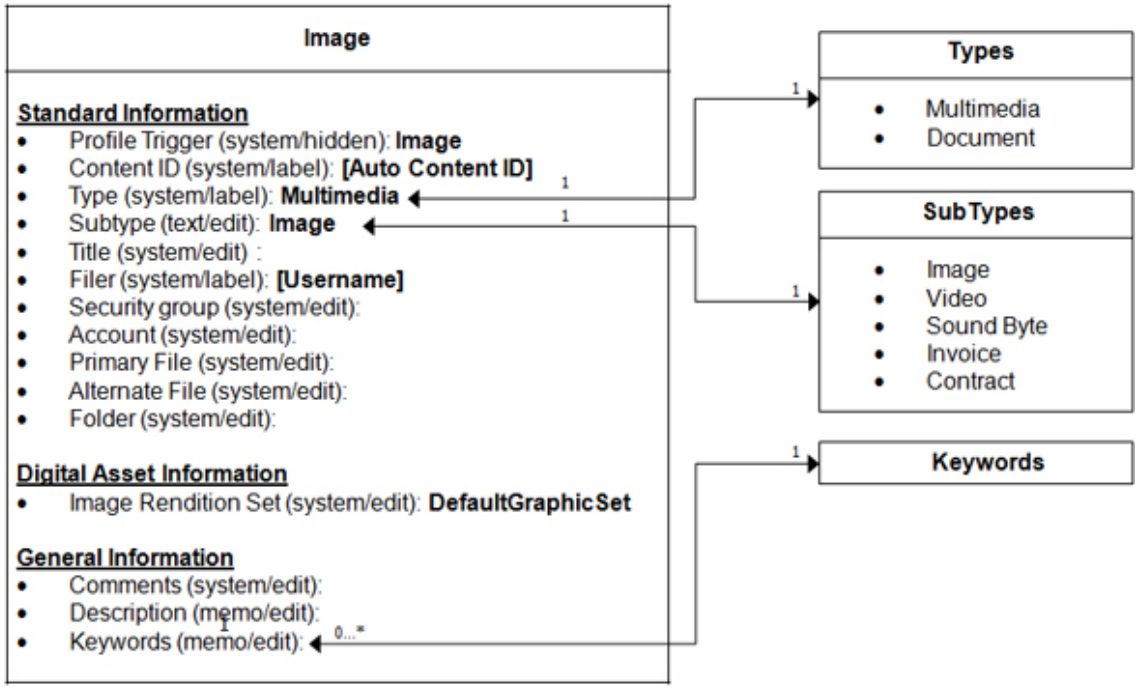

MC.030 Map Business Requirements

OVERVIEW

Assess the fit of the standard WebCenter product and system features to the detailed business requirements as reflected in the following work products:

- Future Process Model (RD.011)
- MoSCoW List (RD.045)
- Supplemental Requirements (RD.055)
- Use Case Model (RA.023)
- Use Case Specification(s) (RA.024)

Back to Top

B.ACT.SSC SPECIFY SOFTWARE CONFIGURATION GUIDANCE

MC.050.1 Define Application Setups

OVERVIEW

Define and document the detailed setup values needed to configure the WebCenter product(s). Continually refine the work product during the Design activity. Refer to the Construction phase iteration for this task to see additional guidance.

For WebCenter engagements, the resulting work product forms a shared central document for retaining and managing general configuration settings for the system. This

prevents conflicting configuration across design documents.

APPROACH

Option 1 - Create one master Application Setup Document that contains all of the individual inserted configuration documents.

- Easy to review, but not as easy to manage updates.

Option 2 - Create one Application Setup Document for each type of configuration and link them together with a master index configuration document.

- Easy to manage updates, but not as easy to review.

WORK PRODUCT

The work product could include:

- General System Configuration
- Metadata Model (WebCenter Content)
- Security Configuration (Security Models, Authority Provider Configuration, etc.)
- Schema Model
- Retention Schedules and Disposition (WebCenter Records)

Example

As an example, you would first t take the Metadata Model produced in from the Domain Model (RD.065) task. Next, create a Metadata Configuration based on this model as part of the task, Define Application Setups (MC.050). Once complete, insert the configuration into, or reference the configuration from, the Application Setup Documents work product. Remember, you may need to update this configuration again in the future so it may be better to keep it as a separate document until the completed Application Setup Documents are ready for review.

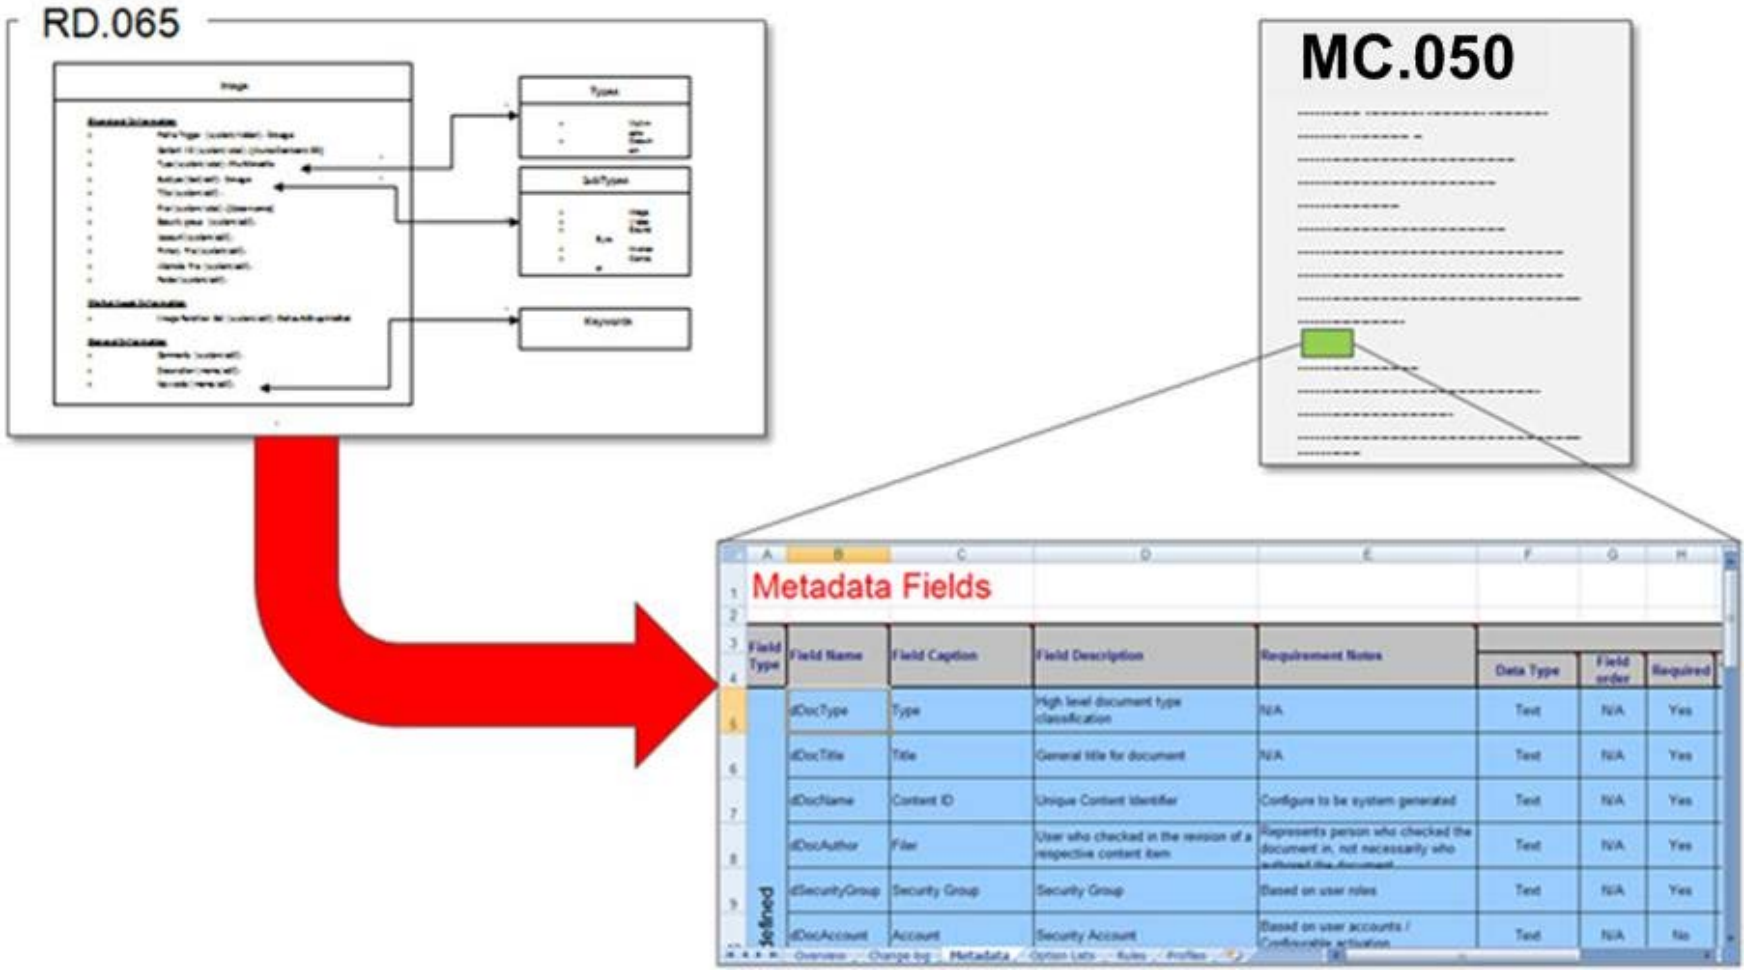

[Back to Top](#)

B.ACT.PGA PERFORM GAP ANALYSIS GUIDANCE

MC.100 Define and Estimate Application Extensions

OVERVIEW

Following the mapping of business requirements (MC.030), if custom development is required to extend the standard capabilities of a WebCenter product, you must consider the various alternatives to satisfy them and estimate the effort required to complete them.

MC.110 Define Gap Resolutions

OVERVIEW

Review the alternative solutions for satisfying gaps with the organization and then identify and document the preferred option, based on the organization's preference.

Back to Top

B.ACT.DUCM DEVELOP USE CASE MODEL GUIDANCE

RA.023.2 Develop Use Case Model

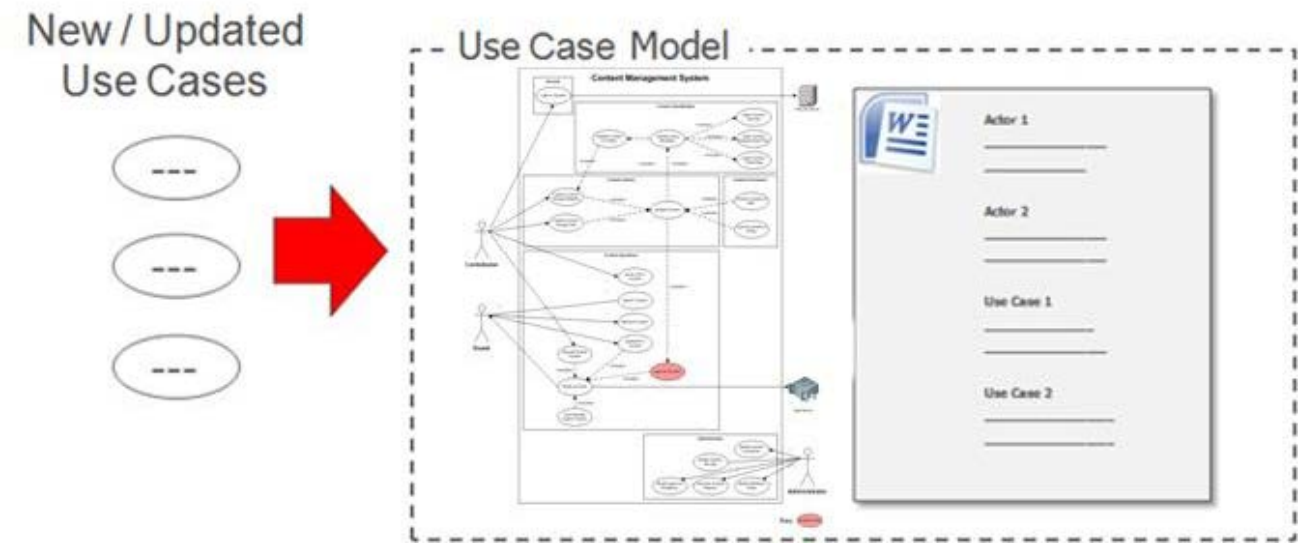

OVERVIEW

The Use Case Model should be refined to capture any new or updated use cases.

Back to Top

B.ACT.CCPE CREATE CONCEPTUAL PROTOTYPE - ELABORATION GUIDANCE

IM.005.2 Develop Conceptual Prototype
RA.030.2 Validate Conceptual Prototype

OVERVIEW

the purpose of the Conceptual Prototype is to visually show the users your understanding of an agreed to set of requirements. This is a mock-up prototype and is usually created using low-fidelity tools, such as sketches on whiteboards or flip charts that represent the general idea behind the user interface but not the details.

In a WebCenter implementation, this task is generally performed only when there is a need to gain further clarification of the business requirements represented in the use cases.

Important Note: This task should not be used to produce the overall storyboard and wireframes for a WebCenter system. Such work products should be produced in the task, Analyze User Interface (AN.090).

APPROACH

- Review the requirements (identified in the MoSCoW List), and agree on which requirements should be prototyped. Typically, execute these tasks at the same time as the task, Develop Use Case Details (RA.024).
- Produce storyboards and wireframes to help understand the requirements.
- Validate the Conceptual Prototype in a workshop.

WORK PRODUCT

- storyboards (typically on a whiteboard or flip chart)
- wireframes (typically on a whiteboard or flip chart)

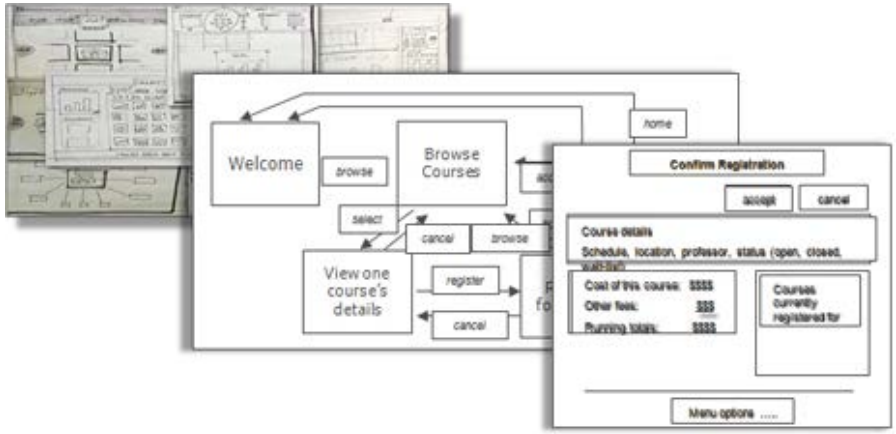

Back to Top

B.ACT.CS CONSOLIDATE SPECIFICATION GUIDANCE

RD.042.2 Develop Glossary

OVERVIEW

Review and refine the Glossary in order to ensure that all terms are identified and correctly defined.

RD.045.2 Prioritize Requirements (MoSCoW)

OVERVIEW

Review and refine the MoSCoW List in order to ensure that all use cases are identified, correctly defined and prioritized.

RD.140.2 Create Requirements Specification

RD.150.2 Review Requirements Specification

OVERVIEW

The following diagram indicated the recommended work products in Elaboration, in addition to those identified in Inception, that should be added to the Requirements Specification, either through links are added directly to the document.

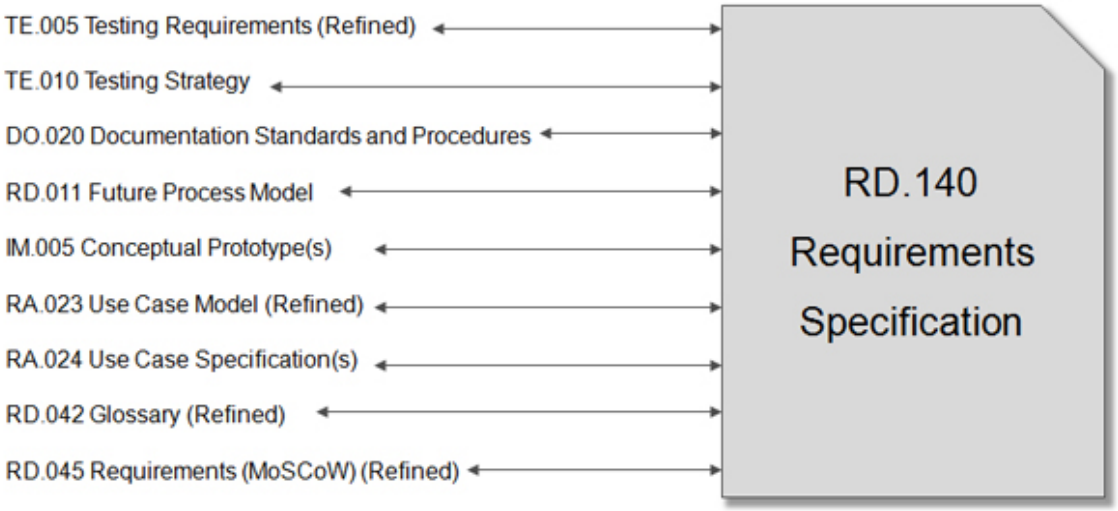

RA.027.2 Identify Candidate Business Rules

OVERVIEW

This optional task highlights business rules as statements that describe business policies. For example, a piece of content submitted into a system by a contributor should always go into a workflow to attain management sign-off before being released.

This task is recommended if you need to include WebCenter Records retention lifecycle type of rules, i.e., taking the organization's records policy and making a concise set of rules.

RA.180.1 Review Use Case Model

OVERVIEW

Review the Use Case Model (RA.023 and RA.024) in conjunction with the MoSCoW List (RD.045) in order to ensure that all use cases are identified and have the correct relationship to each other.

Back to Top

B.ACT.BSA BASELINE SOFTWARE ARCHITECTURE GUIDANCE

RA.035 Develop High-Level Software Architecture Description

OVERVIEW

This task is recommended in order to prioritize and group the use cases / processes. It establishes an initial set of groupings and priorities for the use cases that you have identified.

Identify the use cases that describe important or critical functionality or that involve requirements that must be developed early in the project. These use cases will be described as “architecturally-significant” and will be identified in the High-Level Software Architecture portion of the Architecture Description.

APPROACH

- Prepare a document highlighting the proposed grouping / prioritization.
- Discuss and agree on the grouping / prioritization in a short meeting with the organization.
- Ensure that critical requirements are grouped together, i.e., Iteration group #1, Iteration group #2, etc. This grouping will allow the project team to focus on the critical iteration groups during Elaboration.

WORK PRODUCT

Establish an initial set of packages (iteration groups) and priorities for the use cases that you have identified.

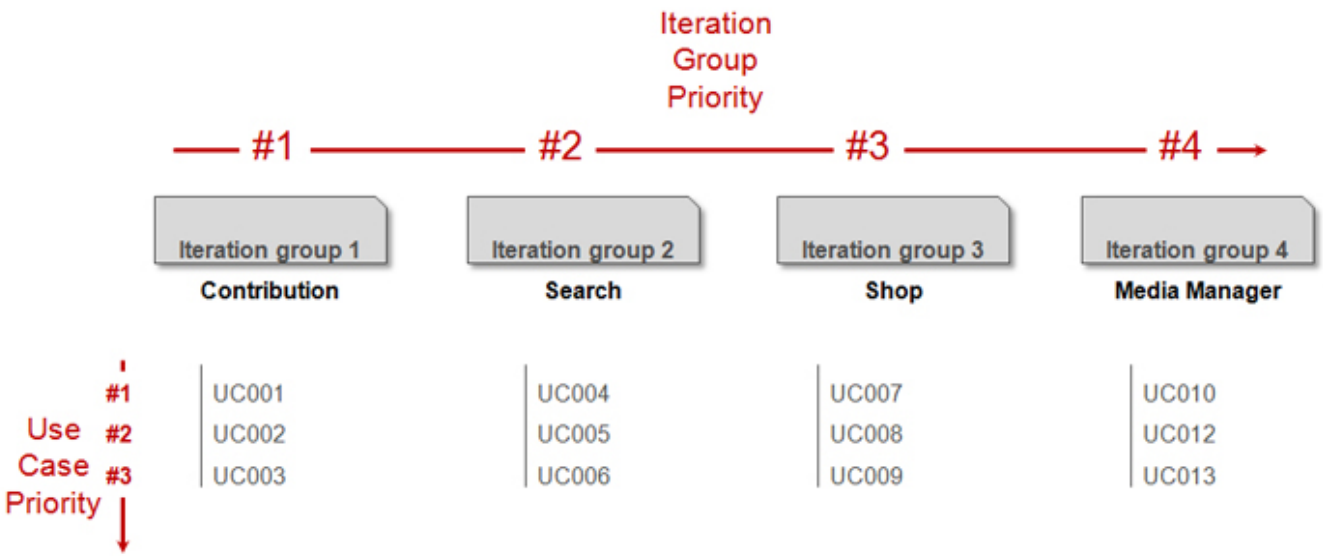

Back to Top

B.ACT.DUCD DEVELOP USE CASE DETAILS GUIDANCE

RA.024.1 Develop Use Case Details

OVERVIEW

Use Case Specification documents should be produced for all functional requirements that are not present within the packaged software. This task should be completed regardless of the type of WebCenter project.

APPROACH

Allow plenty of time for the production of use case specification documents. Remember that a specification document must be produced for each use case that cannot be delivered out-of-the-box. The product specialist and business analyst work together to draft each document – this has proven to reduce the level of customization required for a use case.

WORK PRODUCT

The standard OUM work product template is sufficient for all WebCenter projects.

Note: Make full use of the Technology and Data Variations List section in order to eliminate the need for repeating such details in the scenario steps. This typically causes much confusion for not only the writer of the document but also for the reviewers.

Note: Make use of the Open Issues and Decisions sections within this document as you will typically find that this document is frequently reviewed prior to final approval. These sections allow you to track comments and decisions made in each revision.

Remember: The first step of the Main Success Scenario should be the same as the Trigger.

Back to Top

B.ACT.AE ANALYZE - ELABORATION GUIDANCE

AN.090.1 Analyze User Interface

OVERVIEW

The purpose of this task is to develop a deeper understanding of the look and feel of the user interface as well as the flow that the users will experience when interacting with the system. In this task, you do not design how the user interface will work, but verify your understanding of the users' needs and validate the feasibility of the functional requirements. This task is highly recommended when implementing WebCenter Portal or WebCenter Sites as it provides the business with a clear understanding of the web pages to be provided and their relationship to each other. It also provides the business with a view of the proposed page layouts and their relationship to use cases.

APPROACH

- Review any existing storyboards and wireframes from the Conceptual Prototype (IM.005).
- Produce storyboards and wireframes for the WebCenter implementation. This should be delivered in a PowerPoint presentation including a storyboard on the first page followed by the wireframes.
- Validate the storyboard and wireframes in a presentation / workshop.

Note: You may need to go through multiple iterations of this task for WebCenter Portal and WebCenter Sites. Once the approach has been agreed, you should then move on to task, Design User Interface (DS.130).

WORK PRODUCT

Example

AN.090 Storyboard and Wireframes

AN.100.1 Prepare Analysis Specification

OVERVIEW

Assemble all the information that is required to describe a use case package into a complete Analysis Specification, ready for review. In general, there would be one of these specifications written for each use case package on a project. Prior to being passed on to the designers, the Analysis Specification is reviewed for defects and, as necessary, the defects are corrected.

APPROACH

- Use the High-Level Software Architecture (RA.035) work product to identify the system use case packages (within an iteration group) and their associated priority.
- Produce an Analysis Specification (AN.100) master document - one for each of the use case packages, based on the package priority. Include the following tasks within each specification document:
    - Data Analysis (AN.050)
    - Behavior Analysis (AN.060)
    - Business Rules Analysis (AN.070)
    - User interface Analysis (AN.090)
- Review each Analysis Specification document with the business analyst(s) and ambassador users.

WORK PRODUCT

The diagram below indicates the recommended work products that should be referenced from, or included within the Analysis Specification.

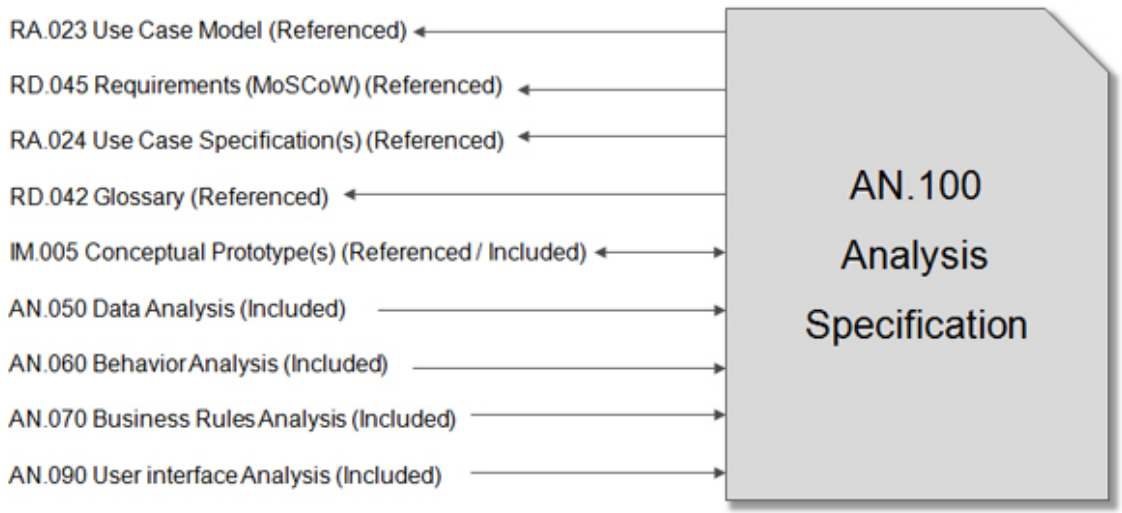

For larger size projects it may be necessary to use a document structure similar to the following:

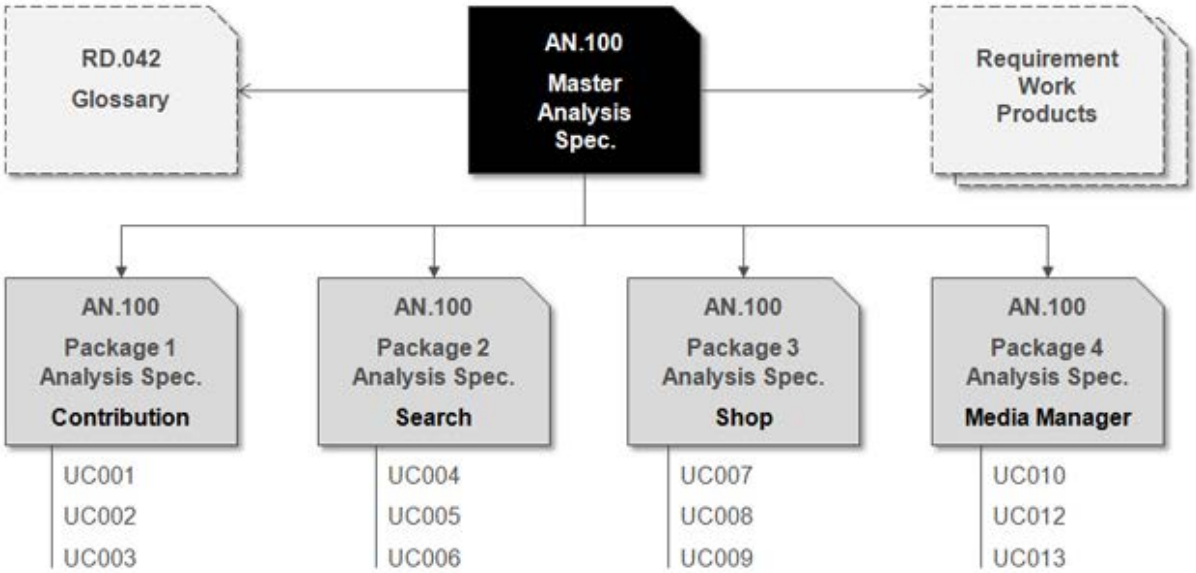

AN.110.1 Review Analysis Model

OVERVIEW

The Analysis Model refers to the complete collection of work products that are developed as part of analyzing the use cases during Analysis. Once work on these materials for a given iteration has been completed, and the materials are ready for review, a team consisting of analysts, users, designers, and architects reviews the Analysis Model, and suggest changes as needed.

APPROACH

- Reviewers must briefly review the Analysis Model initially in a workshop to understand the structure of the model.
    - Identify key resources to approve the model.
- Reviewers must review the Analysis Model work products individually.
- Defects can be found and changes may be required.
    - Some changes can affect scope and these may require formal change requests. Other changes do not affect scope, and these should be discussed with the analyst.
- Once the Model is approved by each of the selected approvers, they must send an email or provide other written confirmation that the Model is accepted.
- Complete a short Approval template – See the work product.

WORK PRODUCT

Create and complete a short Approval template where approval can be inserted into a grid.

Document/Section	Business Analyst	Solution Architect	Oracle Consulting	Business
AN.100 **Master Analysis** Specification				
Signed By				
AN.100 **Package 1** Analysis Specification - Contribution				
Signed By				
AN.100 **Package 2** Analysis Specification - Search				
Signed By				
AN.100 **Package 3** Analysis Specification - Shop				
Signed By				
AN.100 **Package 4** Analysis Specification – Media Manager				
Signed By				

Back to Top

B.ACT.DE DESIGN - ELABORATION GUIDANCE

DS.080.1 Design Software Components

OVERVIEW

Develop the detailed design for a software component. For WebCenter products, a software component is a custom module that contains a number of interoperating processes or classes that work together to perform the high-level functional responsibilities for a major part of the system.

- This task is highly recommended.
- It is delivered In the form of 1 or more documents representing the design of each system component.
- Add a reference to the associated Analysis Specifications (AN.100).
- Add a reference in the Design Specification (DS.140) to each DS.080 document.
- Associated system configuration should be identified within the Application Setup Documents (MC.050) work product.
- You can also create storyboards and wireframes within this task to help clarify the component design.

WORK PRODUCT

Each document should include:

- Technical Overview
  - Document Structure
  - Related Documents
- Requirements Met by this Design
  - UC001

    - UC002
    - UC003
- Associated Analysis
    - AN.100 - Contribution
    - AN.100 – Search
- Application Setups (Associate with MC.050)
- Component Specific
    - Component Overview
    - Specific Configuration
    - Associated Templates (Storyboard & Wireframes)
    - Associated Java Classes
    - Associated Services
    - Associated Database Information
    - Associated Language Strings

DS.130.1 Design User Interface

OVERVIEW

The purpose of this task is to transform the storyboards and wireframes in the User Interface Analysis (AN.090) and specify how they will be implemented. You also specify the navigation sequences between each of the interfaces in the storyboard(s). This task is highly recommended when implementing WebCenter Portal or WebCenter Sites as it provides the final design for the portal or website to be developed.

APPROACH

It is recommended that either of the following approaches is used to satisfy this task:

- The AN.090 User Interface Analysis work product is enhanced to show the actual design of the pages.
- Produce a new DS.130 work product that shows the final design for the storyboard and wireframes.

The following artifacts should be considered as part of this task:

- **Define portal/site navigation.** This is important as it will define your site navigation model. Also, include associated information like whether the new page opens in a new window
- **Design interface.** Add the detail to the pages defined in AN.090 User Interface Analysis. This includes details such as:
    - Pagelet Producers
    - Portlets
    - iFrames
    - Servlets
    - WebCenter Components
    - Personalization
- **Apply initial text and images.** In order to ensure the portal/site looks correct, it is usually necessary to apply real text and images in the design. This will give the business a greater confidence in what is to be delivered.
- **Stylesheets / Scripts** – Design associated stylesheets and scripts required to satisfy the page designs.

WORK PRODUCT

Typically, the User Interface Analysis (AN.090) is enhanced to show the detailed design.

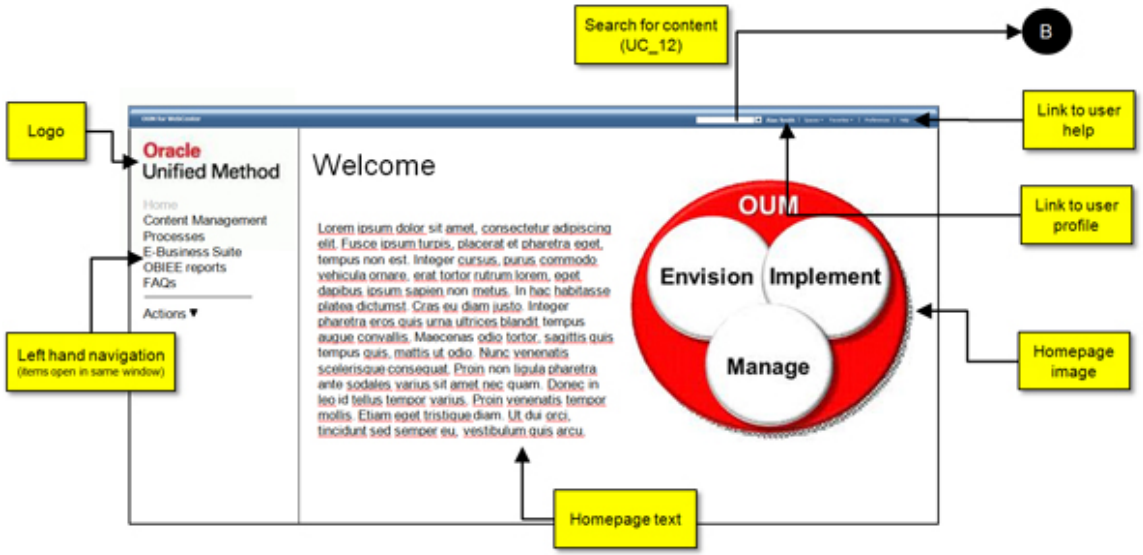

DS.140.1 Prepare Design Specification

Assemble all the information that is required to describe the design of the system into a complete Design Specification, ready for review. Prior to being passed on to the developer, the Design Specification is reviewed for defects and, as necessary, the defects are corrected.

This artifact collects all of the Design work products into a single document and equates roughly to the “technical design document” that was used in some older methodologies.

WORK PRODUCT

The Design Specification should include:

- Technical Overview
  - Document Structure
  - Related Documents
- Information on Standards
  - Java Design (including naming conventions)
  - Component Design (including naming conventions)
  - HTML Design (including naming conventions)
- Packages Overview
  - Package 1 (Associate with DS.080)
  - Package 2 (Associate with DS.080)
  - Package 3 (Associate with DS.080)
  - Package 4 (Associate with DS.080)
- Application Setups (Associate with MC.050)

The diagram below indicates the recommended work products that should be referenced from, or included within the Design Specification.

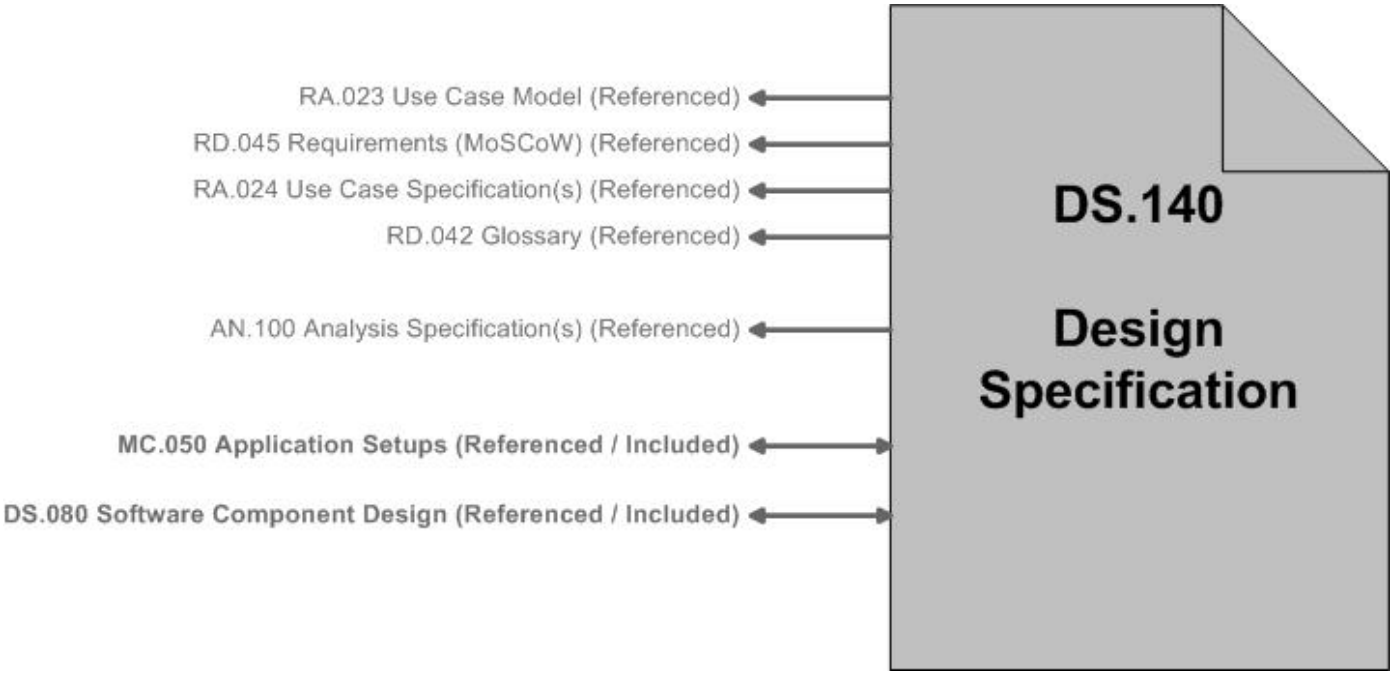

For larger size projects it may be necessary to use a document structure similar to the following:

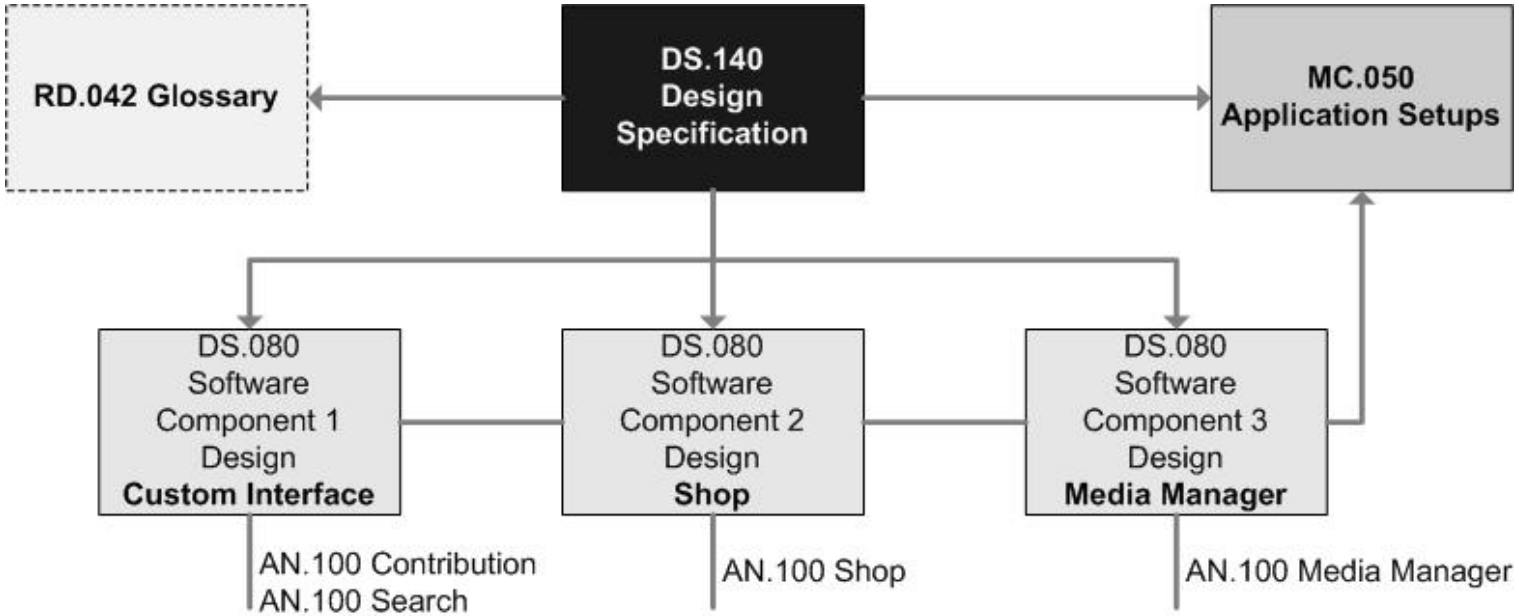

DS.160.1 Review Design Model

OVERVIEW

The Design Model refers to the complete collection of artifacts that are developed to design the software to be developed. Once work on these materials for a given iteration has been completed, and the materials are ready for review, a team consisting of analysts, designers, and architects review the Design Model, and suggest changes as needed.

APPROACH

- Reviewers must briefly review the Design Model initially in a workshop to understand the structure of the model.
  - Identify key resources to approve the model.
- Reviewers must review the Design Model work products individually.
- Defects can be found and changes may be required.
  - Some changes can affect scope and these may require formal change requests.
  - Other changes do not affect scope, and these should be discussed with the analyst.
- Once the Model is approved by each of the selected approvers, they must send an email or provide other written confirmation that the Model is acceptable.
- Complete a short Approval template – see the work product.

WORK PRODUCT

Create and complete a short Approval template where approval can be inserted into a grid.

Document/Section	Business Analyst	Solution Architect	Oracle Consulting
DS.140 Design Specification			
Signed By			
DS.080 **Package 1** Design Specification - Contribution			
Signed By			
DS.080 **Package 2** Design Specification - Search			
Signed By			
DS.080 **Package 3** Design Specification - Shop			
Signed By			
DS.080 **Package 4** Design Specification – Media Manager			
Signed By			

Back to Top

ORACLE

Copyright © 2006, 2016, Oracle and/or its affiliates. All rights reserved.

WEBCENTER SUPPLEMENTAL TASK GUIDELINES - CONSTRUCTION PHASE

Back to View

This document contains OUM supplemental task guidance for WebCenter projects.

- The first column of the following table provides a complete list of all tasks in this document for which "supplemental" guidelines are provided as well as a quick link to the "supplemental" task guideline in this document.
- The second column provides a link to the OUM Task Overview.

The task guidelines in this document should be used to supplement the guidelines that appear in the OUM Task Overview.

WebCenter - OUM Supplemental Task Guidelines (this document) collapse table | expand table	OUM Task Overview
C.ACT.PEC Prepare Environments - Construction	
IM.007.2 Prepare Development Environment	IM.007.2 Prepare Development Environment
TE.018.2 Prepare Static Test Data	TE.018.2 Prepare Static Test Data
C.ACT.DCCTSC Develop Custom Component Test Scripts - Construction	
TE.020.2 Develop Unit Test Scripts	TE.020.2 Develop Unit Test Scripts
TE.035.2 Create Integration Test Scenarios	TE.035.2 Create Integration Test Scenarios
C.ACT.DSTSC Develop System Test Scenarios - Construction	
TE.025.3 Create System Test Scenarios	TE.025.2 Create System Test Scenarios
C.ACT.ICC Implement Custom Components	
IM.050 Implement Components	IM.050 Implement Components
IM.070 Assemble Components	IM.070 Assemble Components
IM.090.2 Create Installation Routines	IM.090.2 Create Installation Routines

C.ACT.PCCTC Perform Custom Test - Construction	
TE.030.2 Perform Unit Test	TE.030.2 Perform Unit Test
TE.040.2 Perform Integration Test	TE.040.2 Perform Integration Test
C.ACT.PST Prepare for System Test	
MC.050.2 Define Application Setups	MC.050.2 Define Application Setups
C.ACT.PSTC Perform System Test - Construction	
TE.070.2 Perform System Test	TE.070.2 Perform System Test
C.ACT.PSIT Perform Systems Integration Test	
TE.100 Perform Systems Integration Test	TE.100 Perform Systems Integration Test
C.ACT.PT Prepare for Transition	
TA.150 Define Final Platform and Network Architecture	TA.150 Define Final Platform and Network Architecture
C.ACT.PCO Prepare for Cutover	
TS.020.2 Define Cutover Strategy	TS.020.2 Define Cutover Strategy
TS.030 Develop Installation Plan	TS.030 Develop Installation Plan
TS.040 Design Production Support Infrastructure	TS.040 Design Production Support Infrastructure

Back to Top

B.ACT.PEC PREPARE ENVIRONMENTS - CONSTRUCTION GUIDANCE

IM.007.2 Prepare Development Environment

OVERVIEW

Verify / refine the Development Environment that you will need during the development.

APPROACH

- Determine which development tools are required for development, e.g., Jdeveloper.
- Determine which unit testing tools and other automated development tools that will be used during development (if required).
- Detail the Development Environment Directory Structure Setup.
- Verify the configuration of the Database, Application Server, and WebCenter product installation.
- Finalize the setup of the Development Environment with all required components, configurations, and tools. This should be available in the Application Setup Documents (DS.030) work product.
- Provide developers with usernames and passwords for the environment.
- Conduct a test of the system to ensure validity of installation/configuration.
- Refine Application Setup Documents (DS.030) work product, if required.
- Refine Installation Routines (IM.090) work product, if required.

WORK PRODUCT

The Development Environment is available and developers are able to login into the system.

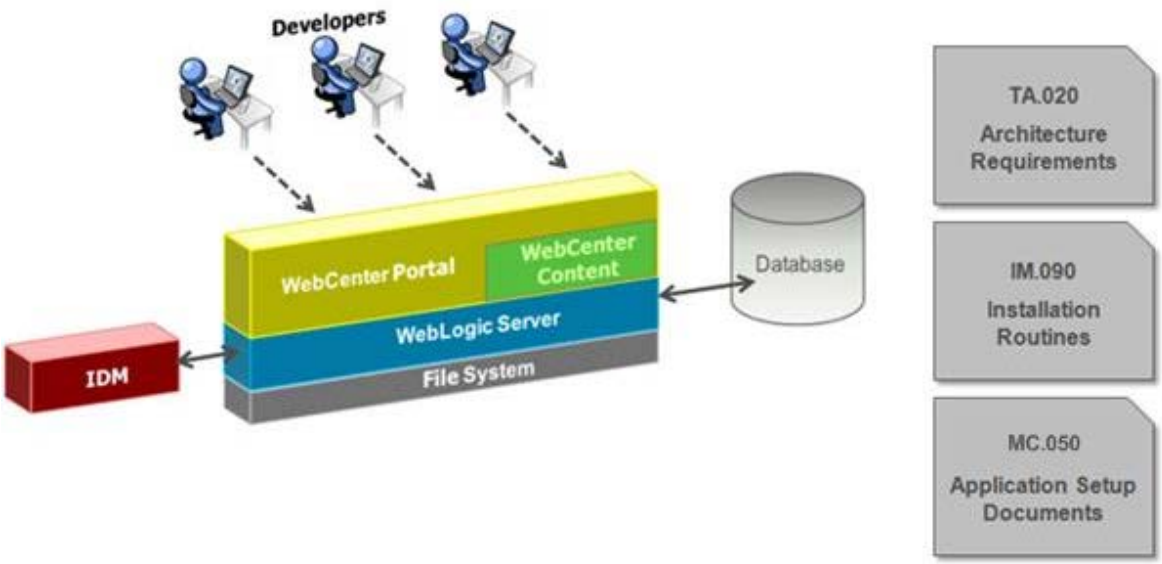

TE.018.2 Static Prepare Test Data

OVERVIEW

Review the required test data you will need throughout the remainder of the project. This data should support unit tests (in the Development Environment), and any other required tests.

APPROACH

Review and refine any work products provided in the first iteration of this task.

Back to Top

C.ACT.DCCTSC DEVELOP CUSTOM COMPONENT TEST SCRIPTS - CONSTRUCTION GUIDANCE

TE.020.2 Develop Unit Test Scripts

OVERVIEW

Develop scripts to test individual components. The tests validate that the component's inputs, outputs, and processing logic function are as required. This task is mainly performed in parallel with the actual development of the components. Thinking through how the component should be tested increases the understanding of what the component should do or produce.

APPROACH

You can use the templates within the OUM Method Pack, or create an Excel spreadsheet similar to that described on the next slide.

WORK PRODUCT

The recommended template for WebCenter is to use an MS Excel spreadsheet with the following structure:

- Tab 1: Title Page
- Tab 2: Document Control
  - Change Record, Reviewers, Approvers
- Tab 3: TE.020 Unit Test Report
- Columns should include:
  - Test ID
  - Associated Process(es)
  - Test Case Name
  - Summary of Steps
  - Expected Result
  - Result
  - Priority
  - Test Execution Date
  - Tester
  - Comments

TE.035.2 Create Integration Test Scenarios

OVERVIEW

An integration test verifies that application extension components are properly linked and no coding errors are generated when related components are linked together. In this task, you develop scripts to test interaction, or linkage, between related application extension modules. This uncovers any integration problems with other application extension components that provide or use the data manipulated by the target modules.

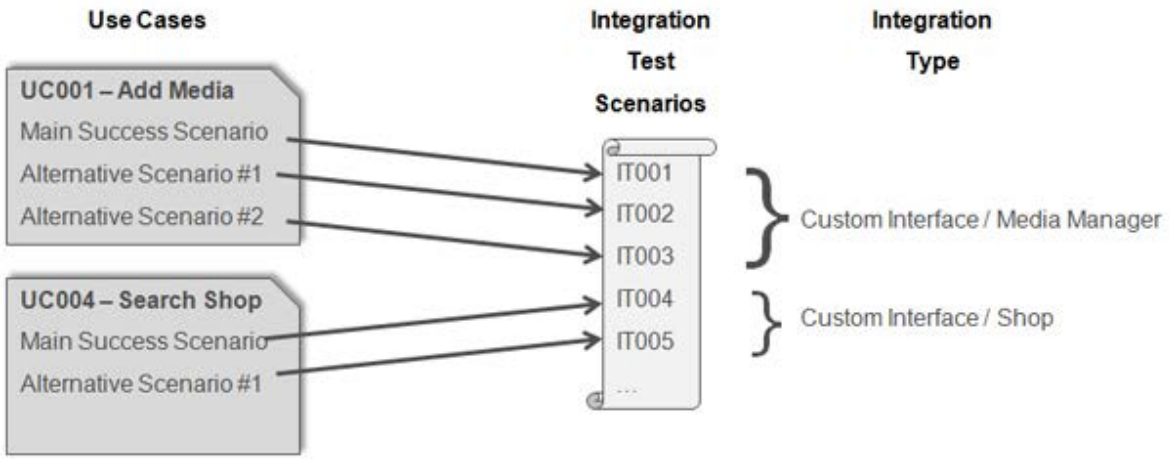

APPROACH

For each use case to be tested, define Integration Test Scenarios for each feature that should be tested.

WORK PRODUCT

The Use Case Integration Test Scenario includes the following information:

- ID and Name
- Reference to System Use Case Scenario
- Revision History
- Objectives for the Test
- Setup Requirements for the Test
- Pre-Conditions for the Test
- Required Test-Data
- Steps Included in the Scenarios
- Expected Result

Back to Top

C.ACT.DSTSC DEVELOP SYSTEM TEST SCENARIOS - CONSTRUCTION GUIDANCE

TE.025.3 Create System Test Scenarios

OVERVIEW

Develop the System Test Scenarios that you use during the final full system test at the end of the Construction phase. If the System Test Scenario relates to a use case, use the use case scenarios in the Use Case Model as a starting point. The Context Process Model can also be used to prepare System Test Scenarios at higher-levels, but details are based on the use case scenarios.

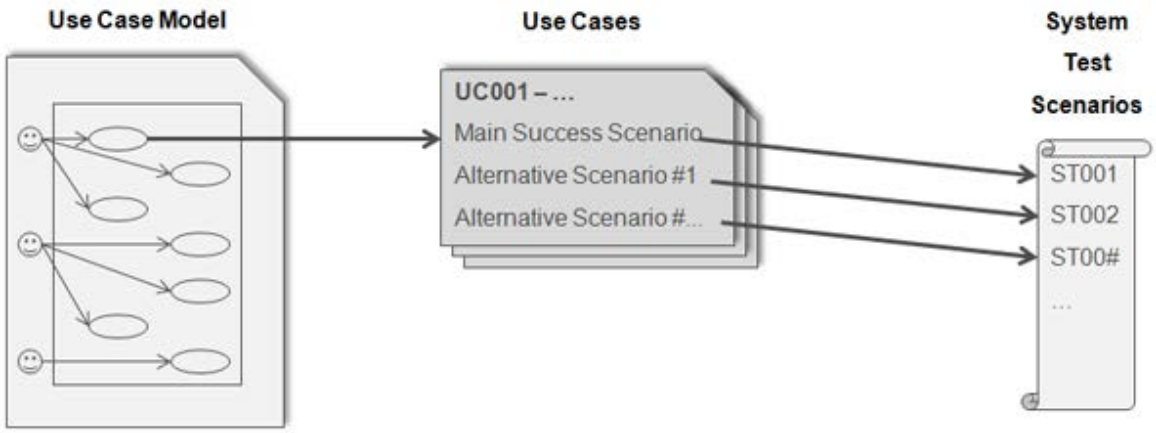

Back to Top

C.ACT.ICC IMPLEMENT CUSTOM COMPONENTS GUIDANCE

IM.050 Implement Components

OVERVIEW

This task is where you create the components of the system. You also perform the first round of testing as part of this task. Review and refine any work products provided in the first iteration of this task.

APPROACH

- Use the High-Level Software Architecture Description (RA.035) work product to identify the prioritization.
- Build each component to satisfy the design in each of the Software Component Design (DS.080) work products.
- Apply supporting configuration identified in both the DS.080 and DS.030 work products.
- Test component functionality to ensure that it satisfies the underlying design.

WORK PRODUCT

Create the components of the system using an agreed on prioritization.

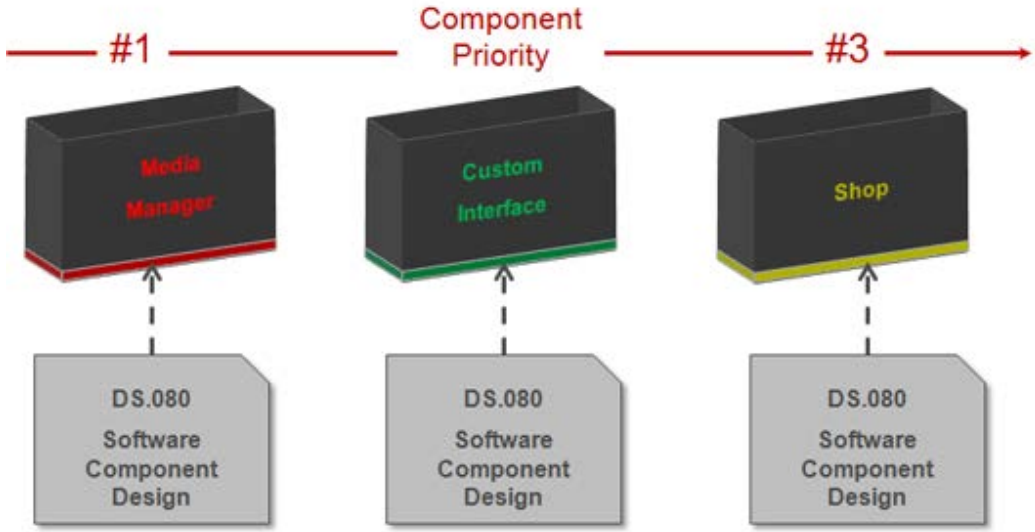

IM.070 Assemble Components

OVERVIEW

Integrate the components into a logical assembly of components. Such an assembly can consist of various types of components, including interface components and other types of components. This task ensures that an assembly fulfils its role and that the requirements (use cases and scenarios) identified for the assembly are correctly implemented.

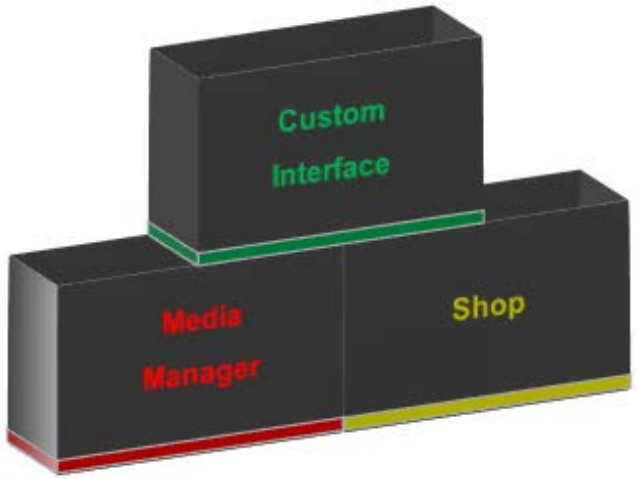

IM.090.2 Create Installation Routines

OVERVIEW

Review and refine the Installation Routines work product to ensure it's readiness for other environments, particularly Production.

APPROACH



- Update the work product based on any revisions to system configuration (DS.030) and custom modules (DS.080).
- Update the work product based on issues identified when installing the Development Environment.
- Update the work product based on any architecture changes that may have arisen (TA.020).
- Refine installation steps in the work product.
    - Customize the steps for the specific WebCenter implementation.
- Refine the verification checklist in the work product.
    - Review the work product following the system design to ensure accuracy.

Back to Top

C.ACT.PCCTC PERFORM CUSTOM COMPONENT TESTING - CONSTRUCTION GUIDANCE

TE.030.2 Perform Unit Test

OVERVIEW

Test the system components on an individual basis to verify that the inputs, outputs, and processing logic of each component functions without errors. This task is performed in parallel with the actual development of the components.

WORK PRODUCT

- Enter or confirm the required setup data.
- Review the Unit Test Script Report (TE.020) and complete the information.
- Perform the unit test and document the unit test results.
- Fix errors identified in the testing process.
- Update the design documentation, if required.
- Record the completed unit test script result for evidence of testing.

TE.040.2 Perform Integration Test

OVERVIEW

Perform the appropriate integration tests during the Construction phase (and Elaboration phase, if required). Test the components using the scenarios described in the Integration Test Scenarios (TE.035).

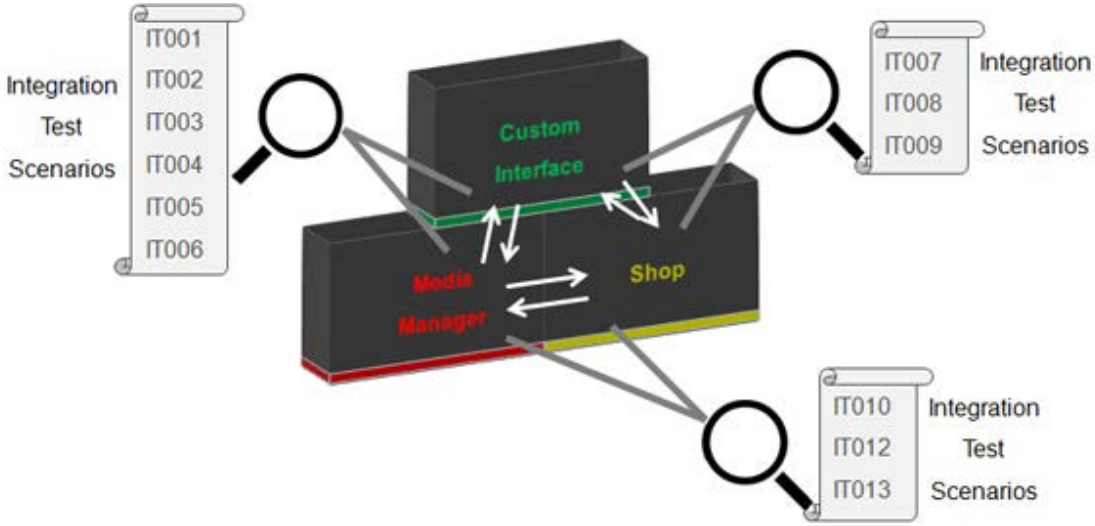

Back to Top

C.ACT.PST PREPARE FOR SYSTEM TEST GUIDANCE

MC.050.2 Define Application Setups

Overview

Review and refine the detailed setup values needed to configure the WebCenter product(s). Continually refine the work product during the implementation.

For WebCenter engagements, the resulting work product forms a shared central document for retaining and managing general configuration settings for the system. This prevents conflicting configuration across design documents.

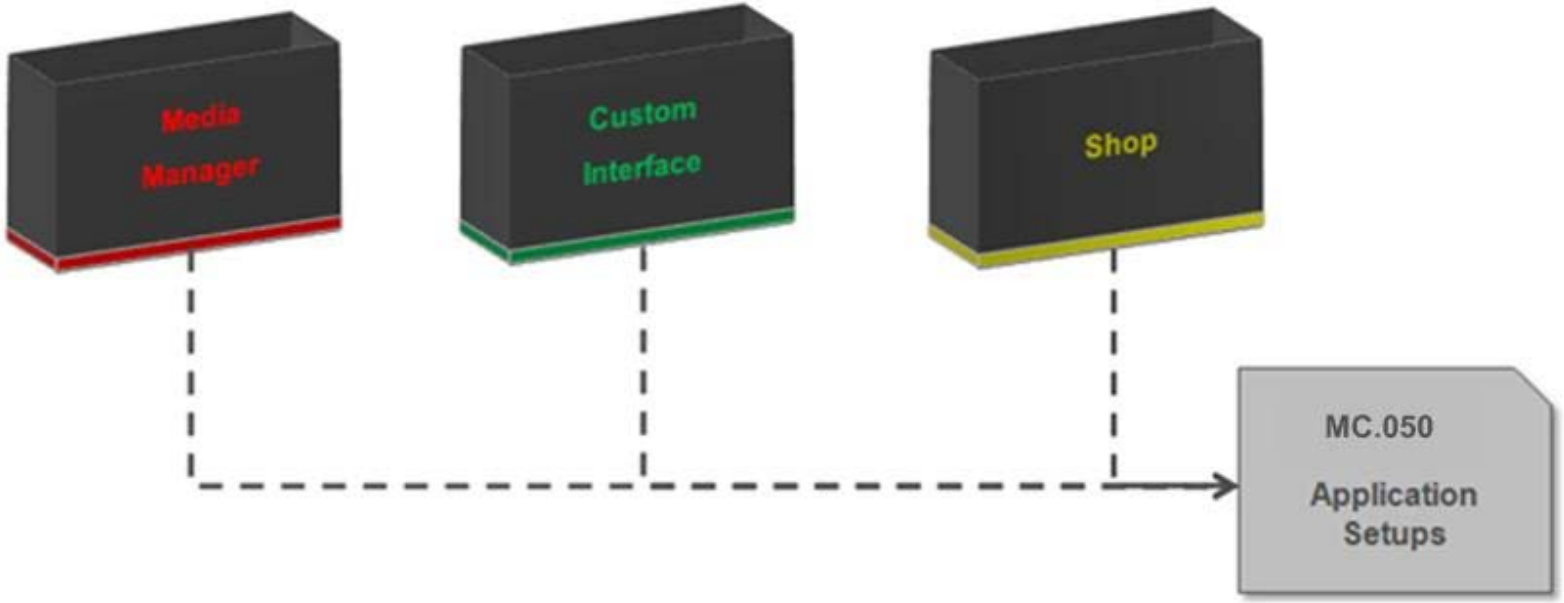

Back to Top

C.ACT.PSTC PERFORM SYSTEM TEST - CONSTRUCTION GUIDANCE

TE.070.2 Perform System Test

OVERVIEW

Perform the system test to test the operation and integration of all business system flows within the WebCenter system, including the integration of application extensions.

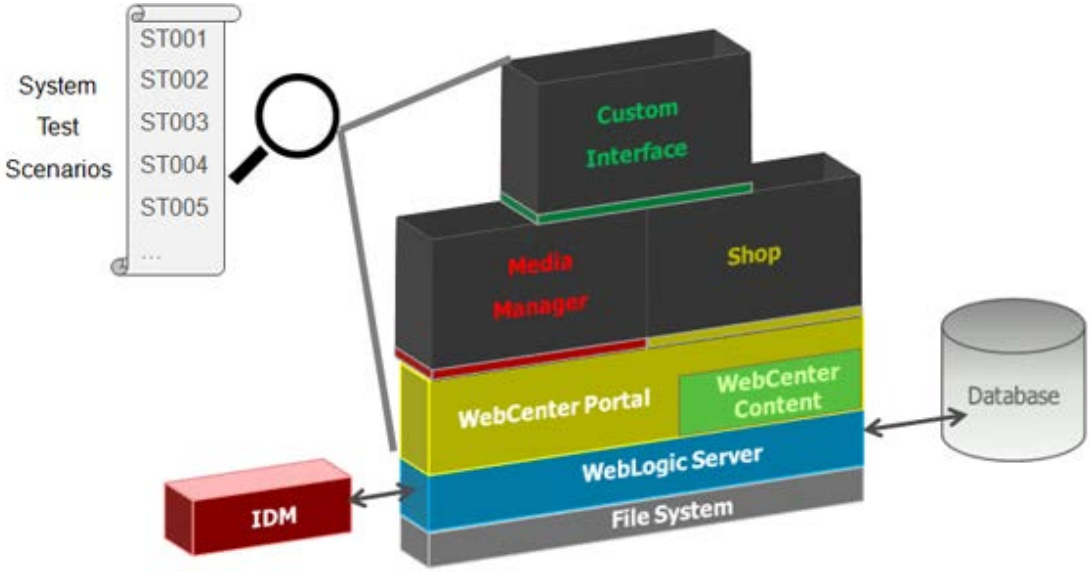

Back to Top

C.ACT.PSIT CONDUCT SYSTEMS INTEGRATION TEST GUIDANCE

TE.100 Perform Systems Integration Test

OVERVIEW

In a WebCenter project, this task validates the integration between the WebCenter system and other systems and verifies that the new system meets defined interface requirements and supports execution of business processes that cross system boundaries.

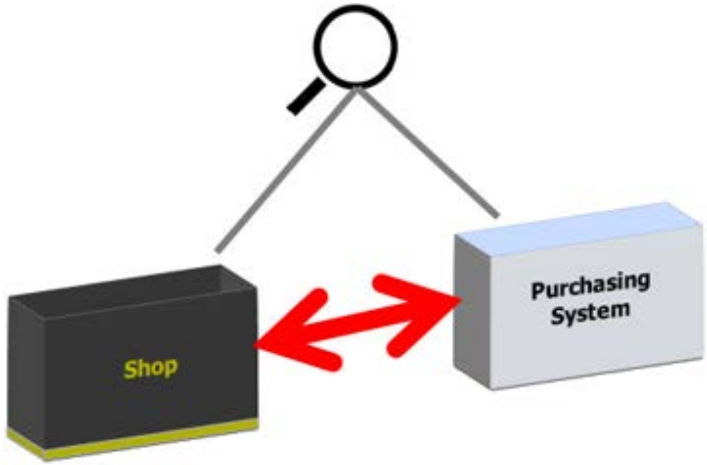

Back to Top

C.ACT.PT PREPARE FOR TRANSITION GUIDANCE

TA.150 Define Final Platform and Network Architecture

OVERVIEW

Define the physical platform and infrastructure that will be implemented to support your technical and application architecture. You map the physical application and database server architectures on to specific computing platforms.

This task updates the work done in the Initial Architecture and Application Mapping (TA.070), incorporating any changes, additions or enhancements that have occurred due to subsequent architecture design work. This task focuses on the future Production Environment and any supporting environments, such as training or production support.

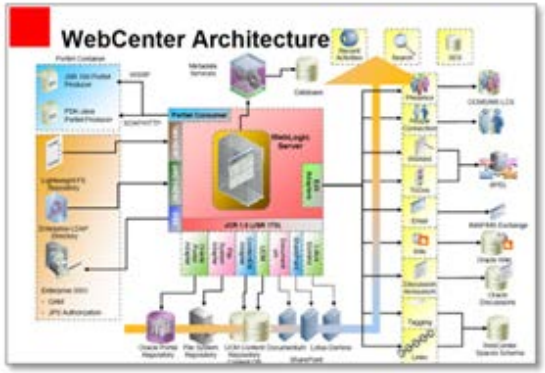

Back to Top

C.ACT.PCO PREPARE FOR CUTOVER GUIDANCE

TS.020.2 Define Cutover Strategy

OVERVIEW

State how the transition is to be made from the old system to the new system. Define your plans for taking the new system into Production. This task may need to be performed several times over the course of the project as you go from an initial Cutover Strategy to a final Cutover Strategy.

For projects that involve the upgrade of WebCenter products, this task is used to define the strategy that will be used during the cutover from the existing Production version to the new software release.

APPROACH

The following points should be taken into consideration:

- if parallel running is to be performed
- how systems being replaced are to be switched for the new system
- how interfaces between the new and current systems are to be run for the first time
- how the live data conversion is to be performed
- how training is being performed for the changeover

TS.030 Develop Installation Plan

OVERVIEW

Develop a general Installation Plan, applicable for the Production Environment as well as any other test or maintenance environments.

In a WebCenter implementation, you should also develop a detailed Transition Plan for moving onto the Production system, as well as an Implementation Contingency Plan.

APPROACH

Using the standard OUM template, complete the steps identified in the Method Pack.

WORK PRODUCT

- Introduction
- Work Products
- Assumptions
- Distributed Requirements
- System Requirements
- Software information
- Name / Location of Components, etc.
- Contingency Plan
- Initial Schedule

TS.040 Design Production Support Infrastructure

OVERVIEW

Identify the operational infrastructure for managing and maintaining the application environment, servers, and network infrastructure in Production.

WORK PRODUCT

The Production Support Infrastructure Design addresses the operational infrastructure for managing and maintaining the application environment, servers, and network infrastructure. It should address the following:

- Production Support Infrastructure Plan
  - Requirements
  - Personnel Learning Plan
  - Equipment and Materials
- Maintenance Procedures
  - Maintaining Metadata
  - Maintaining the Security Model
  - …
- External Support Procedures
  - Access Procedure for External Support, i.e., Oracle Support

- Internal Support Procedures, i.e., Customer Helpdesk
- User Support Levels
- Problem Identification Guide
- Production Cutover Notification to External Support

Back to Top

Copyright © 2006, 2016, Oracle and/or its affiliates. All rights reserved.

WEBCENTER SUPPLEMENTAL TASK GUIDELINES - TRANSITION PHASE

Back to View

This document contains OUM supplemental task guidance for WebCenter projects.

- The first column of the following table provides a complete list of all tasks in this document for which "supplemental" guidelines are provided as well as a quick link to the "supplemental" task guideline in this document.
- The second column provides a link to the OUM Task Overview.

The task guidelines in this document should be used to supplement the guidelines that appear in the OUM Task Overview.

WebCenter - OUM Supplemental Task Guidelines (this document) collapse table | expand table	OUM Task Overview
D.ACT.FD Finalize Documentation	
DO.110 Finalize Documentation	DO.110 Finalize Documentation
D.ACT.PPE Prepare Production Environment	
TS.050 Prepare Production Environment	TS.050 Prepare Production Environment
D.ACT.GP Go Production	
TS.052 Implement Production Support Infrastructure	TS.052 Implement Production Support Infrastructure
TS.058 Verify Production Readiness	TS.058 Verify Production Readiness
TS.060 Go Production	TS.060 Go Production

Back to Top

D.ACT.FD FINALIZE DOCUMENTATION GUIDANCE

DO.110 Finalize Documentation

OVERVIEW

During the Transition phase, minor revisions or changes to the software system may cause updates to any or all of the documentation work products. This task covers the incorporation of any of those changes into the Documentation work products.

Back to Top

D.ACT.PPE PREPARE PRODUCTION ENVIRONMENT

TS.050 Prepare Production Environment

OVERVIEW

This task addresses the installation and configuration of the database, WebCenter, and any custom extensions intended for Production use.

APPROACH

- Prepare Production Hardware:
  - Operating System
  - File Structures
  - Networking Software
- Prepare WebCenter (Installation and Configuration):
  - Database
  - WebLogic Server
  - IDM
  - WebCenter
  - WebCenter Extensions (including custom extensions)

Back to Top

D.ACT.GP GO PRODUCTION GUIDANCE

TS.052 Implement Production Support Infrastructure

OVERVIEW

Activate the support personnel and procedures for the new business system and review requirements for support-related services from software suppliers, contractors, help desks, and other support services.

APPROACH

The Production Support Infrastructure involves implementing the operational infrastructure documented in the Production Support Infrastructure Design (TS.040). It should address the following:

- handling of inquiry calls
- call and response tracking
- system direction for all types of audiences
- links to external support mechanisms or sources
- performance metrics information for support
- personnel (response, history retention, follow-up, accuracy, audit, etc.)
- backup resources and tools

TS.058 Verify Production Readiness

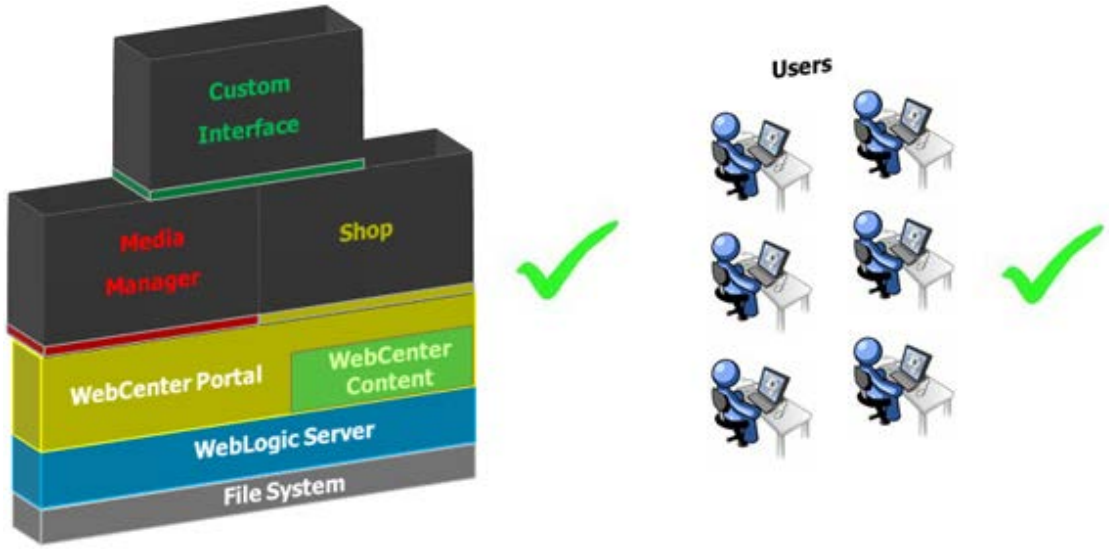

OVERVIEW

Formally verify that the organization's systems, host facilities, local area networks (LANs), wide area networks (WANS), and people are prepared for Production. This is the final approval step before the cutover to the new Production system.

TS.060 Go Production

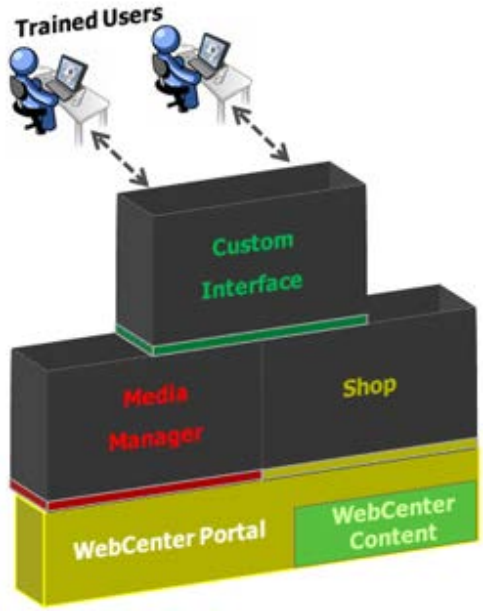

OVERVIEW

Take the new WebCenter system and put it into Production use. The new system is now part of the business and is being used to satisfy business needs.

APPROACH

- The System in Production (SIP) is used by trained users and supported by trained administrators.
- It replaces any legacy systems identified for replacement by the new WebCenter system.
- You have certified that all aspects of the system are operational.

Back to Top

ORACLE

Copyright © 2006, 2016, Oracle and/or its affiliates. All rights reserved.

WEBCENTER SUPPLEMENTAL TASK GUIDELINES - PRODUCTION PHASE

Back to View

This document contains OUM supplemental task guidance for WebCenter projects.

- The first column of the following table provides a complete list of all tasks in this document for which "supplemental" guidelines are provided as well as a quick link to the "supplemental" task guideline in this document.
- The second column provides a link to the OUM Task Overview.

The task guidelines in this document should be used to supplement the guidelines that appear in the OUM Task Overview.

WebCenter - OUM Supplemental Task Guidelines (this document) collapse table | expand table	OUM Task Overview
E.ACT MPSP Manage Production System Performance	
PT.120 Conduct Production Performance Management	PT.120 Conduct Production Performance Management
E.ACT.EPS Evaluate Production System	
PS.010 Audit System	PS.010 Audit System
E.ACT.RPP Resolve Production Problems	
PS.050 Analyze Problems	PS.050 Analyze Problems
PS.060 Monitor and Respond to System Problems	PS.060 Monitor and Respond to System Problems

Back to Top

E.ACT.MPSP MANAGE PRODUCTION SYSTEM PERFORMANCE GUIDANCE

PT.120 Conduct Production Performance Management

OVERVIEW

Implement the Performance Management activities to the Production Environment in conjunction with the implementation of the WebCenter system.

Monitoring, metric collection and review is an ongoing process. This may not be within the scope of your project or may covered by a group outside of the project team, after the system goes into production.

Back to Top

E.ACT.EPS EVALUATE PRODUCTION SYSTEM GUIDANCE

PS.010 Audit System

OVERVIEW

Request an independent quality auditor to review the WebCenter system. This task should be performed after cutover, when the WebCenter system has reached a steady state.

APPROACH

- Review objectives and top-level requirements.
- Review Security and Control Strategy.
- Review technical and system operational documentation.
- Examine the System in Production.

Back to Top

E.ACT.RPP RESOLVE PRODUCTION PROBLEMS GUIDANCE

PS.050 Analyze Problems

OVERVIEW

Analyze each open problem report from the Problem Log (PS.060) and determine which open problems represent faults in the WebCenter system. Determine the changes that are necessary to resolve the set of faults.

Perform this task in parallel with the task, Monitor and Respond to System Problems (PS.060), post Production, if this is within the scope of the project.

PS.060 Monitor and Respond to System Problems

OVERVIEW

Monitor and respond to problems and issues throughout the post-Production support period. It is recommended to also monitor Service Level Agreements (SLAs). This is an ongoing task that may not be full-time.

APPROACH

- Record and acknowledge problem reports from users and administrators.
- Compile and maintain the Problem Log.
- Monitor related SLAs.

Back to Top

Copyright © 2006, 2016, Oracle and/or its affiliates. All rights reserved.

WebCenter PROJECTS AND OUM

Back to View

HOW CAN OUM BE USED FOR WebCenter PROJECTS?

WebCenter project engagements require only a subset of the full list of tasks included within OUM. The WebCenter Supplemental Guide has been developed in order to provide technology-specific guidance for all WebCenter components. When using OUM on your project engagement, it is important to let the method serve you, that is, only select the appropriate tasks that you need.

In most cases, WebCenter project engagements align to the OUM Core Workflow focusing on the activities including the following processes:

- Business Requirements
- Requirements Analysis
- Analysis
- Design
- Implementation
- Testing

In some cases, it is necessary to include additional activities and tasks. For example, you would only require functional prototyping tasks (IM.070) if the project specifically requires such a prototype. The WebCenter Supplemental Activity Guidelines identifies such tasks as option (O) in order to help you identify such tasks. This guidance allows you to quickly and effectively identify the required tasks for your engagement.

Back to Top

WebCenter ACTIVITY CORE WORKFLOW

The WebCenter Activity Core Workflow has been created to identify the core activities within the Implement focus area that should be considered on WebCenter projects. This view should serve to accelerate the understanding of OUM for WebCenter by new practitioners and help to keep the project teams focused on these activities.

There may only be a subset of tasks that need to be performed for each activity when working on a WebCenter project. These tasks are identified in the associated Supplemental Task Guidelines for each phase.

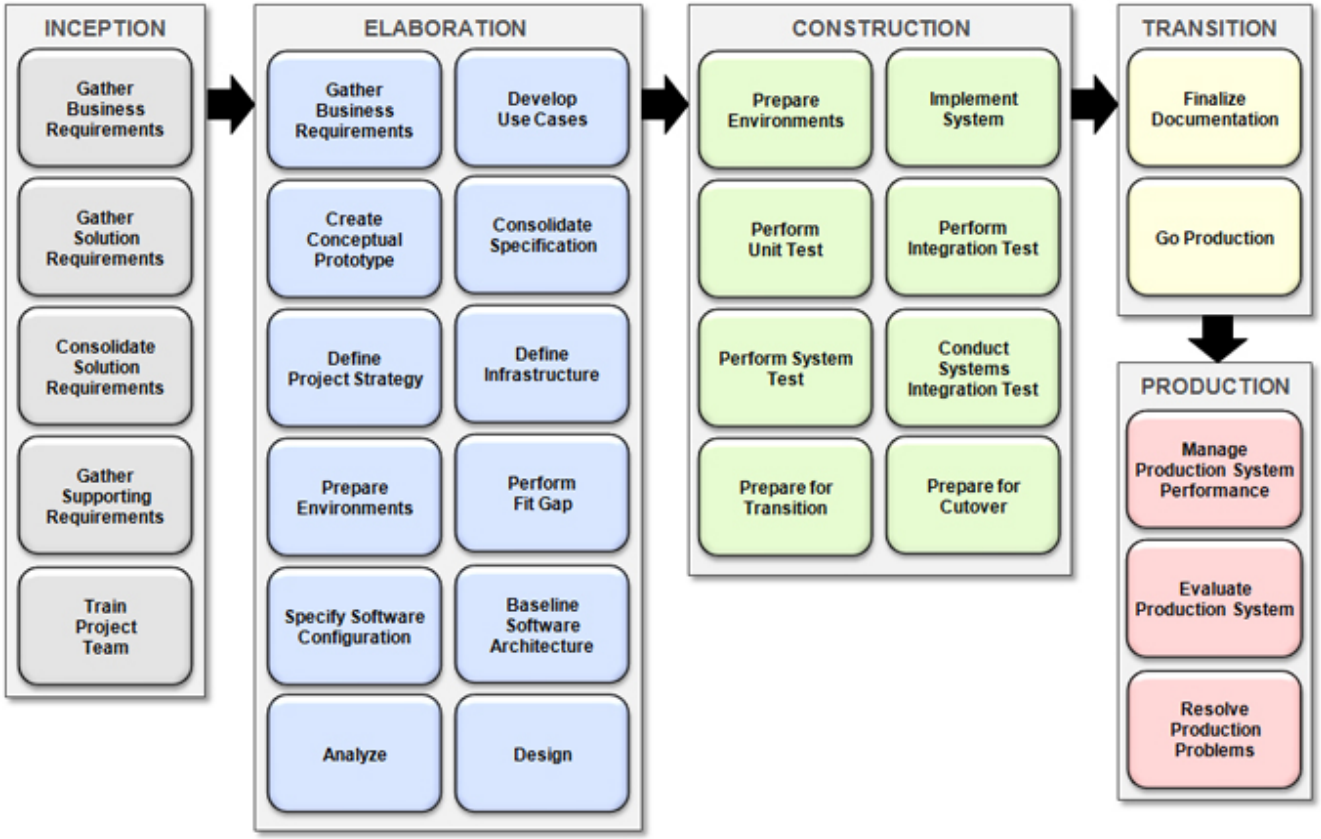

Back to Top

WHAT ARE USE CASES IN THE CONTEXT OF WebCenter?

Use cases identify and describe the possible sequences of interactions between the system and its actors, in relation to a specific goal. They describe the interaction between the primary actors, i.e., Consumers, Contributors, Administrators, and the system itself, i.e., Web sites, Portals, etc.

Use cases should be represented in simple sequences that will lead to the WebCenter solution. When writing a use case you must avoid using technical jargon and use the Actor as the audience. Use Cases describe the system from the Actors point of view. There are many possible system use cases for all WebCenter products. Some possible system use cases are listed below:

WebCenter Content

- Classify Using Metadata
- Apply Content Security
- Apply Content Versioning
- Search Content
- Notify by Email
- Expire Content

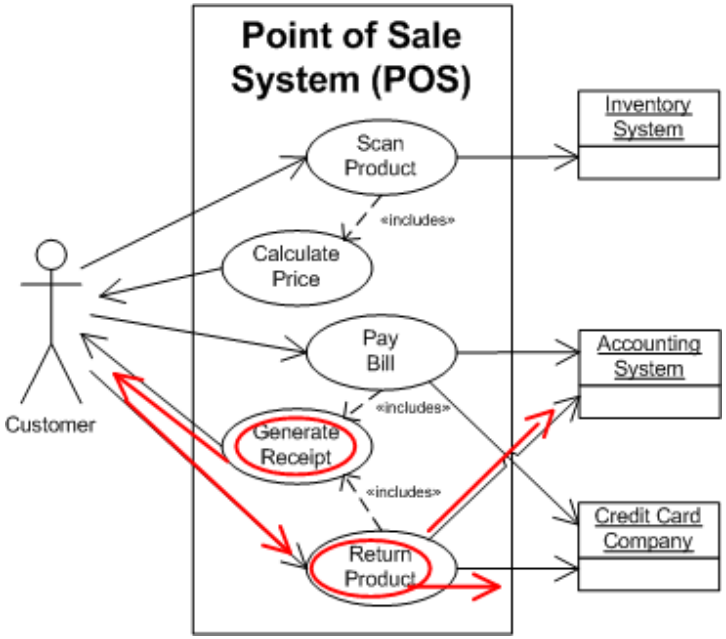

WebCenter Portal

- Login to Portal
- Search Portal
- Update Wiki
- Tag Content

Important OUM tasks for documenting use cases include:

- Prioritize Requirements (MoSCoW) (RD.045) – This task allows you to capture the project use cases / functional requirements for the project (in list form).
- Develop Use Case Model (RA.023) – In this task, the use cases and actors are refined into a consistent model creating a first-cut view of system scope.
- Develop Use Case Details (RA.024) – In this task, you define the details for each use case within the Use Case Model (RA.023).

Back to Top

WebCenter RELATED INFORMATION

Additional information about Oracle WebCenter can be found online:

External Websites

- Oracle.com
- Oracle Technology Network

Social Media

- LinkedIn - Oracle Social Enterprise group
- Facebook - Oracle WebCenter

Back to Top

Copyright © 2006, 2016, Oracle and/or its affiliates. All rights reserved.

DEFINITIONS AND TERMS

Back to View

A | B | C | D | E | F | G | H | I | J | K | L | M | N | O | P | Q | R | S | T | U | V | W | XYZ

Accessibility
Software is accessible when vision- and hearing-impaired users and others with handicaps can access the application using a screen reader or other Section 508-compliant tools.

Access Levels
When you create a security policy, you must select a default access level for it. A default access level is assigned to any Content DB member whom you do not explicitly add to the access list associated with a security policy. You create the access list for a security policy by granting or denying access to specific members, groups, or organizations. As part of this process, you must also select an access level for each member or group that you add to the access list.

Administrative Options
Administrative options allow a Content DB administrator to control global settings that affect the functionality of the Content DB Application for all users.

Administrator
A Content DB administrator is a user who is a member of an administrative group. Administrators can add new users and assign roles, and set global options.

Application Program Interface (API)
A traditional definition of the Application Program Interface (API) is that of an interface between the operating system and application programs. For example, an API may make it possible for programs that run under it to open windows and display message boxes. However, in the case of Content DB, the API gives access to all the functions in Content DB some of which are not currently exposed in the user interface. End users can develop applications to take advantage of the Content DB functionality. For additional information, please refer to the API User Manual.

Annotations
Functionality provided by third party partner viewers such as is provided by Informative Graphics that allow users to add markups to images or electronic documents, without changing the original document, with security controls limiting edit and view access right at the user level Examples of different types of annotations include redlining, comments, highlighting, and redaction.

Archive / Storage
Software that handles the utilization of the appropriate disk subsystem such as NetApp or EMC Centera based on the value and anticipated near-term need of the content.

Auto-Classification
Refers to the use of specialized software to automatically organize content according to its subject or context, based on rules or logic that help determine the proper classification. Partner products such as Kofax can auto-classify content during the scanning process with a combination of database indexes, that can also perform validating lookups and reading the content itself (OCR). The results are used to auto-classify the image into Content DB. Orchestria is a partner product that auto-classifies content using a method known a ‘meta-tagging’ using logic that ‘reads’ incoming content such as emails and extracts relevant information to index, classify and organize the content.

Audit Trail

A record of the changes made to content or user actions related to content. Examples including tracking who accessed content, when the content was changed, and the user, application, or workflow process that made the change. Often used for analyzing the processes within a working environment, or to trace activity on a particular asset for quality assurance or compliance purposes. Content and Records DB have extensive audit capability.

Authorization
Process of granting a user access permissions to create, edit, or delete content.

Author
The creator of a document is referred to as the author. The author has full access rights on the document.

Back to Top

B

Behaviour
A behaviour is the result of configuring the folder to present a default state and functions to users.

Briefcasing / Offline
Creating an editable, offline document collection set for remote use that can be synchronized back to the main repository. Not a feature currently supported by Content DB.

Browser
A browser is an application program that provides a way to look at and interact with all the information on the Web. Technically, a Web browser is a client program that uses the Hypertext Transfer Protocol (HTTP) to make requests of Web servers.

Business Process Management/BPEL
Technology that orchestrates and automates the execution of business processes that involve human and system interactions during which documents, information or tasks are passed from one participant to another for action, according to a set of procedural rules. The BPEL Process Automation technology includes a graphic design tools for mapping out a process definition (including its users, steps, rules, and conditions), and a process engine that executes the process.

Business Analytics
Within the ECM context, tools that provide data of the utilization, workflow, and process automation metadata and statistics, to enable analysis of efficiencies of the ECM tool and the processes it is enabling.

Back to Top

C

Caching
The automated process of staging or assembly of pages or content objects in advance of their required use normally onto a local server in order to improve performance in retrieval and presentation to users. Content DB does not support this feature.

Capture / Scanning
Third party technology that is provided by Partner products such as Kofax, for scanning and digitizing documents, recognizing key data on those documents, and preparing the images and data for import into Content DB. Capture also includes technology for ingesting content files (documents such as faxes, web content, records and email items). Capture also refers to the extraction of forms data from a form and metadata from content, for example, capturing the metadata properties from the Microsoft Office properties page or from within HTML page metatags.

Categories
Categories contain metadata about documents, and help organize documents added to a Content DB library. Each category can contain any combination of documents and subcategories, providing users with the flexibility to group information in a variety of ways. Users can link or add the same document to multiple categories. In addition, they can regroup documents by unlinking or removing them from a category. To organize documents users must create document folders that contain files. Document folders can also be categorized and provide a method to organize documents that rely on a traditional folder hierarchy.

Check-In and Check-Out
Functionality that allows a user to access a document in a repository and lock other users out of that document while the user is making modifications or changes; checking the document back in to the repository removes the lock and also may invoke the creation of a new version.

Classification
The method and process of organizing content according to its subject or context.

COLD/ERM (Computer Output to Laser Disk / Enterprise Report Management)
A third party application such as Xenos that allows the transfer or migration of data such as computer generated reports from disparate legacy systems into a single Oracle Content DB and Records DB repository in order to repurpose the legacy data into a usable, easily accessed format that can be mined for information or presented on the Web for end-user / customer self-service.

Collaboration
Defined as a working practice whereby individuals work together to a common purpose to achieve business benefit. Collaboration tools such as Collaboration Suite, often through the implementation of team “workspaces,” facilitate discussion through forums and discussion threads, joint development and review of content, faster completion of tasks, and process visibility. Collaboration Suite also includes messaging, persistent chat, and presence notifications. Collaboration Suite is typically needed, by end-users who control content access, as opposed to a centrally-coordinated and constrained environment.

Component
Components are information objects, self-contained information that, when compiled with other components, make up a document. They provide their own context. Components can be created with many different tools, including Microsoft Word, Excel, or PowerPoint, and can be designed in any number of different formats. The defining characteristic of a component is not its format, but its scope, or level of granularity that allows it to be reused in creating many different documents. The method of storing components is often referred to as Compound Document Management and Content DB does not at this time support this approach.

Content Integration
The ability for disparate content (unstructured) systems to integrate with each other using a common architecture or approach such as SOA. Also allows for structured content (meta data) systems such as e-Business to communicate with content systems.

Content Management
see ENTERPRISE CONTENT MANAGEMENT.

Container
An Oracle DB virtual folder object that forms part of a structural element that can only have an administrative role assigned and can only contain a library or another container.

Customized Templates
Customized templates are normally designed to meet the needs of vertical market solutions to save time by pre-populating libraries with a meaningful taxonomy, common documents, and other frequently used items without sacrificing the flexibility to respond to changing work scenario’s.

Back to Top

D

Destination Document
The document in which a linked or embedded object is inserted using Microsoft object linking and embedding (OLE). The document that contains the information used to create the linked or embedded object is the source document. When you edit a destination document, the information in the source document is not updated.

Digital Asset Management (DAM)
A third party application that provides a repository for the storage and retrieval of digital assets such as images, graphics, audio, and video. Content DB can act as the storage location for all content types however the unique dynamic rendering, management and re-purposing of digital assets is only provided through a partner application such as Sealed Media (Stellent) and Media Bin (Interwoven).

Digital Rights Management (DRM/e-DRM)
A system for protecting the copyrights of data circulated via the Internet by enabling secure distribution and/or disabling illegal distribution of the data. Typically, a DRM system protects intellectual property either by encrypting the data so that it can only be accessed by authorized users or by marking the content with a digital watermark or similar method so that the content can not be freely distributed.

Digital Signature
The digital equivalent of affixing a person’s signature to a piece of paper, indicating authorship or approval.

Directory Services

A terminology normally used by Microsoft to describe a LDAP style directory that assists in finding the location of objects, such as documents, users, metadata synonyms, etc., in a computer system. For the Microsoft version of Content DB the integration is done using the OID (Oracle Internet Directory).

Disposition Schedule
The lifecycle of a record includes a point at which it is either archived permanently or disposed of. The disposition schedule defines the timeline and procedure to be used leading up to a documents destruction. Multiple steps can occur prior to a documents final destruction which are all supported by Records DB. These include 'retain', 'move' to another location or folder, 'destroy' the document and meta-data, and trigger a 'workflow' action or step.

Document
Documents are information objects designed to be stand-alone, self-contained, and complete. Documents are not dependent on other content for their meaning to be understood. They provide their own complete context. Documents can be created with many different tools, including Microsoft Word, Excel, or PowerPoint, and designed in any number of different formats. The defining characteristic of a document is not its format, but the way it organizes information. Examples of documents might include formal reports and manuals. A document is well suited to creation by a single or multiple authors, material that is well established, material that is likely to have a long shelf life and to be of interest to a wider audience. Documents are typically written with a wider audience and a longer timeframe in mind.

Document Folders
Document folders can contain any combination of documents and subfolders, providing the flexibility to group documents in a variety of ways. Each document folder and subfolder can be assigned a unique security policy, allowing controlled access to its contents.

Document History
A document history panel lists operations that have been performed on the document according to user, date, version, and other customizable criteria. see AUDIT TRAIL.

Document Profile / Document Index
A document profile or index is a record of document-specific metadata that is entered by a user who imports a document to a Content DB library. Metadata fields can be used as search criteria in document searches. Document profiles can be created or modified by a Content DB administrator.

Document Management/Electronic Document Management (DM/EDM)
The computerized capture, indexing, search, and lifecycle management of electronic documents (such as Microsoft Office documents) into the Content DB repository. Usually used to manage electronic documents that may need to undergo revisions or that may have multiple versions associated with them as they are used in a business process. Management of component (compound) documents is a mandatory requirement (not supported by Content DB at this time). The Content DB Application allows documents to be organized and manipulated in a wide variety of document formats. Common functions include:

- Organize documents in customized document folders and categories
- Assign additional custom metadata to documents
- Share documents with users by assigning the appropriate security policy to the document
- Track document history and versions
- Delete obsolete documents
- Create document reviews

Desktop Applications
The "thick-client", content-centric applications to enable users to create, search, view, and update content and metadata. Content DB provides this capability through an approach known as the 'Oracle Drive' or 'O Drive', which integrates with, for example, Microsoft Word and Windows Explorer (via WebDAV).

Download Document
In the Content DB system, downloading means exporting a file to a directory outside the Content DB repository.

Back to Top

E

E-Forms
Online form generation tool such as Adobe Forms that automates and collects, stores, and distributes information, usually with the objective of avoiding redundant manual data input processes. Usually simpler than building a full-blown business application. E-Forms are typically used as part of a repetitive business process in conjunction with BPEL or another third party business process tool to manage the workflow.

Email Management
The ability to capture and store individual users' e-mail messages (and attachments) as official records, and to retrieve, retain, or dispose of them based on business rules, filters, and

corporate policy.

Embedded Object
All or a portion of a Word document, Excel spreadsheet, or Power Point slide can be pasted into a destination document as an embedded object using Microsoft object linking and embedding (OLE). Embedded objects become part of the destination document and, once inserted, have no connection to the source file. Double-click the embedded object to open it in its native application.

Enterprise Content Management (ECM)/Enterprise Content Services (ECS)
A set of technologies that help manage and control how enterprises create, capture, track, organize, store and publish an organization's unstructured content. Such technologies bring increased control over content while making it easier for users to find and retrieve the right content in the right format at the right time. The technologies are usually presented as a series of solutions or applications (ECM) and as a range of services (ECS) exposed through an API (see API). Examples of functional categories that fall under the ECM umbrella include capture, document management, imaging, digital asset management, records management, web content management, and portal technology. Oracle Content DB along with third party partners provides a partial set of ECM applications and services.

Error Handling
Error handling generally involves catching and either recovering from or throwing an exception to be caught by the invoking object.

Event Handler
An event in Content DB is a programmable function whereby an automated event is triggered as the result of a specific action occurring. For example a workflow event is triggered when a new document is added to a folder.

Extranets
Extranets are a system of semi-private Web pages and shared files. An example of this would be a partner-download site where current customers can go to download the latest documentation and patches; however, someone simply surfing the Internet would not be able to access the site. Extranets are commonly hosted outside the firewall.

Back to Top

F

File Plan
A file plan is part of Records DB and contains the rules that determine how long a document is to be retained for (the retention schedule) and the process that should be followed until its destruction (the disposition schedule). Multiple file plans can exist in the Records DB configuration and once a document is declared as a record it will inherit a file plan.

Full-Text Search
Content DB searches support searching the full text of documents as well as the document profile fields for specified text strings.

Back to Top

G

Group
A group is a list of users who are defined as a collective for the purpose of assigning identical access privileges to all members. Groups can be composed of internal or external users. Only members of administrative groups can perform administration tasks such as adding users and modifying templates.

Back to Top

H

HTML
HTML, or Hypertext Mark-up Language, is the language used to create pages for the World Wide Web. You can use HTML to create hyperlinks as well as the text formatting. To view HTML, you will need a browser.

HTML Connectors
HTML Connectors support custom parameters that can be inserted into the HTML during page generation. The parameters can be defined for both administrative and per instance usage.

HTML Connectors Worklets

HTML Connector Worklets are Java classes that generate HTML for HTML Connectors.

Back to Top

I

Imaging
Ability to capture, index, manage, store, and display document images. Usually refers to the digitization of paper documents, and the indexing and import of those images into a managed repository for use in business processes or for archival.

Index
Profile data that describes a document. see METADATA, AUTO-CLASSIFICATION and DOCUMENT PROFILE.

Import Document
Uploading a file to a Content DB library. For example, a user can import documents to a folder on a Content DB page. When a file is imported, the user enters metadata on a document profile form.

Instant Messaging
Instant Messaging is part of Collaboration Suite and is an on-line conversation that takes place between just two people.

Intranets
Intranets are a company's internal Web facilities. Intranets are hosted behind a firewall and are used only by a company's employees.

Back to Top

J

JAMES (Java Apache Mail Engine Server)
JAMES is a 100% pure Java SMTP, POP3 Mail server, and NNTP News server designed to be a complete and portable enterprise-mail-engine solution based on currently available open protocols. JAMES is also a mail-application platform. The JAMES project hosts the Apache Mailet API and provides an implementation of this mail application platform API.

JAMES is based upon the Apache Avalon application framework. (For more information about Avalon, please go to http://jakarta.apache.org/avalon).

Java Authentication and Authorization Service (JAAS)
JAAS can be thought of as having two different parts: authentication and authorization. Authentication refers to an identity check (exactly like a login screen that asks for a name and password) while authorization refers to what an authenticated user can or cannot do (similar to the concept of access control).

Back to Top

K

Knowledge Management
Knowledge Management is the formal process of attempting to capture and manage a business's intellectual property or assets. Generally, knowledge management involves collaboration across an organization to organize information assets.

Back to Top

L

LDAP (Lightweight Directory Access Protocol)
Lightweight Directory Access Protocol, or LDAP, is an open Internet standard. LDAP defines four basic models, which include an information model, a naming model, a functional model, and a security model. LDAP aims to make it possible for almost any application running on virtually any computer platform to obtain directory information, such as e-mail addresses and Public Keys. Because LDAP is an open protocol, applications need not worry about the type of server hosting the directory.

Library

A library is a Content DB folder that acts as a workspace that can contain folders and documents. Administrator defined access control roles such as creator and consumer can be assigned at this level.

Library Manager
An administration role that enables the user to assign rights to users and is able to define the configuration of the library and the workflow routing schema.

Link Document
A document that is stored in a Content DB library can be added to a folder on a Content DB page using the Link command on the folder's Action menu. The link that appears in the folder is a reference to the document.

Link Types
Content DB allows a user to select a specific type for a link that is added to a link's list, for example, a Content DB page, a URL to a Web site, or an email.

Linked Object
All or a portion of a Word document, Excel spreadsheet, or Power Point slide can be inserted into a source document as a linked object using Microsoft object linking and embedding (OLE). Linked data is stored in the source document. The destination file displays a representation of the linked data or an icon link, and stores the location of the source document.

Back to Top

M

Metadata
Metadata is data about data, the background information that helps users or search engines search for documents more effectively. Having more metadata enables users to search more effectively for and find specific documents. Metadata can include data about a particular document's contents or structure. Metadata has the ability to make use of time stamps, tags, or user keywords defined by the document's creator.

Back to Top

N

Native Connectors
Native Connectors expose the full internal functionality of the application and can do virtually anything the Content DB Application supports. They use the same native interfaces as the built-in items. Native Connectors can provide access to external data sources complete with custom property pages and views. They can also add functionality to existing Content DB objects. This type of connector requires extensive Java programming knowledge and requires XML knowledge for the development of page layouts.

Notification Engine
The concept of a notification engine supports various types of notification to enhance collaboration. The engine sends reminder-based and event-based notifications in the form of emails or messages and supports both system-defined and application-defined events. Additionally, the Notification Engine provides support for immediate or delayed delivery of server-side rules when an event is triggered. This feature is not currently provided in Content DB however could be considered as part of a consulting engagement.

Back to Top

O

Objects
Grady Booch describes objects as having state, behavior, and identity. What this means is that objects can have internal data and methods. Objects are also unique, meaning that they can be distinguished from other objects. Generally, an object is any item that can be individually selected and manipulated. This can include shapes and pictures that appear on a display screen as well as less tangible entities. In object-oriented programming, for example, an object is a self-contained entity that consists of both and manipulates data.

OLE
OLE (Object Linking and Embedding) is a framework for creating and manipulating compound documents. Content DB supports the embedding and linking of Word, Excel, and Power Point documents in a container document.

Operator / User
The operator or user of a document is the user to whom the document is currently checked out or with whom it is in use.

Operators / Query
To construct a query based on more than one term, operators must be inserted between the terms. Operators are codes that represent logic applied to a search. For example, Boolean operators such as AND, OR, NOT (or AND NOT), and NEAR are used to work with True/False values.

Owner
The creator of a Content DB content is referred to as the owner. The owner has full access rights to the page or page item.

Back to Top

P

Portable Document Format (PDF)
An Adobe Systems file format to which documents in nearly any format can be converted, retaining the fidelity of the original document. PDF makes it possible for formatted documents to appear on the recipient's monitor or printer as intended, irrespective of the user's operating system or output device used.

Portal
A browser-based gateway to a variety of content resources, repositories, and applications. Historically used in the context of Internet content sharing (i.e. web portals), but more increasingly used to describe a means of delivering enterprise wide content to internal users, i.e. become the de facto user interface for content consumers.

Process Automation / BPEL
Technology that manages and automates the execution of business processes that involve human and system interactions. The Oracle process automation tool is based on BPEL, which can be fully integrated with Content DB and includes design tools for mapping out a process definition (including its users, steps, rules, and conditions), and a process engine that executes the process.

Privilege
Privileges govern the actions that can be taken by a trustee. Privileges can govern library-level document folder-level and document-level actions and can be granted or revoked through the Privilege-setting properties. Privilege is not to be used as a synonym for permissions or rights.

Profile
Index data that describes a document (see Metadata). Also the act of indexing a document, most often via entry in an e-form.

Publish Document
When a document is published, it is full-text indexed and stored in a Content DB repository.

Back to Top

Q

Back to Top

R

Realm
A realm is a storage location in the OID (Oracle Internet Directory) where users and groups are located. Multiple realms can be supported based on an organizations logical groupings. Content DB uses the OID realm to connect the Site to the users and groups in the realm. Realms are used as high level method of access control that separates users from discrete Content DB Sites.

Records Management
The management of records to meet business, compliance, audit, and accountability requirements. Records DB provides the ability to define a classification plan and retention schedule for business records (which can include documents, e-mail, and other file types), and to apply retention and disposition rules to those records in accordance with the organization's records management policies and procedures. At this time Records DB does not include the management of paper records. Typically electronic records management systems are expected to comply with records management standards such as the Department of Defense (DoD) 5015.2. At this time Records DB is undergoing the process to comply with this standard.

Record Series
A record series is a 'virtual folder' with the purpose of containing multiple categories of record types. see RECORD CATEGORY.

Record Category
A record category contains meta-data attributes, security rights, the lifecycle rules and a destruction or disposition schedule for a collection of records. Multiple record categories would be managed as a record series.

Rendition / Rendering
The act of converting or “rendering” content in one format to another format (e.g. rendering a Microsoft Word document content as PDF), each separate, yet maintain a cross-reference link to maintain their existence as the “same” version.

Repository
A collection or library of documents or content, along with any metadata that describes the content and allows users to locate content. The Content DB repository uniquely uses the Oracle relational database to manage the metadata, unstructured content, and user access to the content.

Review and Approval
A specific set of workflow and collaboration tasks which makes the review of new and revised content easier and more efficient. Occasionally may utilize email, but more often an application environment specifically suited. Content DB currently includes Oracle Workflow (separate to BPEL) as a lightweight workflow engine built into Content DB for this purpose.

Roles
Roles are a pre-configured collection of permissions that are normally linked to users and groups. Content DB has a set of standard roles and hidden roles that are provided out of the box however an unlimited number of roles can be customized.

Back to Top

S

Search
Technology that allows users to submit queries to a repository, to receive a “hit list” of relevant content to which they have rights, and to retrieve the individual content objects. Content DB provides both fielded searching (to locate content based on metadata field values or ranges) as well as full-text searching (to locate content based on specific words that may exist within the content). By using Secure Enterprise Search (SES) as a separate component for advanced federated search – that is, searching across multiple repositories this is over-and-above the core functionality.

Search Folder
A Search Folder contains a list of links to documents that have been returned in a Content DB search.

Search Profile Index
A search profile is a list of document-specific fields that can be used as search criteria when performing a document search. In Content DB, search profiles contain all the search criteria and the results list filters documents based on the permissions and access controls assigned to the user.

Security
1. Technology that provides authorization and access to content for users and systems. Content DB does not install with pre-defined security policies however does include pre-defined roles that can be used as templates for defined access control for users. 2. In Content DB, security refers to methods and policies that enable authorized users to access content while unauthorized users are denied access. Security can exist on the network level (user authentication), the user or group level (roles), or the page, folder, or document level (access levels).

Security Policies
Security policies allow users to manage user access to content objects.

Server Cluster
The server cluster such as RAC can be described as a group of servers running Content DB services. The server cluster itself makes up the core entity of the server configuration. The middle tier can be separated and run on it’s own cluster.

Session Timeout Interval
The Session Timeout parameter determines how long a Content DB user can be inactive before being logged out by the system. This feature provides protection when users leave their workstation during a Content DB session.

Site
This is the top tier of a Content DB configuration. A site can contain one or many containers and/or libraries. Multiple sites can be supported however they require multiple realms in the OID (Oracle Internet Directory/LDAP Server) – see realms.

Source Document
This is the document that contains the information used to create a linked or embedded object using Microsoft object linking and embedding (OLE). When the source document is updated, the information in the linked object in the destination document can be automatically updated.

Start Page
The start page is the first Content DB page the user sees after login.

Structured Document
A collection of data items with implicit semantic relationships between the elements based on their organization. Simply, information that resides in fixed fields within a record or file, managed in the Oracle database.

Subfolder
A subfolder is a document folder that is contained within another folder. Multiple subfolders can be added to create a folder hierarchy for organizing documents on a Content DB page.

Syndication
The supply of content from a variety of sources, usually via a paid service subscription for reuse and integration with other content. A new functionality in some ECM tools, allowing users to subscribe to folders and change events, which is not currently provided in the core Content DB application.

Back to Top

T

Taxonomy
Taxonomy is the study of the general principles of scientific classification. This word is most commonly associated with biological or horticultural classifications according to natural relationships; however, it is also used in reference to technology to a hierarchical breakdown of information. Taxonomies help users organize content, navigate to specific content objects within the repository, and search for content. A good taxonomy enables the same content to be located and accessed via multiple paths.

Thesaurus
The ability to define synonym terms and other relationships, such as related or narrower terms for words, such that, either with the instantiated metadata for a given piece of content, or for a search term, the users likelihood of categorizing correctly and finding the desired content increases since the system provides synonym terms via a thesaurus capability.

Tomcat
Tomcat is the servlet container that is used in the official Reference Implementation for the Java Servlet and Java Server Pages technologies. The Java Servlet and Java Server Pages specifications are developed by Sun under the Java Community Process. Tomcat is developed in an open and participatory environment and released under the Apache Software License. For additional information about Tomcat, please refer to http://jakarta.apache.org/tomcat/index.html.

Trusted Logon / Single Signon
Defined as a logical relationship established between domains to allow pass-through authentication, in which a trusting domain honors the logon authentications of a trusted domain. User accounts and global groups defined in a trusted domain can be given rights and permissions in a trusting domain, even though the user accounts or groups don't exist in the trusting domain's directory. With regards to Content DB, a single signon is a trusted logon that is authenticated via the Content DB Server but through some third-party authentication system (SSO Server).

Back to Top

U

Unstructured Data
Data that does not reside in a fixed database or field. Examples of unstructured data include word processing files, spreadsheets, images, graphics, and web content.

User-Defined Security Policies
Content DB allows users to have security rights to content objects based on their role that contains a set of permissions such as create, delete or modify objects. This is part of a project definition and not provided out of the box.

User Profile
A user profile is a set of preferences that contains settings for default features that each user has as their working environment in Content DB. User default profile information can be configured only by a Content DB administrator however users can change their personal settings.

Back to Top

V

Version Control
Functionality that allows users to edit a document, retaining both the previous and the new versions, with an explicit version assignment. Content DB currently only maintains a major versioning scheme with no minor versioning scheme. In competing systems versioning can become quite complex with component documents where each component (e.g. chapter) has a unique version, and the collection of the components (e.g. full report) has its own assigned version.

View
Views determine how pages, folders, and searches display document information. Each document or search folder on a Content DB page has a customizable view that by default is presented in the documents host application. Third party viewers, supplied by Oracle partners such as Informative Graphics allows several hundred document formats to be viewed in a generic viewer that is not dependent on the the presence of a documents host application.

Back to Top

W

Web-based Distributed Authoring and Versioning (WebDAV)
A set of extensions to the HTTP protocol that allow users to create, edit, and move content on remote, often web servers.

Web Page
A web page, in contrast to a document, is not self-contained and relies on the context (navigation) of the web site it belongs to and the web as a whole. When a web page “wants” to refer to another piece of information, it links to it rather than copying and including it. This makes the reuse problem easy, but creates consistency and navigation problems.

Web Conferencing
Web Conferencing refers to the use of Web applications to allow people in different locations to view some type of presentation simultaneously. Web conferences focus on showcasing an event rather than the people participating in the event.

Web Content Management (WCM)
Provides a set of procedures for managing content from it’s creation throughout it’s lifecycle that is destined for publication to the Web. Content management across an enterprise also includes software-code management, integration with other enterprise systems, and the organization’s Web content.

Wizard
This is a series of dialogs that prompts the user to provide information necessary to complete a process. An example of this is the New Page Wizard.

Workflow / BPEL
Workflow is a term used to describe the tasks, procedural steps, organizations or people involved, required input and output information, and tools needed for each step in a business process. Oracle Workflow/BPEL includes design tools for mapping out a workflow or process definition (including its users, steps, rules, and conditions), and a workflow engine that executes the workflow. Oracle workflow manages both document-centric business processes with managing the document status during the process and includes advanced features and capabilities for controlling processes that require performing outside of Content DB.

Back to Top

XYZ

eXtensible Markup Language (XML)
A standard language that enables the exchange of the content and format of documents among systems. It is extensible because designers can easily generate new definitions and schema understood by other systems. XML is increasingly changing the view of ECM systems managing “unstructured” content as XML, by definition, can provide structure to content files.

XSL
Extensible Style Language (XSL) is a style-sheet standard currently in development. XSL is similar to HTML in that it uses cascading style sheets to change document into formatted objects that are then presented via some type of media.

Back to Top

Copyright © 2006, 2016, Oracle and/or its affiliates. All rights reserved.
