ORACLE UNIFIED METHOD

CLOUD APPLICATION SERVICES OUM SOLUTION DELIVERY GUIDE

Release 3.3.1
September 2016

ORACLE

Cloud Application Services OUM Solution Delivery Guide, Release 3.3.1

Copyright © 2012, 2016, Oracle and/or its affiliates. All rights reserved. This document is provided for information purposes only, and the contents hereof are subject to change without notice. This document is not warranted to be error-free, nor subject to any other warranties or conditions, whether expressed orally or implied in law, including implied warranties and conditions of merchantability or fitness for a particular purpose. We specifically disclaim any liability with respect to this document, and no contractual obligations are formed either directly or indirectly by this document. This document may not be reproduced or transmitted in any form or by any means, electronic or mechanical, for any purpose, without our prior written permission. Oracle and Java are registered trademarks of Oracle and/or its affiliates. Other names may be trademarks of their respective owners.

Authors: Oracle's Global Methods Team

CONTENTS

CHAPTER *1* **Introduction 1-1**

What is the Cloud Application Services OUM Approach? 1-2

How to Use This Guide 1-3

Contributors 1-3
Your Feedback is Requested 1-3

CHAPTER *2* **Approach Overview 2-1**

Scope 2-2

Objectives 2-3

Approach Overview 2-4

Core and Optional Tasks 2-6

Core and Optional Tasks in the CAS OUM Approach 2-6
Task Selection Guidelines 2-6

Important Concepts 2-9

Cloud Environment Provisioning 2-9
Environment Management and Usage 2-9
Project Management 2-10

CHAPTER *3* **Project Design (A) Phase 3-1**

Project Design Phase Objectives 3-2

PSU.RCSWB – Review Contract, Scope, Workplan and Budget (Core) 3-6

Activity/Task Group 3-6
Work Product 3-6
Prerequisites 3-6
Approach 3-7
Roles and Responsibilities 3-7

PSU.RPAC – Review Project Approach with Customer and Confirm Customer Readiness (Core) 3-8

Activity/Task Group 3-8
Work Product 3-8
Prerequisites 3-8
Approach 3-8
Roles and Responsibilities 3-9

PSU.EGSI – Establish Governance and Supporting Infrastructure (Core) 3-10

Activity/Task Group 3-10
Work Product 3-10
Prerequisites 3-10
Approach 3-10
Roles and Responsibilities 3-11

STM.050 – Conduct Customer Kickoff Meeting (Core) 3-12

Work Product 3-12
Activity/Task Group 3-12
Prerequisites 3-12
Approach 3-12
Roles and Responsibilities 3-12

TR.050 – Train Project Team (Optional) 3-13

Activity/Task Group 3-13
Work Product 3-13
Prerequisites 3-13
Approach 3-13
Roles and Responsibilities 3-13

WM.070 – Schedule Workshops (Core) 3-14

Activity/Task Group 3-14
Work Product 3-14
Prerequisites 3-14
Approach 3-14
Roles and Responsibilities 3-14

MC.040 – Conduct Functional Design Workshops (Core) 3-15

Activity/Task Group 3-15
Work Product 3-15
Prerequisites 3-15
Approach 3-15
Roles and Responsibilities 3-16

DS.145 – Conduct Technical Design Workshops (Optional) 3-17

Activity/Task Group 3-17
Work Product 3-17
Prerequisites 3-17
Approach 3-17
Roles and Responsibilities 3-18

DS.160 – Conduct Design Reviews (Core) 3-19

Activity/Task Group 3-19
Work Product 3-19
Prerequisites 3-19
Approach 3-19
Roles and Responsibilities 3-19

MC.060 – Develop Security Strategy and Plan (Core) 3-20

Activity/Task Group 3-20
Work Product 3-20
Prerequisites 3-20
Approach 3-20
Roles and Responsibilities 3-20

TE.010 – Define Validation Strategy and Plan (Core) 3-21

Activity/Task Group 3-21
Work Product 3-21
Prerequisites 3-21
Approach 3-21
Roles and Responsibilities 3-21

DO.010 – Define Documentation Requirements and Strategy (Optional) 3-22

Activity/Task Group 3-22
Work Product 3-22
Prerequisites 3-22
Approach 3-22
Roles and Responsibilities 3-22

TA.010 – Conduct Technical Readiness Assessment Kickoff Meeting (Optional) 3-23

Activity/Task Group 3-23
Work Product 3-23
Prerequisites 3-23
Approach 3-23
Roles and Responsibilities 3-23

WM.055.1 – Conduct Implementation Checkpoint (Core) 3-24

Activity/Task Group 3-24
Work Product 3-24
Prerequisites 3-24
Approach 3-24
Roles and Responsibilities 3-24

PEC.MPE.1 – Manage Project Execution (Core) 3-25

Activity/Task Group 3-25
Work Product 3-25
Prerequisites 3-25
Approach 3-25
Roles and Responsibilities 3-26

CHAPTER *4* **Configure (B) Phase 4-1**

Configure Phase Objectives 4-2

MC.070.1 –Setup Applications (Core) 4-7

Activity/Task Group 4-7
Work Product 4-7
Prerequisites 4-7
Approach 4-7
Roles and Responsibilities 4-7

TE.025 – Prepare Validation Scripts (Core) 4-8

Activity/Task Group 4-8
Work Product 4-8
Prerequisites 4-8
Approach 4-8
Roles and Responsibilities 4-8

MC.080 – Conduct Configuration Validation Workshops (Core) 4-9
Activity/Task Group 4-9
Work Product 4-9
Prerequisites 4-9
Approach 4-9
Roles and Responsibilities 4-10
Prototyping Technique 4-10
MC.050 – Update Setup Documentation (Core) 4-11
Activity/Task Group 4-11
Work Product 4-11
Prerequisites 4-11
Approach 4-11
Roles and Responsibilities 4-11
RD.011 – Update Business Process Model (Core) 4-12
Activity/Task Group 4-12
Work Product 4-12
Prerequisites 4-12
Approach 4-12
Roles and Responsibilities 4-12
MC.063 – Conduct Configuration Familiarization/Coaching Sessions (Core) 4-13
Activity/Task Group 4-13
Work Product 4-13
Prerequisites 4-13
Approach 4-13
Roles and Responsibilities 4-14
CV.027 – Perform Data Mapping (Optional) 4-15
Activity/Task Group 4-15
Work Product 4-15
Prerequisites 4-15
Approach 4-15
Roles and Responsibilities 4-15
CV.053 – Prepare Data for Loading (Optional) 4-16
Activity/Task Group 4-16
Work Product 4-16
Prerequisites 4-16
Approach 4-16
Roles and Responsibilities 4-16
CV.065.1 – Load, Reconcile and Validate Data (Optional) 4-17
Activity/Task Group 4-17
Work Product 4-17
Prerequisites 4-17
Approach 4-17
Roles and Responsibilities 4-17

CV.026 – Conduct Content Strategy Session (Optional) 4-18

Activity/Task Group 4-18
Work Product 4-18
Prerequisites 4-18
Approach 4-18
Roles and Responsibilities 4-18

CV.066 – Prepare and Load Content (Optional) 4-19

Activity/Task Group 4-19
Work Product 4-19
Prerequisites 4-19
Approach 4-19
Roles and Responsibilities 4-19

IM.050.1 – Implement Integration Packages – Oracle (Optional) 4-20

Activity/Task Group 4-20
Work Product 4-20
Prerequisites 4-20
Approach 4-20
Roles and Responsibilities 4-21

IM.050.2 – Implement Integration Packages – Customer Systems (Optional) 4-22

Activity/Task Group 4-22
Work Product 4-22
Prerequisites 4-22
Approach 4-22
Roles and Responsibilities 4-23

TE.045 – Validate Integration Packages (Optional) 4-24

Activity/Task Group 4-24
Work Product 4-24
Prerequisites 4-24
Approach 4-24
Roles and Responsibilities 4-24

IM.050.3 – Implement Extensions (Optional) 4-25

Activity/Task Group 4-25
Work Product 4-25
Prerequisites 4-25
Approach 4-25
Roles and Responsibilities 4-25

MC.070.2 – Implement Extensible Items (Optional) 4-26

Activity/Task Group 4-26
Work Product 4-26
Prerequisites 4-26
Approach 4-26
Roles and Responsibilities 4-26

MC.085 – Prepare Reports (Optional) 4-27

Activity/Task Group 4-27
Work Product 4-27
Prerequisites 4-27
Approach 4-27
Roles and Responsibilities 4-27

TE.030 – Validate Extensions (Optional) 4-28

Activity/Task Group 4-28
Work Product 4-28
Prerequisites 4-28
Approach 4-28
Roles and Responsibilities 4-28

TS.020– Define Cutover Strategy (Core) 4-29

Activity/Task Group 4-29
Work Product 4-29
Prerequisites 4-29
Approach 4-29
Roles and Responsibilities 4-29

TS.040 – Design Production Support Infrastructure (Core) 4-30

Activity/Task Group 4-30
Work Product 4-30
Prerequisites 4-30
Approach 4-30
Roles and Responsibilities 4-30

MC.070.3– Implement Security (Core) 4-31

Activity/Task Group 4-31
Work Product 4-31
Prerequisites 4-31
Approach 4-31
Roles and Responsibilities 4-31

WM.055.2 – Conduct Implementation Checkpoint (Core) 4-32

Activity/Task Group 4-32
Work Product 4-32
Prerequisites 4-32
Approach 4-32
Roles and Responsibilities 4-32

PEC.MPE.2 – Manage Project Execution (Core) 4-33

Activity/Task Group 4-33
Work Product 4-33
Prerequisites 4-33
Approach 4-33
Roles and Responsibilities 4-34

CHAPTER *5* **Validate (C) Phase 5-1**

Validate Phase Objectives 5-2

MC.070.4 –Setup Applications (Core) 5-5

Activity/Task Group 5-5
Work Product 5-5
Prerequisites 5-5
Approach 5-5
Roles and Responsibilities 5-5

TE.027 – Update Validation Scripts (Core) 5-6
Activity/Task Group 5-6
Work Product 5-6
Prerequisites 5-6
Approach 5-6
Roles and Responsibilities 5-6
TE.105 – Prepare Users for Validation (Core) 5-7
Activity/Task Group 5-7
Work Product 5-7
Prerequisites 5-7
Approach 5-7
Roles and Responsibilities 5-7
CV.065.2 – Load, Reconcile and Validate Data (Optional) 5-8
Activity/Task Group 5-8
Work Product 5-8
Prerequisites 5-8
Approach 5-8
Roles and Responsibilities 5-8
TE.070 – Conduct End-to-End Review (Core) 5-9
Activity/Task Group 5-9
Work Product 5-9
Prerequisites 5-9
Approach 5-9
Roles and Responsibilities 5-10
DO.070 – Publish User Guide (Job Aid) (Optional) 5-11
Activity/Task Group 5-11
Work Product 5-11
Prerequisites 5-11
Approach 5-11
Roles and Responsibilities 5-12
DO.075 – Publish Admin Guide (Optional) 5-13
Activity/Task Group 5-13
Work Product 5-13
Prerequisites 5-13
Approach 5-13
Roles and Responsibilities 5-13
TR.080 – Prepare for Training (Optional) 5-14
Activity/Task Group 5-14
Work Product 5-14
Prerequisites 5-14
Approach 5-14
Roles and Responsibilities 5-15
TR.095 – Conduct Train-the-Trainer Workshops (Optional) 5-16
Activity/Task Group 5-16
Work Product 5-16
Prerequisites 5-16
Approach 5-16
Roles and Responsibilities 5-16

TA.125 – Execute Technical Readiness Assessment (Optional) 5-17

Activity/Task Group 5-17
Work Product 5-17
Prerequisites 5-17
Approach 5-17
Roles and Responsibilities 5-17

WM.055.3 – Conduct Implementation Checkpoint (Core) 5-18

Activity/Task Group 5-18
Work Product 5-18
Prerequisites 5-18
Approach 5-18
Roles and Responsibilities 5-18

PEC.MPE.3 – Manage Project Execution (Core) 5-20

Activity/Task Group 5-20
Work Product 5-20
Prerequisites 5-20
Approach 5-20
Roles and Responsibilities 5-21

CHAPTER 6 Transition (D) Phase 6-1

Transition Phase Objectives 6-2

TS.045 – Remove Test Data from Production (Optional) 6-5

Activity/Task Group 6-5
Work Product 6-5
Prerequisites 6-5
Approach 6-5
Roles and Responsibilities 6-5

TS.050 – Migrate Configuration to Production (Core) 6-6

Activity/Task Group 6-6
Work Product 6-6
Prerequisites 6-6
Approach 6-6
Roles and Responsibilities 6-6

TS.051 – Migrate Integrations and Extensions to Production (Optional) 6-7

Activity/Task Group 6-7
Work Product 6-7
Prerequisites 6-7
Approach 6-7
Roles and Responsibilities 6-7

CV.065.3 – Load, Reconcile and Validate Data Loads in Production (Optional) 6-8

Activity/Task Group 6-8
Work Product 6-8
Prerequisites 6-8
Approach 6-8
Roles and Responsibilities 6-8

TE.120 – Conduct Final Validation Review with Users and Stakeholders (Core) 6-9

Activity/Task Group 6-9
Work Product 6-9
Prerequisites 6-9
Approach 6-9
Roles and Responsibilities 6-10

TR.100 – Conduct End-User Training (Optional) 6-11

Activity/Task Group 6-11
Work Product 6-11
Prerequisites 6-11
Approach 6-11
Roles and Responsibilities 6-11

TS.052 – Implement Production Support Infrastructure (Core) 6-12

Activity/Task Group 6-12
Work Product 6-12
Prerequisites 6-12
Approach 6-12
Roles and Responsibilities 6-12

TS.058 – Verify Production and Operational Readiness (Core) 6-13

Activity/Task Group 6-13
Work Product 6-13
Prerequisites 6-13
Approach 6-13
Roles and Responsibilities 6-13

TS.060 – Begin Production Use (Core) 6-14

Activity/Task Group 6-14
Work Product 6-14
Prerequisites 6-14
Approach 6-14
Roles and Responsibilities 6-14

WM.055.4 – Conduct Implementation Checkpoint (Core) 6-15

Activity/Task Group 6-15
Work Product 6-15
Prerequisites 6-15
Approach 6-15
Roles and Responsibilities 6-15

PEC.MPE.4 – Manage Project Execution (Core) 6-16

Activity/Task Group 6-16
Work Product 6-16
Prerequisites 6-16
Approach 6-16
Roles and Responsibilities 6-17

CHAPTER 7 **Realization (E) Phase 7-1**

Realization Phase Objectives 7-2

PS.005 – Manage Transition to Steady-State Operations (Core) 7-4

Activity/Task Group 7-4
Work Product 7-4
Prerequisites 7-4
Approach 7-4
Roles and Responsibilities 7-4

PS.065 – Post Go-Live Support (Core) 7-5

Activity/Task Group 7-5
Work Product 7-5
Prerequisites 7-5
Approach 7-5
Roles and Responsibilities 7-5

PS.070 – Execute Handoff to Customer Relationship Manager (Optional) 7-6

Activity/Task Group 7-6
Work Product 7-6
Prerequisites 7-6
Approach 7-6
Roles and Responsibilities 7-6

PEC.MPE.5 – Manage Project Execution (Core) 7-7

Activity/Task Group 7-7
Work Product 7-7
Prerequisites 7-7
Approach 7-7
Roles and Responsibilities 7-8

PC.GA – Gain Acceptance (Core) 7-9

Activity/Task Group 7-9
Work Product 7-9
Prerequisites 7-9
Approach 7-9
Roles and Responsibilities 7-9

PC.CPC – Close Processes and Contract (Core) 7-10

Activity/Task Group 7-10
Work Product 7-10
Prerequisites 7-10
Approach 7-10
Roles and Responsibilities 7-11

APPENDIX A **Work Breakdown Structure A-1**

How to Read the Work Breakdown Structure A-1
Cloud Application Services OUM WBS A-1

CHAPTER

1 Introduction

The *Cloud Application Services OUM (CAS OUM) Solution Delivery Guide* provides an overview of the approach, phases, activities and tasks that define the CAS OUM approach. The information in this guide enables project managers, and project team members, to better understand the full scope of a Cloud Application Services implementation, and to plan and execute those projects.

What is the Cloud Application Services OUM Approach?

The Cloud Application Services Oracle® Unified Method (CAS OUM) approach (formerly known as the OUM Cloud Application Services Implementation Approach) is Oracle's lightweight approach for implementing applications running on a cloud infrastructure. It emphasizes an out-of-the-box approach and adoption of best practices inherent in the application products as a foundational element of the approach.

How to Use This Guide

The *Cloud Application Services OUM Solution Delivery Guide* contains general information about using this approach for Cloud applications implementation projects.

Contributors

Freddie Bellini, Simon Boulanger, Patti Burke, Sara Chejanovich, Laurie Coleman, Denise Duncan, Lars Ebert, Stuart Fleming, Candelas Cano Gallego, Oscar Gendrop, Matt Hammerbacher, Helle Hennings, Rebecca Hodgson, Rich Isola, Gregory Jones, Steve Karnes, Sareetha Kanchan, Chris Kirsanoff, Sesh Komanduri, Bas Laat, Pablo Macchi, Haruka Matsumoto, Gareth Millwood, Tamzin Morphy, Peter Moss, Daniel Muddiman, John Palethorpe, Kjirsten Petersen, Dinesh Pillay, Gergana Radoutcheva, Nadeem Rahman, Sasikala Rajagopal, Rob Readmond, Florencia Rizzi, Gerhard Seebacher, Shashank Shukla, Sabine Smith, Harrie Stoltenberg, Tatsuhiko Suekane, Ken Thompson, Deepak Thuse, Revathi Venkatraman, Sujith Verghese, Louann Weaver, Leslie Williams , Ian Wood

Your Feedback is Requested

Global Methods values and appreciates your comments as an Oracle practitioner and reader of this guide. As we write, revise, and evaluate our documentation and other delivery materials, your comments are the most valuable input we receive. If you would like to contact us regarding comments on this manual, or other CAS OUM materials, please use the following email address:

mailto:ominfo_us@oracle.com

CHAPTER

2 Approach Overview

The Cloud Application Services OUM approach is intended to support the implementation of all Oracle applications running on a cloud infrastructure. It provides a lightweight approach for SaaS implementations.

Scope

The Cloud Application Services OUM approach is applicable to all HCM Cloud, Sales Cloud, Service Cloud and ERP Cloud application implementations.

While the focus of the approach is on the implementation of the standard, out-of-the-box functionality embodied in the products selected for implementation, the approach also includes support for selected additional services, such as integrations, data loads, project-specific documentation, training, etc.

Objectives

The objectives of the CAS OUM approach follow:

- Rapid design, configuration and deployment of an initial release of the software solution consisting of standard functionality embodied in the products selected for implementation.
- Emphasis on getting customers up and using the new system in less time and at a lower cost following a standard approach.
- Maximize use of best practices inherent in the product.
- Implementation of standard business rules, standard integrations and standard data loads.
- To the extent possible, implementation of additional functionality and custom integrations, etc. should be addressed in subsequent releases.

Approach Overview

The diagram below depicts the key activities that describe the CAS OUM approach. While it clearly does not reflect all of the activities that might be performed during a project, it does represent the "Top Level Flow" of activities that define the approach.

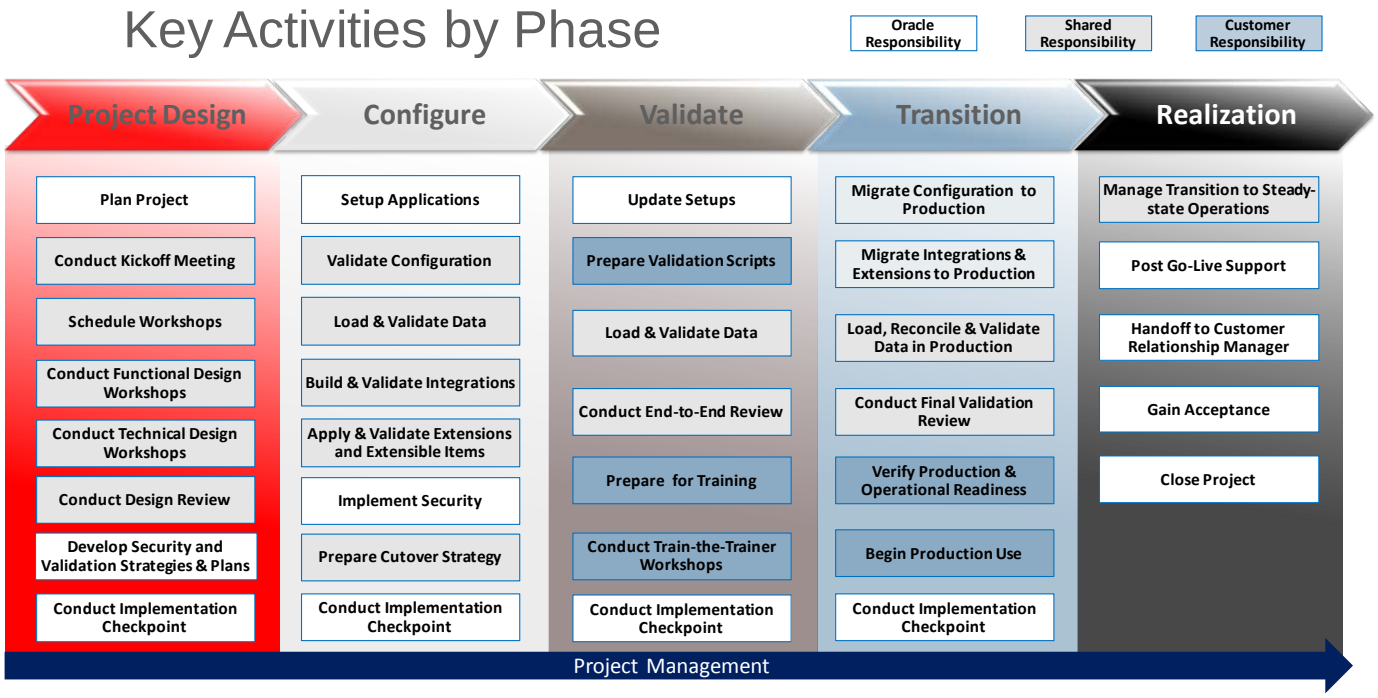

The approach is comprised of 5 phases – Project Design, Configure, Validate, Transition and Realization.

The Project Design phase is the first phase in the CAS OUM approach and is critical for establishing a positive impression, and setting appropriate expectations, with the customer and the project team. During this phase, the project is planned and the processes governing the conduct of the project defined. A Kickoff Meeting is then held to orient the entire project team to the project objectives and how the project will be conducted. Workshops are scheduled and conducted to gather setup information (Functional Design) and define technical details for integrations and data loads (Technical Design). Security and testing requirements are reviewed and plans for addressing them are prepared. The phase concludes with a checkpoint to verify that the phase objectives have been met and necessary approvals obtained.

In the Configure phase, the configuration settings documented in the Functional Design are implemented in the non-production environment. Workshops are then conducted with customer personnel to demonstrate the standard functionality and validate that the system behavior is as expected and meets the customer's business needs. Customer data is also prepared, loaded and verified during this phase, and integrations, extensions and extensible items built and tested. Security is implemented, and a plan for taking the new system to production is prepared. The phase culminates with another checkpoint to confirm that the phase objectives have been met and obtain the necessary approvals.

It should be stressed at this point that SaaS implementations focus on the implementation of standard product and do not involve customizing the product in the traditional sense. Extensions and extensible items as referenced in this guide represent adjustments which can be made to the product look and feel, etc., using standard product features that preserve those changes during upgrades.

The Validate phase is focused on preparing for and conducting an End-to-End Review of the new SaaS system, including standard functionality, data loads and integrations. Activities during the Validate phase include the entry of any configuration changes in the non-production environment and the validation of those values. If necessary, business processes and test cases are updated to reflect the resulting state of the environment and sample customer data is loaded in preparation for an End-to-End Review.

The End-to-End Review conducted in the Validate phase is intended to validate the final configuration, which will be used to configure the production environment in the next phase. During the End-to-End Review, a series of Validation Scripts are executed to validate the proper functioning of the software solution. The test cases should also exercise the customer data that has been loaded to the non-production environment to validate that the data has been loaded properly. A train-the-trainer event is also held in the Validate phase to prepare designated customer personnel to train end users. Like the previous phases, a checkpoint at the end of the phase confirms that the objectives have been met and necessary approvals obtained.

The Transition phase focuses on moving the new software system and the organization to production use. The validated configuration is migrated to the production environment, the customer data is loaded, and a final review is conducted with users and stakeholders to help ensure that the new environment is ready for use. A production and operational readiness assessment is made as a final checkpoint and the Transition phase concludes with the new system being placed in production use.

The Realization phase begins active use of the system and, during the phase, the transition to steady-state operations is managed. This phase also includes any post-production support called for in the contract, the obtaining of the final acceptance of the system, and the closing out of the project and related processes.

Core and Optional Tasks

Cloud Application Services implementation projects may range from simple projects involving only the configuration of standard functionality to more complex projects requiring custom integrations, complex workflows, additional data loads, etc.

Core and Optional Tasks in the CAS OUM Approach

The core tasks in the CAS OUM approach define the minimum set of steps necessary to implement the standard, out-of-the-box functionality embodied in the products selected for implementation. You may also need to include several other tasks in your project depending on your specific circumstances. For example, if your project includes custom integrations, or additional training or documentation requirements, you may need to include several optional tasks that support those additional services. A good test during project planning is to walk through the core tasks to ensure they meet the project's needs. If not, begin considering optional tasks. This planning process will help create an efficient project approach.

Task Selection Guidelines

Determining which optional tasks to include in the project plan is ultimately the responsibility of the project manager. To assist you in making your determinations, a number of optional task criteria, which serve as indicators for inclusion of related optional tasks, have been identified. Use the general guidelines below as well as the optional task criteria included in the task overview for all tasks identified as optional, to determine which optional tasks to include in your project.

Optional task criteria and the optional tasks associated with them are described below in terms of the following general groupings:

- Training
- Documentation
- Extensible Items/Extensions/Custom Reports
- Data Loads
- Integrations
- Other

Training

If your project objectives include training for the project team, end users or both, you should include one or more of the following tasks:

- TR.050 Train Project Team
- TR.080 Prepare for Training
- TR.095 Conduct Train-the-Trainer Workshops
- TR.100 Conduct End-User Training

Documentation

If your project objectives include publishing project-specific documentation, you should include one or more of the following tasks:

- DO.010 Define Documentation Requirements and Strategy

- DO.070 Publish User Guide (Job Aid)
- DO.075 Publish Admin Guide

Extensible Items/Extensions/Custom Reports

If your project objectives include extensible items, extensions, or custom reports, you should include one or more of the following tasks:

- IM.050.3 Implement Extensions
- MC.070.2 Implement Extensible Items
- MC.085 Prepare Reports
- TE.030 Validate Extensions

Data Loads

If your project objectives include the population of production tables in the new Oracle application system with data from legacy systems, you should include one or more of the following tasks:

- DS.145 Conduct Technical Design Workshops
- CV.027 Perform Data Mapping
- CV.053 Prepare Data for Loading
- CV.065.1 Load, Reconcile and Validate Data
- CV.065.2 Load, Reconcile and Validate Data
- CV.065.3 Load, Reconcile and Validate Data Loads in Production

Integrations

If your project objectives include integrations to third-party or internally-developed systems, or integrations between Oracle applications installed in separate environments, you should include one or more of the following tasks:

- DS.145 Conduct Technical Design Workshops
- IM.050.1 Implement Integration Packages – Oracle
- IM.050.2 Implement Integration Packages - Customer Systems
- TE.045 Validate Integration Packages

Other

If your project objectives include conducting a Technical Readiness Assessment, you should include the following tasks:

- TA.010 Conduct Technical Readiness Assessment Kickoff Meeting
- TA.125 Execute Technical Readiness Assessment

If your project objectives include the preparation and loading of predefined correspondence, such as, Offer Letters, or job descriptions, competence and job catalogs, or similar content, you should include the following tasks:

- CV.026 Conduct Content Strategy Session
- CV.066 Prepare and Load Content

For Taleo implementations only, if your project objectives include the removal of test data from the Production Zone (Environment), you should include the following task:

- TS.045 Remove Test Data from Production

If your project objectives include a handoff to a customer relationship manager, you should include the following task:

- PS.070 Execute Handoff to Customer Relationship Manager

Important Concepts

There are several key concepts that are important to understand in order to fully appreciate the CAS OUM approach. These concepts include:

- Cloud Environment Provisioning
- Environment Management and Usage
- Project Management

Cloud Environment Provisioning

The provisioning of Cloud environments is initiated by the Oracle License Sales representative, when the customer contracts with Oracle to provide SaaS hosted applications. The customer is asked to complete a questionnaire specifying the SaaS applications to be provided, which is then forwarded to the Cloud Operations team for provisioning of the environments.

Project managers should confirm that the customer's environments have been provisioned and that administrative login information is available prior to commencement of the project. This is typically accomplished during the initial phone contact with the customer or as part of task PS.ACT.RPAC Review Project Approach with Customer and Confirm Customer Readiness during Project Start Up activities, at the latest.

Environment Management and Usage

A standard Oracle Cloud Service subscription is auto provisioned with two environments:

1. Non-Production (sometimes referred to as staging), and
2. Production

With the exception of increased sizing for improved performance in production, these environments are identical when auto provisioned. Environments are provisioned with English as the default language. To add support for additional languages, you must request that the appropriate language packs be installed on your environments.

In some cases, you might want to request special-purpose environments in addition to the standard production and non-production environments provided with the service. These additional environments have additional costs associated with them and typically are used like non-production environments.

A critical step in the project planning process is to develop a time-phased environment usage plan that describes the implementation tasks and the environment where they will take place aligned with the overall project timeline. In general, the non-production environment supports all non-production activities. The sole purpose of production is to run your real day-to-day business operations and it should not be used for non-production activities.

The following diagram illustrates a typical usage plan for the cloud implementation lifecycle:

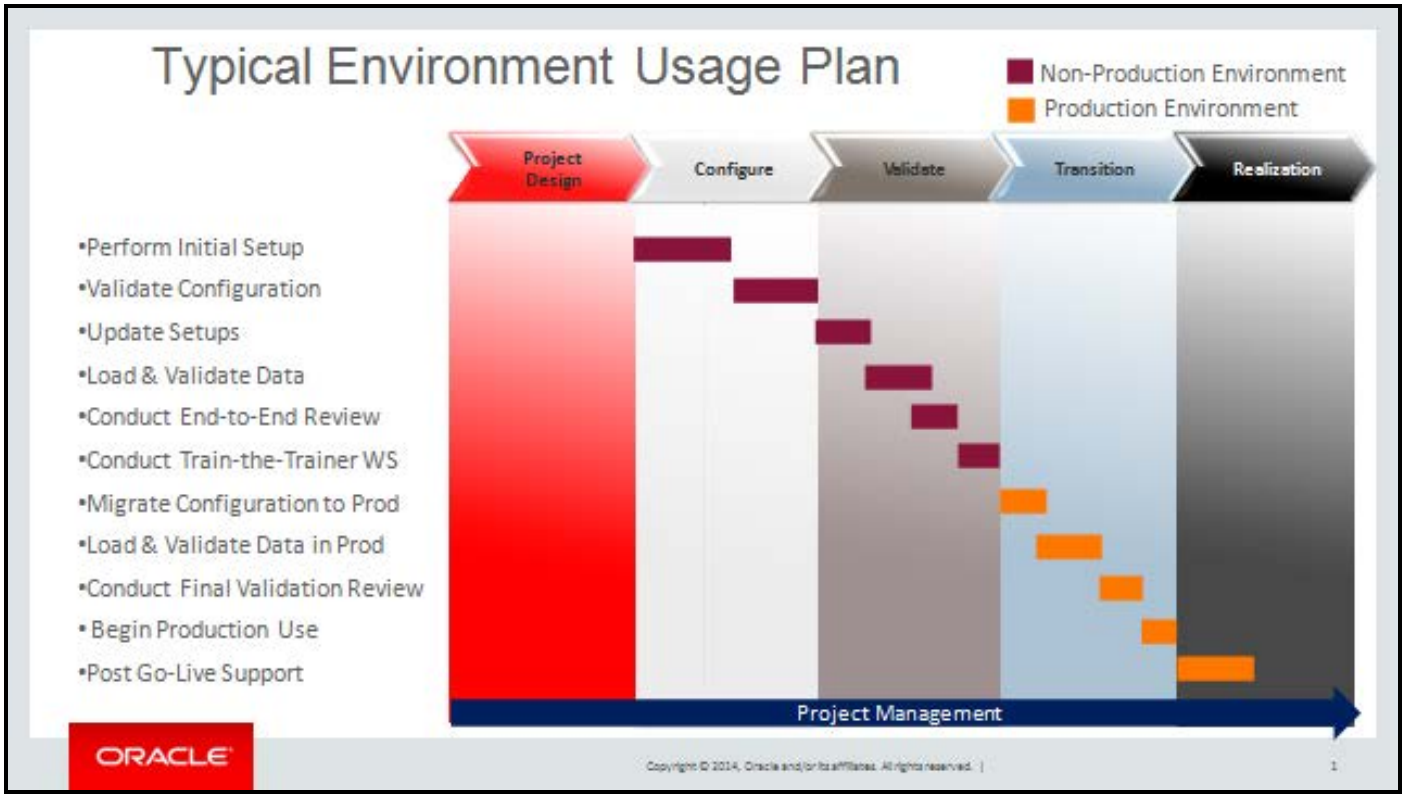

Project Management

Project management in a Cloud Application Services implementation is not significantly different from project management in a *traditional on-premises* implementation. The key difference is the depth of detail to which the project management tasks and associated work products are produced.

As with other OUM projects, project managers should adhere to standard operating procedures and customer-facing project management practices when executing a CAS OUM project, commensurate with the size and complexity of the project.

CHAPTER

3 Project Design (A) Phase

The goals of the Project Design phase include review and agree on the scope of the project, provide a clear framework for how the project will be delivered, prepare a detailed plan for the remainder of the project and capture functional and technical design decisions related to the software system being implemented.

Following confirmation of the project scope and objectives, preparation of a Project Workplan, and confirmation of the customer's readiness to proceed, a Kickoff Meeting is held to orient the entire team to the project's goals, objectives, and protocols to be followed during the project.

During the Project Design phase, a series of workshops are conducted to gather initial setup information and determine the approach, or approaches, that will be employed to address required integrations and the loading of legacy data.

Project Design Phase Objectives

The objectives of the Project Design phase follow:

- Statement of work is reviewed and agreement with customer obtained.
- Project plan (including planned releases) is completed and base lined for project planning and control.
- Project budget is reviewed and finalized.
- Project is appropriately staffed.
- Conduct Customer Kickoff Meeting.
- Schedule workshops.
- Define Functional Design/Configuration Parameters.
- Prepare Technical Designs.

Project Design Phase Task Groups

The Project Design phase is comprised of the following Task Groups:

- A.TG.PSU Project Start Up
- A.TG.TR Prepare Project Team
- A.TG.FT Conduct Functional and Technical Design Workshops
- A.TG.SP Security Planning
- A.TG.VP Validation Planning
- A.TG.DO Documentation
- A.TG.TA Technical Readiness Assessment Kickoff
- A.TG.IC Implementation Checkpoint
- A.TG.PM Project Management

Key Work Products

The key work products of the Project Design phase are as follows:

Work Product	Description
Reviewed Contract, Scope, Workplan and Budget	The Reviewed Contract, Scope, Workplan and Budget is the result of the project manager reviewing the executed contract and related bid material, creating or validating the project plan, requesting the project resources and validating the project budget.

Work Product	Description
Confirmed Customer Readiness	The contract and project approach are reviewed with the customer to arrive at a common understanding of the project scope and objectives and the customer's ability to begin the project and fulfill customer obligations is confirmed.
Project Management Plan and Established Project Infrastructure	The Project Management Plan defines the governance approach for managing the project by identifying how the project will be planned, executed, controlled, monitored and reported on. The project infrastructure includes the systems and procedures to support the execution of the project.
Functional Design	The Functional Design contains the configuration information for the functionality that is in-scope for the project. This will be based on standard functionality.
Technical Designs	The Technical Designs contain the detailed technical specifications for custom data loads, integrations and other extensions.
Security Strategy and Plan	The Security Strategy and Plan documents the strategy for addressing security requirements, as well as the information necessary to establish good controls and transaction access through configuration of the functional security features of the applications and Single Sign-On.
Validation Strategy and Plan	The Validation Strategy and Plan documents the approach to testing and specific testing activities to be employed on the project.

Tasks and Work Products

The tasks and work products for this phase are:

ID	Task Name	Work Product	Required
PSU.RCSWB	Review Contract, Scope, Workplan and Budget	Reviewed Contract, Scope, Workplan and Budget	Always

ID	Task Name	Work Product	Required
PSU.RPAC	Review Project Approach with Customer and Confirm Customer Readiness	Confirmed Customer Readiness	Always
PSU.EGSI	Establish Governance and Supporting Infrastructure	Project Management Plan and Established Project Infrastructure	Always
STM.050	Conduct Customer Kickoff Meeting	Kickoff Meeting	Always
TR.050	Train Project Team	Trained Project Team	Project Team training is in-scope for the project.
WM.070	Schedule Workshops	Workshop Schedule	Always
MC.040	Conduct Functional Design Workshops	Functional Design	Always
DS.145	Conduct Technical Workshops	Technical Designs	Data loads, integrations, extensions, or custom reports are in-scope for the project.
DS.160	Conduct Design Reviews	Approved Designs	Always
MC.060	Develop Security Strategy and Plan	Security Strategy and Plan	Always
TE.010	Define Validation Strategy and Plan	Validation Strategy and Plan	Always
DO.010	Define Documentation Requirements and Strategy	Documentation Requirements and Strategy	Project-specific documentation is in-scope for the project.
TA.010	Conduct Technical Readiness Assessment Kickoff Meeting	Technical Readiness Assessment Kickoff Results	A Technical Readiness Assessment is in-scope for the project.
WM.055.1	Conduct Implementation Checkpoint	Implementation Checkpoint Meeting/Approval to Proceed	Always
PEC.MPE.1	Manage Project Execution	Managed Project Assets	Always

Responsibilities

The Oracle Implementation team has primary responsibility for the following tasks in this phase:

- PSU.RCSWB Review Contract, Scope, Workplan and Budget

- PSU.RPAC Review Project Approach with Customer and Confirm Customer Readiness
- PSU.EGSI Establish Governance and Supporting Infrastructure
- TR.050 Train Project Team (Optional)
- MC.060 Develop Security Strategy and Plan
- TE.010 Develop Validation Strategy and Plan
- DO.010 Define Documentation Requirements and Strategy (Optional)
- TA.010 Conduct Technical Readiness Assessment Kickoff Meeting (Optional)
- WM.055.1 Conduct Implementation Checkpoint
- PEC.MPE.1 Manage Project Execution

The Oracle Implementation team and the customer have a shared responsibility for the following tasks in this phase:

- STM.050 Conduct Customer Kickoff Meeting
- WM.070 Schedule Workshops
- MC.040 Conduct Functional Design Workshops
- DS.145 Conduct Technical Design Workshops
- DS.160 Conduct Design Reviews

PSU.RCSWB – Review Contract, Scope, Workplan and Budget (Core)

This task is the first activity the project manager does after being assigned to the project. This is the opportunity for the project manager to participate in a handoff from the sales team. Even when direct contact with the sales team is not feasible, the bid material, including the executed contract and any supporting collateral should be obtained and reviewed by the project manager.

While reviewing the contract, the project manager confirms the contracted scope, paying special attention to optional areas such as data loads and integrations. The project manager compares the Project Workplan to the contracted scope and addresses any inconsistencies.

The Project Workplan denotes the tasks to be performed by the team and may include customer activities or placeholders on which the project is dependent. During Project Execution and Control, the project plan will be revised as necessary.

The Project Workplan is used as input to develop the staff plan and the project budget. It is also during this task that the resources are requested and the project is staffed.

If there are gaps among the contract, the workplan or the financials, these gaps must be addressed prior to moving forward with a commitment to deliver the project.

Activity/Task Group

A.TG.PSU Project Start Up

Work Product

Reviewed Contract, Scope, Workplan and Budget – The Reviewed Contract, Scope, Workplan and Budget is the result of the project manager reviewing the executed contract and related bid material, creating or validating the project plan, requesting the project resources and validating the project budget. The following may be included components:

- Reviewed Bid Material
- Reviewed Contract
- Confirmed Project Scope
- Requested Resources
- Staffed Project
- Baseline Workplan
- Confirmed Budget

Prerequisites

You need the following for this task:

Prerequisite	Usage
Executed Contract	The executed contract signed by both the customer and Oracle is an input to this task. The contract scope, financials, assumptions, customer obligations, terms and conditions must be well understood by the project manager.

Approach

When performing this task, consider the following:

- If feasible, meet with the bid team to perform a hand-off between sales and delivery.
- Review final contract and bid material.
- Review contract estimates and approved profitability figures including labor, non-bill expenses and staff plan.
- Review contract for terms and conditions and any exceptions that may include special billing instructions, expense guidelines, and receipt requirements.
- Understand project scope and review generated project timeline to make sure it is consistent with the contract.
- Review Project Objectives.
- Document all assumptions concerning scope, resources, user participation, sign-off, issues resolution.
- Determine the content of the release(s).
- Create Project Workplan.
- Staff project by securing project resources.
- Validate/Revise Project Budget based on actual resource assignments.
- Address any disconnects prior to the start of the project.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

PSU.RPAC – Review Project Approach with Customer and Confirm Customer Readiness (Core)

As soon as feasible, the project manager contacts the customer to assess the customer's readiness to begin the project. During this contact, the availability of provisioned Cloud environments, the project approach, including project scope, objectives, assumptions and customer obligations, is confirmed. Customer resource commitments are also discussed and confirmed.

Activity/Task Group

A.TG.PSU Project Start Up

Work Product

Confirmed Customer Readiness – The contract and project approach is reviewed with the customer to arrive at a common understanding of the project scope and objectives and the customer's ability to begin the project and fulfill customer obligations is confirmed.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Executed Contract	The executed contract signed by both the customer and Oracle is an input to this task. The contract scope, financials, assumptions, customer obligations, terms and conditions must be well understood by the project manager.

Approach

When performing this task, consider the following:

- Establish contact with the customer and assess their readiness to begin the project.
- Confirm that environments have been provisioned and administrative login information is available. (There is a lead time associated with the provisioning process so this needs to be addressed as early as possible.)
- Conduct high-level review of contract scope and conditions with the customer.
- Set expectations regarding the project approach, planned releases and key milestones.
- Emphasize the importance of Organizational Change Management in maximizing the benefits of investments in new technology. Reiterate the usefulness of clearly articulating and communicating the project's value proposition, as well as having the support of key stakeholders throughout the project.
- Obtain customer resource commitments to fulfill customer obligations and to attend planned workshops.

Roles and Responsibilities

The Oracle Implementation team and the customer have a shared responsibility for this task.

PSU.EGSI – Establish Governance and Supporting Infrastructure (Core)

This task establishes the governance model for the project including the detailed plans that are used to manage the project.

The governance model and supporting plans are known as the Project Management Plan (PMP). The PMP is not intended to be a large, complex plan. Rather, it is meant to clearly and concisely explain how the project will be governed, planned, executed and controlled. The PMP provides an overall project management framework for executing the project.

Additionally, this task establishes the necessary project infrastructure needed to support the execution of the PMP and conduct the project. With a Cloud implementation, much of the infrastructure and related governance may already be established. In this case, the focus of this task is to verify that the current established procedure and tools align with the project needs and support the project delivery.

Activity/Task Group

A.TG.PSU Project Start Up

Work Product

Project Management Plan and Established Project Infrastructure – The Project Management Plan defines the governance approach for managing the project by identifying how the project will be planned, executed, controlled, monitored and reported on. The project infrastructure includes the systems and procedures to support the execution of the project.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Executed Contract	The contract scope, financials, assumptions, customer obligations, terms and conditions must be well understood by the project manager.

Approach

When performing this task, consider the following:

- Establish project governance.
- Verify or determine the process for:
  - Change Control
  - Financial Management
  - Risk Tracking and Resolution
  - Issue Tracking and Resolution
  - Problem Tracking and Resolution

    - Quality Standards, Project Standards, including naming conventions and standard look and feel, quality reporting
    - Configuration Control and Release Management
    - Standard Communications - to whom, what format and frequency
    - Project documentation archiving policy and process
    - Process for on-boarding resources
    - Procurement process, if required
    - Execution of planned quality checkpoints and validations
- Establish/review project infrastructure to support the project approach including risk, issue, problem and configuration management systems.
- Set up time, expense and billing (invoice) tracking processes.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

STM.050 – Conduct Customer Kickoff Meeting (Core)

The purpose of this task is to plan and conduct a project Kickoff Meeting to orient the team to the project. If warranted, similar orientation meetings can be given for new team members that join the project after kickoff. This meeting helps streamline the on-boarding process, communicate the project objectives and structure, and begin to develop cohesion among the team.

Work Product

Kickoff Meeting – The Kickoff Meeting is conducted to orient the project team and communicate to them the project objectives and structure.

Activity/Task Group

A.TG.TR Prepare Project Team

Prerequisites

You need the following for this task:

Prerequisite	Usage
Project Management Plan and Established Project Infrastructure	The Project Management Plan defines the governance approach for managing the project by identifying how the project will be planned, executed, controlled, monitored and reported on. The project infrastructure includes the systems and procedures to support the execution of the project.

Approach

When performing this task, consider the following:

- Allow each team member to introduce themselves and the role they will play on the project.
- Capture any issues and concerns that cannot be addressed during the meeting and establish a plan to respond back to the team.
- Introduce the project's Organizational Change Management approach, if applicable. Outline the key components of a Change Management Plan and how each component contributes to making the project a success.

Roles and Responsibilities

The Oracle Implementation team and the customer have a shared responsibility for this task.

TR.050 – Train Project Team (Optional)

The purpose of this task is to conduct learning events for the project team.

The scope of the training may include knowledge and skills deemed necessary for the effective functioning of the team, if specified in the contract.

Δ If project team training is in-scope for your project, you should perform this task.

Activity/Task Group

A.TG.TR Prepare Project Team

Work Product

Trained Project Team – The Trained Project Team represents all members of the team who have participated in the learning events intended to give them the knowledge and skills they need to perform their roles on the team.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Project Management Plan and Established Project Infrastructure	The Project Management Plan defines the governance approach for managing the project by identifying how the project will be planned, executed, controlled, monitored and reported on. The project infrastructure includes the systems and procedures to support the execution of the project.

Approach

When performing this task, consider the following:

- Project team training should cover tools, applications, and all knowledge and skill areas deemed necessary for the effective functioning of the team.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

WM.070 – Schedule Workshops (Core)

In this task, you schedule a series of workshops aimed at gathering initial setup information, as well as those needed to disseminate, and gather, information regarding the integrations and data loads in-scope for the project.

Activity/Task Group

A.TG.TR Prepare Project Team

Work Product

Workshop Schedule – The Workshop Schedule lists the workshops that are planned for gathering setup information and addressing the integrations and data loads that are in-scope for the project. It specifies the date, time, duration, objectives, and required participants for each workshop. The Workshop Schedule should be incorporated into the Project Workplan.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Confirmed Customer Readiness	The contract and project approach is reviewed with the customer to arrive at a common understanding of the project scope and objectives and the customer's ability to begin the project and fulfill customer obligations is confirmed.
Kickoff Meeting	The Kickoff Meeting is conducted to orient the project team and communicate to them the project objectives and structure.

Approach

When performing this task, consider the following:

- Establish order of workshops based on Validated Scope.
- Determine how many workshops will be required for each business process area and how the work will be divided up across those workshops.
- If applicable, identify when the Organizational Change Management approach and related artifacts will be reviewed in detail.
- Identify the customer personnel required for each of the planned workshops and obtain their availability.
- Prepare the schedule and have it reviewed and approved by the customer.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

MC.040 – Conduct Functional Design Workshops (Core)

The purpose of this task is to gather detailed information about how the customer wants to operate in the new application system once it is in production use.

Conduct scheduled workshops aimed at reviewing business processes in scope for the project and collecting the input for completing configuration workbooks, or other documentation related to capturing setup information.

Activity/Task Group

A.TG.FT Conduct Functional and Technical Design Workshops

Work Product

Functional Design – The Functional Design contains the configuration information for the functionality that is in-scope for the project. It records the parameters, user-defined codes, and other setups for each application.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Confirmed Customer Readiness	The contract and project approach is reviewed with the customer to arrive at a common understanding of the project scope and objectives and the customer's ability to begin the project and fulfill customer obligations is confirmed.
Workshop Schedule	The Workshop Schedule lists the workshops that are planned for gathering setup information and addressing the integrations and data loads that are in-scope for the project. It specifies the date, time, duration, objectives, and required participants for each workshop.

Approach

When performing this task, consider the following:

- Strong facilitation skills are required for this task and a process for capturing issues is essential.
- Use standard Process Models reflecting the functionality in scope as the basis this review, if available. The purpose of these sessions is to ensure that the implementation of standard product functionality is realized, not to explore alternative processes.
- Have metrics the customer is hoping to improve been identified and baseline values established?
- What is the customer's reporting requirements? Will standard, out-of-the-box reports meet those requirements?

- For Financials/ERP implementations, verify that the Functional Design addresses key configuration elements like enterprise structures, chart of accounts and hierarchies, as well as reporting requirements.

Roles and Responsibilities

The Oracle Implementation team and the customer have a shared responsibility for this task.

DS.145 – Conduct Technical Design Workshops (Optional)

In this task, you conduct workshops to determine the data conversion options and integration concepts to be used, and prepare detailed design specifications for custom data loads, integrations and other extensions in scope for the project. If applicable, the Organizational Change Management approach and related artifacts are also reviewed in detail.

Δ If data loads, integrations, extensions, or custom reports are in-scope for the project, you should perform this task.

Activity/Task Group

A.TG.FT Conduct Functional and Technical Design Workshops

Work Product

Technical Designs – The Technical Designs contain the detailed technical specifications for custom data loads, integrations and other extensions.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Confirmed Customer Readiness	The contract and project approach is reviewed with the customer to arrive at a common understanding of the project scope and objectives and the customer's ability to begin the project and fulfill customer obligations is confirmed.
Workshop Schedule	The Workshop Schedule lists the workshops that are planned for gathering setup information and addressing the integrations and data loads that are in-scope for the project. It specifies the date, time, duration, objectives, and required participants for each workshop.

Approach

When performing this task, consider the following:

- Which integrations are considered in-scope for the project?
- Are there any additional pre-built or custom integrations that have been requested by the customer?
- Which integration approaches are appropriate for the integrations in scope?
- If applicable, distribute Organizational Change Management documents and related materials in conjunction with a detailed review of the Organizational Change Management approach adopted for the project.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

DS.160 – Conduct Design Reviews (Core)

The purpose of this task is to review the design specifications.

Conduct a review of the Functional and Technical Designs with the customer and obtain acceptance.

Activity/Task Group

A.TG.FT Conduct Functional and Technical Design Workshops

Work Product

Approved Designs – The Approved Designs are the Functional and Technical Designs, which have been reviewed with the customer and approved.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Functional Design	The Functional Design contains the configuration information for the functionality that is in-scope for the project.
Technical Designs	The Technical Designs contain the detailed technical specifications for custom data loads, integrations and other extensions.

Approach

When performing this task, consider the following:

- Have internal peer reviews been conducted prior to the review with the customer?
- The review team may either be assembled in one place or review comments submitted via electronics means.
- Have any defects, or inconsistencies, been addressed?

Roles and Responsibilities

The Oracle Implementation team and the customer have a shared responsibility for this task.

MC.060 – Develop Security Strategy and Plan (Core)

The purpose of this task is to gather role and function information and relate them to application security features and roles.

You also define which Single Sign-On Protocol the customer will implement, if applicable.

Activity/Task Group

A.TG.SP Security Planning

Work Product

Security Strategy and Plan– The Security Strategy and Plan documents the strategy for addressing security requirements, as well as the information necessary to establish good controls and transaction access through configuration of the functional security features of the applications. It also identifies which Single Sign-On protocol has been selected for the implementation, the resources involved, as well all the tasks necessary for a successful implementation of Single Sign-On.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Functional Design	Functional Design contains the configuration information for the functionality that is in-scope for the project.

Approach

When performing this task, consider the following:

- Does the security structure defined support the business processes?
- Map business process steps and their agents (owners) with the application-provided user roles and make adjustments to the roles as required.
- Are users assigned to roles that map to their job responsibilities for the new system?

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

TE.010 – Define Validation Strategy and Plan (Core)

The purpose of this task is to define the testing strategy for the project.

Define a strategy and plan for validating/testing the proper functioning of the system throughout the project.

Activity/Task Group

A.TG.VP Validation Planning

Work Product

Validation Strategy and Plan – The Validation Strategy and Plan documents the approach to testing and specific testing activities to be employed on the project.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Functional Design	Functional Design contains the configuration information for the functionality that is in-scope for the project.
Technical Designs	The Technical Designs contain the detailed technical specifications for custom data loads, integrations and other extensions.

Approach

When performing this task, consider the following:

- Describe the scope of validation testing to be performed by defining the type and number of tests to be conducted.
- Define the criteria that determine whether an item has passed or failed a test.
- Describe testing roles and responsibilities
- How will converted data and integrations be included in the validations?

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

DO.010 – Define Documentation Requirements and Strategy (Optional)

In this task, you outline the overall requirements for creating user documentation and specify the work products to be produced. You also identify the strategy you will use for publishing project-specific documentation.

Δ If project-specific documentation is in scope for your project, you should perform this task.

Activity/Task Group

A.TG.DO Documentation

Work Product

Documentation Requirements and Strategy – The Documentation Requirements and Strategy identifies the project-specific documentation that must be published and the strategy for publishing that documentation.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Functional Design	Functional Design contains the configuration information for the functionality that is in-scope for the project.

Approach

When performing this task, consider the following:

- Has the customer requested project-specific documentation as an additional service?
- Which process areas are included in the scope of the project and what priority has been assigned to those process areas by the customer?
- Which process areas require user documentation or job aids?
- What strategy, tools, or techniques will be employed to develop and deploy the required user documentation?
- How much project-specific documentation is the customer committed to produce?

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

TA.010 – Conduct Technical Readiness Assessment Kickoff Meeting (Optional)

The purpose of this task is to conduct a Technical Architecture Workshop.

Conduct a kickoff meeting to orient project team, including customer resources, to the Technical Readiness Assessment approach.

Δ If a Technical Readiness Assessment is in-scope for the project, you should perform this task.

Activity/Task Group

A.TG.TA Technical Readiness Assessment Kickoff

Work Product

Technical Readiness Assessment Project Plan – The Technical Readiness Assessment Project Plan lists the tasks that need to occur to perform the Technical Readiness Assessment, as well as the dates and resources for when the assessments will take place.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Confirmed Customer Readiness	The contract and project approach is reviewed with the customer to arrive at a common understanding of the project scope and objectives and the customer's ability to begin the project and fulfill customer obligations is confirmed.

Approach

When performing this task, consider the following:

- Prepare the assessment schedule and have it reviewed and approved by the customer.
- Identify the customer personnel required for each assessment and obtain their availability.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

WM.055.1 – Conduct Implementation Checkpoint (Core)

In this task, you review the key work products completed during the phase with the customer, verify that the phase objectives have been met, confirm the next steps to be taken, and obtain approval to proceed with the next phase.

Activity/Task Group

A.TG.IC Implementation Checkpoint

Work Product

Implementation Checkpoint Meeting/Approval to Proceed – The Implementation Checkpoint Meeting/Approval to Proceed provides an opportunity to review the work completed during the phase with the customer, confirm the next steps and obtain the approval to proceed with the next phase of the implementation.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Functional Design	The Functional Design contains the configuration information for the functionality that is in-scope for the project.
Technical Designs	The Technical Designs contain the detailed technical specifications for custom data loads, integrations and other extensions.
Security Strategy and Plan	The Security Strategy and Plan documents the strategy for addressing security requirements, as well as the information necessary to establish good controls and transaction access through configuration of the functional security features of the applications and Single Sign-On.
Validation Strategy and Plan	The Validation Strategy and Plan documents the approach to testing and specific testing activities to be employed on the project.

Approach

When performing this task, consider the following:

- Have the key work products for the phase been completed and reviewed?
- Have the objectives set out for the phase been achieved?
- Have the next steps been determined and confirmed?

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

PEC.MPE.1 – Manage Project Execution (Core)

In this task, the execution of the project is managed. This includes using the policies, standards, and procedures delineated in the Project Start Up phase, performing the necessary reviews and measurements to validate that the project is being executed according to the Project Management Plan.

It also includes comparing actual performance with planned performance, analyzing variances, evaluating possible alternatives, and taking appropriate corrective action as needed.

The Manage Project Execution is made up of many *ongoing* tasks. An ongoing task is defined as a task that occurs continuously throughout a project, rather than at a specific pre-defined time. The ongoing tasks occur as needed and do not include dependencies among the tasks or with the execution method tasks.

Activity/Task Group

A.TG.PM Project Management

Work Product

Managed Project Assets – Reviewed project progress, analyzed variances and updated management plans and policies.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Project Management Plan and Established Project Infrastructure	The Project Management Plan defines the governance approach for managing the project by identifying how the project will be planned, executed, controlled, monitored and reported on. The project infrastructure includes the systems and procedures to support the execution of the project.

Approach

When performing this task, consider the following:

- Document lessons learned.
- Track project actual.
- Adjust Project Workplan, staff and budget as necessary.
- Adjust project approach (PMP) as necessary.
- Review the key outputs for the phase with customer and obtain agreement or acceptance (for fixed price projects).
- Verify that phase objectives have been met and confirm next steps.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

CHAPTER

4 Configure (B) Phase

The goal of the Configure phase is to demonstrate the standard functionality as configured in the non-production environment and validate that the configurations, integrations and data loads meet the customer's business needs.

At the outset of the Configure phase, the initial setup information, which was gathered during the Functional Design Workshops in the Project Design phase, is used to configure the non-production environment. A series of workshops are then conducted to demonstrate the standard functionality (as configured in the non-production environment) and validate that system behavior is as expected. Any refinements to the configurations are identified, prioritized, entered and reviewed during subsequent workshop sessions.

When pre-built or custom integrations or data loads are in scope for the project, optional tasks related to data mapping and preparation of components specified in the Technical Designs may also be executed. Customer data is prepared, loaded and validated during this phase, and inbound and outbound integrations are built, implemented and tested.

During the Configure phase, customer personnel may be tasked with cleaning and obtaining legacy data in preparation for loading, as appropriate. The phase then culminates with an implementation checkpoint to verify that phase objectives have been achieved and approval to proceed obtained.

Configure Phase Objectives

The objectives of the Configure phase follow:

- Perform initial setups in the non-production environment.
- Conduct workshops to validate the configuration of standard functionality.
- Load, reconcile and validate customer data.
- Implement and validate integrations and extensions (only where essential to the business and does not compromise the integrity of the SaaS solution).
- Prepare a Cutover Strategy.

Configure Phase Task Groups

The Configure phase is comprised of the following Task Groups:

- B.TG.IF Initial Configuration
- B.TG.FC Configuration Familiarization and Coaching
- B.TG.DL Load and Validate Data - Configure
- B.TG.CL Prepare and Load Content
- B.TG.IP Implement Integration Packages
- B.TG.IE Implement Extensions
- B.TG.PC Prepare for Cutover
- B.TG.IS Implement Security Plan
- B.TG.IC Implementation Checkpoint
- B.TG.PM Project Management

Key Work Products

The key work products of the Configure phase are as follows:

Work Product	Description
Validated Configuration	The Validated Configuration verifies that all setup data has been entered in accordance with the Functional Design/setup documentation and that system behavior is as expected.
Validated Data	The Validated Data is the customer data that has been loaded to the non-production environment, reconciled and validated to correctly reflect the legacy data in the format required by the new system.

Work Product	Description
Validated Integrations	The Validated Integrations represent the implemented integrations, which have been validated to function as expected, in accordance with the design.
Cutover Strategy	The Cutover Strategy documents how the new system is to be introduced. This work product is not a plan but describes the approach that is being taken to place the new system into production.

Tasks and Work Products

The tasks and work products for this phase are:

ID	Task Name	Work Product	Required
MC.070.1	Setup Applications	Configured Applications	Always
TE.025	Prepare Validation Scripts	Validation Scripts	Always
MC.080	Conduct Configuration Validation Workshops	Validated Configuration	Always
MC.050	Update Setup Documentation	Setup Documentation	Always
RD.011	Update Business Process Model	Future Process Model	Always
MC.063	Conduct Configuration Familiarization/Coaching Sessions	Configuration Familiarization/Coaching Sessions	Always
CV.027	Perform Data Mapping	Data Mapping	Custom data loads or custom integrations are in-scope for the project.
CV.053	Prepare Data for Loading	Prepared Data	Pre-built data loads, or custom data loads, are in-scope for the project.
CV.065.1	Load, Reconcile & Validate Data	Validated Data	Pre-built data loads, or custom data loads, are in-scope for the project.

ID	Task Name	Work Product	Required
CV.026	Conduct Content Strategy Session	Content Strategy	Content such as predefined correspondence (for example, Offer Letters) job descriptions, competence and job catalogs, or similar content, is in-scope for the project.
CV.066	Prepare and Load Content	Loaded Content	Content such as predefined correspondence (for example, Offer Letters) job descriptions, competence and job catalogs, or similar content, is in-scope for the project.
IM.050.1	Implement Integration Packages - Oracle	Integration Components - Oracle	Integrations are in-scope for the project.
IM.050.2	Implement Integration Packages - Customer Systems	Integration Components – Customer Systems	Integrations are in-scope for the project.
TE.045	Validate Integration Packages	Validated Integration Packages	Integrations are in-scope for the project.
IM.050.3	Implement Extensions	Implemented Extensions	Custom extensions intended to tailor the look and feel, navigation, etc., are in-scope for the project.
MC.070.2	Implement Extensible Items	Configured Extensible Items	Extensible items are in-scope for the project.
MC.085	Prepare Reports	Developed Reports	Custom reports are in-scope for the project.
TE.030	Validate Extensions (QA Testing)	QA Tested Extensions	Custom extensions intended to tailor the look and feel, navigation, etc., are in-scope for the project.
TS.020	Define Cutover Strategy	Cutover Strategy	Always
TS.040	Design Production Support Infrastructure	Production Support Infrastructure Design	Always

ID	Task Name	Work Product	Required
MC.070.3	Implement Security	Implemented Security	Always
WM.055.2	Conduct Implementation Checkpoint	Implementation Checkpoint Meeting/Approval to Proceed	Always
PEC.MPE.2	Manage Project Execution	Managed Project Assets	Always

Responsibilities

The Oracle Implementation team has primary responsibility for the following tasks in this phase:

- MC.070.1 Setup Applications
- TE.025 Prepare Validation Scripts
- MC.050 Update Setup Documentation
- MC.063 Conduct Configuration Familiarization/Coaching Sessions
- CV.026 Conduct Content Strategy Session (Optional)
- IM.050.1 Implement Integration Packages – Oracle (Optional)
- IM.050.3 Implement Extensions (Optional)
- MC.070.2 Implement Extensible Items
- MC.085 Prepare Reports
- MC.070.3 Implement Security
- WM.055.2 Conduct Implementation Checkpoint
- PEC.MPE.2 Manage Project Execution

The customer has primary responsibility for the following tasks in this phase:

- RD.011 Update Business Process Model
- CV.053 Prepare Data for Loading
- CV.066 Prepare and Load Content (Optional)
- IM.050.2 Implement Integration Packages - Customer Systems (Optional)
- TS.020 Define Cutover Strategy
- TS.040 Design Production Support Infrastructure

The Oracle Implementation team and the customer have a shared responsibility for the following tasks in this phase:

- MC.080 Conduct Configuration Validation Workshops
- CV.027 Perform Data Mapping (Optional)
- CV.065.1 Load, Reconcile & Validate Data (Optional)
- TE.045 Validate Integration Packages (Optional)
- TE.030 Validate Extensions (QA Testing) (Optional)

MC.070.1 –Setup Applications (Core)

The purpose of this task is to prepare the commercial-off-the-shelf (COTS) application environment for configuration prototyping or validation activities.

Configure the non-production environment according to the setup information contained in the Functional Design.

Activity/Task Group

B.TG.IF Initial Configuration

Work Product

Configured Applications – The Configured Applications is a software environment, generally the non-production environment, which has been configured according to the Functional Design.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Functional Design	The Functional Design contains the configuration information for the functionality that is in-scope for the project.

Approach

When performing this task, consider the following:

- Have all application parameters required to enable transactions been configured?
- Has enough business data been loaded to demonstrate application features effectively?
- Has access to setup and transaction screens been provided to appropriate users?
- Utilize available setup tools, such as Functional Setup Manager, as applicable.
- Include enabling of the Integration Layer.
- Verify setups and update setup documentation, as necessary.
- Should Configuration Validation Workshops result in changes that compromise the initial configuration, it may be necessary to configure subsequent validation workshop iterations using separate enterprise structures on the same non-production/test environment copy, or even - to request an additional non-production /test environment or a refresh from the production environment.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

TE.025 – Prepare Validation Scripts (Core)

The purpose of this task is to develop the System Test scripts/scenarios for testing the system.

Prepare demo scripts/test scripts for use in validating the setups, and related functionality, during the Configuration Validation Workshops. If predefined scripts are available for the functionality in question, update them as necessary instead of preparing new scripts.

Activity/Task Group

B.TG.IF Initial Configuration

Work Product

Validation Scripts – The Validation Scripts consist of the set of test scenarios, that each includes a number of test steps, which will be executed during the Configuration Validation Workshops and End-to-End Review.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Functional Design	The Functional Design contains the configuration information for the functionality that is in-scope for the project.

Approach

When performing this task, consider the following:

- Identify the functionality to be validated.
- Collect any predefined demo scripts/test scripts available for the functionality in question.
- Verify that scripts are aligned with setup values contained in the Functional Design.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

MC.080 – Conduct Configuration Validation Workshops (Core)

The purpose of this task is to prepare for and conduct a workshop(s) to validate the configuration.

Conduct workshops to demonstrate the standard functionality as configured in the non-production environment and validate that the configuration supports the customer's intended use of the system.

Activity/Task Group

B.TG.IF Initial Configuration

Work Product

Validated Configuration – The Validated Configuration is the set of setup parameters, which have been shown to support the customer's intended use of the system.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Workshop Schedule	The Workshop Schedule lists the workshops that are planned for gathering setup information and addressing the integrations and data loads that are in-scope for the project. It specifies the date, time, duration, objectives, and required participants for each workshop.
Configured Applications	The Configured Applications is a software environment, generally the non-production environment, which has been configured according to the Functional Design.
Validation Scripts	The Validation Scripts consist of the set of test scenarios, that each includes a number of test steps, which will be executed during the configuration prototyping workshops and End-to-End Review.

Approach

When performing this task, consider the following:

- Leverage applicable business process models as a starting point for the Configuration Validation Workshop sessions.
- Keep track of customer feedback during the workshop sessions.
- Determine how many sessions are required to validate all functional areas included in the project scope.
- Additional and revised configurations identified during these sessions may be implemented and validated in a subsequent session.
- Should Configuration Validation Workshops result in changes that compromise the initial configuration, it may be necessary to configure subsequent validation

workshop iterations using separate enterprise structures on the same non-production /test environment copy, or even - to request an additional non-production /test environment or a refresh from the production environment.

Roles and Responsibilities

The customer and Oracle Implementation team share responsibility for this task.

Prototyping Technique

Where appropriate, this task may be executed using an iterative prototyping technique, where configuration settings and extensible features of the application products are entered, revised and validated while working side-by-side with subject matter experts from the customer organization.

During the iterative prototyping sessions, the full set of functionality selected for implementation is partitioned into smaller subsets of that functionality. Each prototyping session then concentrates on one or more of the smaller segments to refine and validate that component of the overall solution, while taking into account any dependencies inherent in other related components. Each increment is considered in a logical order until the overall solution has been reviewed, refined and validated.

It is recommended that the initial prototyping session be used to demonstrate leading practice configuration settings and processes inherent in the products. Using the models of leading practice and experience as a guide, assist the users in determining the most appropriate parameters consistent with the organization's intended use of the system.

MC.050 – Update Setup Documentation (Core)

The purpose of this task is to document the setup options/values needed to configure the application(s) in accordance with the requirements.

Update the documentation of the setup options/values to reflect any revised setups or additional configuration requirements identified during the Configuration Validation workshops. Update the MC.040 Functional Design to reflect the changes required.

Activity/Task Group

B.TG.IF Initial Configuration

Work Product

Setup Documentation – The Setup Documentation defines the detailed setup parameters that have been shown to support the future business processes. Use the MC.040 Functional Design to prepare this work product.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Functional Design	The Functional Design contains the configuration information for the functionality that is in-scope for the project.
Validated Configuration	The Validated Configuration is the set of setup parameters, which have been shown to support the customer's intended use of the system.

Approach

When performing this task, consider the following:

- Does the Setup Documentation address mandatory or optional setups?
- Does the Setup Documentation address common setups across applications?
- Does it address navigation to the screen, justification for selected options, maintenance consolidation (if any) and date of last update?
- Does it include the impact of any setup changes in the course of the implementation?
- If possible, it is preferable for the customer to undertake these adjustments with the support of the Oracle team.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

RD.011 – Update Business Process Model (Core)

The purpose of this task is to define or update the future business process model.

Update the business process models as necessary to reflect the results of the Configuration Validation Workshops.

Activity/Task Group

B.TG.IF Initial Configuration

Work Product

Future Process Model – The Future Process Model describes the future business process that the business executes in response to triggering events as a set of one or more activities. Where pre-defined business process models exist, you should leverage them to prepare this work product.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Validated Configuration	The Validated Configuration is the set of setup parameters, which have been shown to support the customer's intended use of the system.

Approach

When performing this task, consider the following:

- Use pre-existing process models reflecting the functionality being implemented as a starting point, if available.
- Update the pre-existing process models to reflect the processes the customer will employ with the new system.
- Since the SaaS Model advocates the implementation of standard functionality, standard process models should not require modification beyond the inclusion of integrations, etc.

Roles and Responsibilities

The customer has primary responsibility for this task.

MC.063 – Conduct Configuration Familiarization/Coaching Sessions (Core)

In this task, you walk through the configuration to familiarize customer personnel with the specific configuration options and values selected and educate them on how to make changes to the configuration throughout the rest of the project, and after go-live. If appropriate, you also conduct functional and technical product coaching sessions to assist the customer's personnel in gaining a working knowledge of advanced product features and functions, as well as how to tailor its look and feel.

Activity/Task Group

B.TG.FC Configuration Familiarization and Coaching

Work Product

Configuration Familiarization/Coaching Sessions – The Configuration Familiarization/Coaching Sessions familiarize customer personnel with how to maintain the configuration, assists then in gaining a working knowledge of advanced product features and functions, and educates them on how to tailor the product's look and feel.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Validated Configuration	The Validated Configuration is the set of setup parameters, which have been shown to support the customer's intended use of the system.
Setup Documentation	The Setup Documentation defines the detailed setup parameters that have been shown to support the future business processes.

Approach

When performing this task, consider the following:

- The configuration at the conclusion of the Configuration Validation Workshops serves as a baseline for the configuration moving forward.
- Are there appropriate controls in place regarding who is able to make changes to the configuration?
- Have guidelines been established and communicated regarding when approvals are necessary prior to a change being made and who must approve them?
- Schedule and conduct applicable coaching sessions for advanced product features and functions, such as workflow, scripting, and data import, etc.
- Schedule and conduct applicable coaching sessions related to tailoring the product's look and feel, such as Customer Portal web framework, etc.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

CV.027 – Perform Data Mapping (Optional)

The purpose of this task is to perform a data mapping.

Create a detailed conversion mapping from the source legacy system to the target application and an extract file layout to be used for extraction of the data from the source system.

Δ Custom data loads or custom integrations are in-scope for the project.

Activity/Task Group

B.TG.DL Load and Validate Data - Configure

Work Product

Data Mapping – The Data Mapping defines the key assumptions, mapping between source and target, and mapping rules and logic that is needed to create the conversions and interfaces necessary to support the solution. It is intended to provide the developer with the necessary information for writing accurate conversion, transformation and load logic.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Technical Designs	The Technical Designs contain the detailed technical specifications for custom data loads, integrations and other extensions.

Approach

When performing this task, consider the following:

- In addition to identifying the data sources and target tables and columns, you also identify default values and validation rules.

Roles and Responsibilities

The customer and Oracle Implementation team share responsibility for this task.

CV.053 – Prepare Data for Loading (Optional)

In this task, you populate the specified data load templates, or comparable tools, with customer data from legacy systems and prepare the data for loading to the new Oracle Cloud system.

Δ If pre-built data loads, or custom data loads, are in-scope for the project, you should perform this task.

Activity/Task Group

B.TG.DL Load and Validate Data - Configure

Work Product

Prepared Data – The Prepared Data includes the customer data that's been obtained from the legacy systems and prepared for loading to the new Oracle system.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Data Mapping	The Data Mapping defines the key assumptions, mapping between source and target, and mapping rules and logic that is needed to create the conversions and interfaces necessary to support the solution. It is intended to provide the developer with the necessary information for writing accurate conversion, transformation and load logic.
Validated Configuration	The Validated Configuration is the set of setup parameters, which have been shown to support the customer's intended use of the system.

Approach

When performing this task, consider the following:

- Data should be populated in accordance with the predefined data load templates, or comparable tools.
- Data obtained from customer source systems should be cleansed prior to loading.

Roles and Responsibilities

The customer has primary responsibility for this task.

CV.065.1 – Load, Reconcile and Validate Data (Optional)

The purpose of this task is to load, reconcile and validate data.

Load customer data into the non-production environment. Initially, you convert sufficient data in each information category for test purposes, at the same time making visible any inconsistencies or inadequacy in the legacy data.

Δ If pre-built data loads, or custom data loads, are in-scope for the project, you should perform this task.

Activity/Task Group

B.TG.DL Load and Validate Data - Configure

Work Product

Validated Data – The Validated Data is the customer data that has been loaded to the non-production/test environment via the data load templates or other means and validated to correctly reflect the legacy data in the format required by the new system.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Prepared Data	The Prepared Data includes the customer data that's been obtained from the legacy systems and prepared for loading to the new Oracle system.

Approach

When performing this task, consider the following:

- Problems with production data are usually invisible until the data load processes have been run.
- It is assumed that data has been cleansed, but you should look for potential data issues as part of this process.

Roles and Responsibilities

The customer and Oracle Implementation team have a shared responsibility for this task.

CV.026 – Conduct Content Strategy Session (Optional)

In this task, you conduct a workshop aimed at guiding the customer in selecting the proper content creation and management strategy for their organization. This task applies primarily to Taleo implementations, but may also be useful in other implementations requiring the preparation and loading of predefined correspondence and similar content.

Δ If content such as predefined correspondence (for example, Offer Letters), job descriptions, competence and job catalogs, or similar content, is in-scope for the project, you should perform this task.

Activity/Task Group

B.TG.CL Prepare and Load Content

Work Product

Content Strategy – The Content Strategy contains the strategy and process selected by the customer to create and manage content.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Functional Design	The Functional Design contains the configuration information for the functionality that is in-scope for the project.

Approach

When performing this task, consider the following:

- Explain the various options for creating and managing content
- Help the customer in elaborating their strategy
- Make sure the customer understands that they own the content.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

CV.066 – Prepare and Load Content (Optional)

In this task, with the implementation team's guidance, the customer prepares and loads the content in the application. This task applies primarily to Taleo implementations, but may also be useful in other implementations requiring the preparation and loading of predefined correspondence and similar content.

Δ If content such as predefined correspondence (for example, Offer Letters), job descriptions, competence and job catalogs, or similar content, is in-scope for the project, you should perform this task.

Activity/Task Group

B.TG.CL Prepare and Load Content

Work Product

Loaded Content – The Loaded Content is the predefined correspondence, job descriptions, or similar content, which has been loaded to the new Oracle system and available to users.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Content Strategy	The Content Strategy contains the strategy and process selected by the customer to create and manage content.

Approach

When performing this task, consider the following:

- Review the customer content before it is loaded.
- Demonstrate how to load the content into the zone/environment.
- Make clear that the customer should expect to load any additional content without assistance.

Roles and Responsibilities

The customer has primary responsibility for this task.

IM.050.1 – Implement Integration Packages – Oracle (Optional)

The purpose of this task is to implement custom components required for the application system.

Develop the components needed to implement the integrations documented in the Technical Designs. This task focuses on the components needed on the Oracle-side of inbound or outbound integrations.

Δ If integrations are in-scope for your project, you should perform this task.

Activity/Task Group

B.TG.IP Implement Integration Packages

Work Product

Integration Components – Oracle – The Integration Components – Oracle consist of the actual program code for the integrations identified in the Technical Designs for the Oracle-side of inbound or outbound integrations.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Technical Design	The Technical Designs contain the detailed technical specifications for custom data loads, integrations and other extensions.
Data Mapping	The Data Mapping defines the key assumptions, mapping between source and target, and mapping rules and logic that is needed to create the conversions and interfaces necessary to support the solution. It is intended to provide the developer with the necessary information for writing accurate conversion, transformation and load logic.

Approach

When performing this task, consider the following:

- Review detailed design documents.
- Code modules.
- Integrate custom modules.
- Perform initial unit tests.
- Perform initial integration tests.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

IM.050.2 – Implement Integration Packages – Customer Systems (Optional)

The purpose of this task is to implement custom components required for the application system.

Develop the components needed to implement the integrations documented in the Technical Designs. This task focuses on the components needed on the Customer Systems-side of inbound or outbound integrations.

Δ If integrations are in-scope for your project, you should perform this task.

Activity/Task Group

B.TG.IP Implement Integration Packages

Work Product

Integration Components – Customer Systems – The Integration Components – Customer Systems consist of the actual program code for the customer-side of inbound or outbound integrations.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Technical Designs	The Technical Designs contain the detailed technical specifications for custom data loads, integrations and other extensions.
Data Mapping	The Data Mapping defines the key assumptions, mapping between source and target, and mapping rules and logic that is needed to create the conversions and interfaces necessary to support the solution. It is intended to provide the developer with the necessary information for writing accurate conversion, transformation and load logic.

Approach

When performing this task, consider the following:

- Review detailed design documents.
- Code modules.
- Integrate custom modules.
- Perform initial unit tests.
- Perform initial integration tests.

Roles and Responsibilities

The customer has primary responsibility for this task.

TE.045 – Validate Integration Packages (Optional)

In this task, you validate the proper functioning of implemented integrations.

Δ

If integrations are in-scope for your project, you should perform this task.

Activity/Task Group

B.TG.IP Implement Integration Packages

Work Product

Validated Integrations – The Validated Integrations represent the implemented integrations, which have been validated to function as expected, in accordance with the design.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Integration Components – Oracle	The Integration Components – Oracle consist of the actual program code for the integrations identified in the Technical Design for the Oracle-side of inbound or outbound integrations.
Integration Components – Customer Systems	The Integration Components – Customer Systems consist of the actual program code for the customer-side of inbound or outbound integrations.

Approach

When performing this task, consider the following:

- Test the system's integration with other application systems in the non-production environment.
- Test/validate integrations in accordance with the Validation Strategy and Plan.
- Validate that integration points (interfaces) can successfully support business operations across and between application systems.
- If applicable, perform Taleo Integrations Release Management Quality Assurance review as part of this task.

Roles and Responsibilities

The customer and Oracle Implementation team have a shared responsibility for this task.

IM.050.3 – Implement Extensions (Optional)

The purpose of this task is to implement custom components required for the application system.

Prepare extensions as required, based on the Functional and Technical Designs and the Configuration Validation sessions. (This task is intended to address RightNow customizations such as End-User Pages - Custom look and feel, Customer Portal custom widgets, and RightNow Console customizations).

Δ

If extensions are in-scope for the project, you should perform this task.

Activity/Task Group

B.TG.IE Implement Extensions

Work Product

Implemented Extensions – The Implemented Extensions represent the tailored look and feel, customized navigation and integration, and/or custom widgets applied to the application per the customer's specifications.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Technical Designs	The Technical Designs contain the detailed technical specifications for custom data loads, integrations and other extensions.

Approach

When performing this task, consider the following:

- Apply basic HTML and CSS branding and styling design elements to Customer Portal pages.
- Extensions are limited to template-specific styling such as header, footer, colors, fonts, and logo.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

MC.070.2 – Implement Extensible Items (Optional)

The purpose of this task is to prepare the commercial-off-the-shelf (COTS) application environment for configuration prototyping or validation activities.

Implement the extensible features delivered with the applications as required, based on the configuration validation sessions.

Δ If Extensible items are in-scope for the project, you should perform this task.

Activity/Task Group

B.TG.IE Implement Extensions

Work Product

Configured Extensible Items – The Configured Extensible Items represent the implemented extensibility features of the application products, such as personalizations, flexfields and composer updates.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Technical Designs	The Technical Designs contain the detailed technical specifications for custom data loads, integrations and other extensions.

Approach

When performing this task, consider the following:

- Extensible items for Fusion Applications should be prepared in accordance with the Oracle Fusion Applications Extensibility Guide.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

MC.085 – Prepare Reports (Optional)

In this task, you prepare BI Publisher and other reports as required.

Δ If custom reports are in-scope for the project, you should perform this task.

Activity/Task Group

B.TG.IE Implement Extensions

Work Product

Developed Reports – The Developed Reports include BI Publisher and other reports requested by the customer.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Technical Designs	The Technical Designs contain the detailed technical specifications for custom data loads, integrations and other extensions.

Approach

When performing this task, consider the following:

- Do any of the delivered BI Publisher Reports contain the required data elements?
- Additional steps may be required to run your report.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

TE.030 – Validate Extensions (Optional)

The purpose of this task is to test custom application components on an individual basis to verify that the inputs, outputs, and processing logic of each custom application component functions without errors.

Δ If extensions are in-scope for the project, you should perform this task.

Activity/Task Group

B.TG.IE Implement Extensions

Work Product

QA Tested Extensions – QA Tested Extensions consist of the tailored look and feel, customized navigation and integration, and/or custom widgets applied to the applications, which have been confirmed to comply with established standards.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Implemented Extensions	The Implemented Extensions represent the tailored look and feel, customized navigation and integration, and/or custom widgets applied to the application per the customer's specifications.

Approach

When performing this task, consider the following:

- Obtain the results of the QA testing from the QA Testing team.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

TS.020– Define Cutover Strategy (Core)

The purpose of this task is to describe how the transition is to be made from the old system to the new system. Define your plans for taking the new system into production.

Activity/Task Group

B.TG.PC Prepare for Cutover

Work Product

Cutover Strategy – The Cutover Strategy documents how the new system is to be introduced. This work product describes the approach that is being taken to place the new system into production.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Functional Design	The Functional Design contains the configuration information for the functionality that is in-scope for the project.
Technical Designs	The Technical Designs contain the detailed technical specifications for custom data loads, integrations and other extensions.

Approach

When performing this task, consider the following:

- What is the cutover approach?
- When should cutover occur?
- What is the time window for cutover?

Roles and Responsibilities

The customer and Oracle Implementation team have a shared responsibility for this task.

TS.040 – Design Production Support Infrastructure (Core)

The purpose of this task is to identify the internal and external support resources and procedures required to support production use of the system.

Activity/Task Group

B.TG.PC Prepare for Cutover

Work Product

Production Support Infrastructure Design – The Production Support Infrastructure Design addresses the operational infrastructure (for example, Helpdesk, Self-Help Q&A's, escalation procedures, etc.) for supporting the production use of the application system.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Cutover Strategy	The Cutover Strategy documents how the new system will be introduced.

Approach

When performing this task, consider the following:

- Clarify and communicate the support processes by creating diagrammatic flows of the processes.
- Support process diagrams need to show how issues are triaged and classified, and may have alternative resolution paths depending on severity.
- Document escalation criteria and procedures.

Roles and Responsibilities

The customer and Oracle Implementation team have a shared responsibility for this task.

MC.070.3– Implement Security (Core)

The purpose of this task is to prepare the commercial-off-the-shelf (COTS) application environment for configuration prototyping or validation activities.

In this task, you configure the functional security features of the applications. You also deploy the integration feed for the users and implement the Single Sign-On protocol, as specified in the Security Strategy and Plan.

Activity/Task Group

B.TG.IS Implement Security Plan

Work Product

Implemented Security – The Implemented Security consists of the configured role-based security features of the applications and Single Sign-On operating as intended between the customer network and Oracle applications.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Security Strategy and Plan	The Security Strategy and Plan documents the strategy for addressing security requirements, as well as the information necessary to establish good controls and transaction access through configuration of the functional security features of the applications. It also identifies which Single Sign-On protocol has been selected for the implementation, the resources involved, as well all the tasks necessary for a successful implementation of Single Sign-On.

Approach

When performing this task, consider the following:

- Configure functional security and Single Sign-On in the non-production environment.
- Test configuration in the non-production environment.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

WM.055.2 – Conduct Implementation Checkpoint (Core)

In this task, you review the key work products completed during the phase with the customer, verify that the phase objectives have been met, confirm the next steps to be taken, and obtain approval to proceed with the next phase.

Activity/Task Group

B.TG.IC Implementation Checkpoint

Work Product

Implementation Checkpoint Meeting/Approval to Proceed – The Implementation Checkpoint Meeting/Approval to Proceed provides an opportunity to review the work completed during the phase with the customer, confirm the next steps and obtain the approval to proceed with the next phase of the implementation.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Validated Configuration	The Validated Configuration verifies that all setup data has been entered in accordance with the Functional Design/setup documentation and that system behavior is as expected.
Validated Data	The Validated Data is the customer data that has been loaded to the non-production/test environment and validated to correctly reflect the legacy data in the format required by the new system.
Validated Integrations	The Validated Integrations represent the implemented integrations, which have been validated to function as expected, in accordance with the design.
Cutover Strategy	The Cutover Strategy documents how the new system is to be introduced. This work product is not a plan but describes the approach that is being taken to place the new system into production.

Approach

When performing this task, consider the following:

- Have the key work products for the phase been completed and reviewed?
- Have the objectives set out for the phase been achieved?
- Have the next steps been determined and confirmed?

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

PEC.MPE.2 – Manage Project Execution (Core)

In this task, the execution of the project is managed. This includes using the policies, standards, and procedures delineated in the Project Start Up phase, performing the necessary reviews and measurements to validate that the project is being executed according to the Project Management Plan.

It also includes comparing actual performance with planned performance, analyzing variances, evaluating possible alternatives, and taking appropriate corrective action as needed.

The Manage Project Execution is made up of many *ongoing* tasks. An ongoing task is defined as a task that occurs continuously throughout a project, rather than at a specific pre-defined time. The ongoing tasks occur as needed and do not include dependencies among the tasks or with the execution method tasks.

Activity/Task Group

B.TG.PM Project Management

Work Product

Managed Project Assets – Reviewed project progress, analyzed variances and updated management plans and policies.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Project Management Plan and Established Project Infrastructure	The Project Management Plan defines the governance approach for managing the project by identifying how the project will be planned, executed, controlled, monitored and reported on. The project infrastructure includes the systems and procedures to support the execution of the project.

Approach

When performing this task, consider the following:

- Document lessons learned.
- Track project actual against the workplan.
- Identify reasons for variations between plan and actions and remedy.
- Adjust Project Workplan, staff and budget as necessary.
- Adjust project approach (PMP) as necessary.
- Review the key outputs for the phase with customer and obtain agreement or acceptance (for fixed price projects).
- Verify that phase objectives have been met and confirm next steps.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

CHAPTER

5 Validate (C) Phase

The goal of the Validate phase is to conduct an End-to-End Review of the final solution including any adjusted configurations, integrations, extensions and customer legacy data.

During the Validate phase, revised configurations required by the customer that have not previously been reviewed, are applied to the non-production environment and validated. An End-to-End Review of the final solution is conducted using established validation scripts, which have been revised to reflect the customer's configuration.

Also during the Validate phase, preparations are made to train a cadre of instructors from the customer's personnel ranks to teach the end users. One or more train-the-trainer session(s) is/are conducted to equip those selected to train the end user community in the use of the new system.

Like the Configure phase, this phase culminates with an implementation checkpoint to verify that phase objectives have been achieved and approval to proceed obtained.

Validate Phase Objectives

The objectives of the Validate phase follow:

- Apply adjusted setup changes to the non-production environment.
- Load, reconcile and validate data loads.
- Prepare users for Validation.
- Confirm solution to be migrated to Production.
- Prepare for training (customer responsibility).
- Conduct train-the-trainer sessions.

Validate Phase Task Groups

The Validate phase is comprised of the following Task Groups:

- C.TG.PR Prepare for End-to-End Review
- C.TG.DL Validate Data Load – Validate
- C.TG.ER End-to-End Review
- C.TG.DO Documentation
- C.TG.TR Prepare for Training
- C.TG.TA Execute Technical Readiness Assessment
- C.TG.IC Implementation Checkpoint
- C.TG.PM Project Management

Key Work Products

The key work products of the Validate phase are as follows:

Work Product	Description
Validated Data	The Validated Data is the customer data that has been loaded to the non-production/test environment via the data load templates or other means and validated to correctly reflect the legacy data in the format required by the new system.
End-to-End Review Results	The End-to-End Review Results are the findings of the End-to-End Review of the application system. It should validate that the applications work in a way that is consistent with what the users expect.
Trained Trainers	The Trained Trainers have learned what they need to succeed in training the end users. This knowledge covers system literacy, procedural, and business skills.

Tasks and Work Products

The tasks and work products for this phase are:

ID	Task Name	Work Product	Required
MC.070.4	Setup Applications	Configured Applications	Always
TE.027	Update Validation Scripts	Updated Validation Scripts	Always
TE.105	Prepare Users for Validation	Prepared Users	Always
CV.065.2	Load, Reconcile & Validate Data	Validated Data	Pre-built data loads, or custom data loads, are in-scope for the project.
TE.070	Conduct End-to-End Review	End-to-End Review Results	Always
DO.070	Publish User Guide (Job Aids)	User Guide	Project-specific documentation is in-scope for the project.
DO.075	Publish Admin Guide	Admin Guide	Project-specific documentation is in-scope for the project.
TR.080	Prepare for Training	Training Preparations	Training is in-scope for the project.
TR.095	Conduct Train-the-Trainer Workshops	Trained Trainers	Training is in-scope for the project.
TA.125	Execute Technical Readiness Assessment	Technical Readiness Assessment Recommendations	A Technical Readiness Assessment is in-scope for the project.
WM.055.3	Conduct Implementation Checkpoint	Implementation Checkpoint Meeting/Approval to Proceed	Always
PEC.MPE.3	Manage Project Execution	Managed Project Assets	Always

Responsibilities

The Oracle Implementation team has primary responsibility for the following tasks in this phase:

- MC.070.4 Setup Applications
- DO.070 Publish User Guide (Job Aids) (Optional)
- DO.075 Publish Admin Guide (Optional)
- WM.055.3 Conduct Implementation Checkpoint

- PEC.MPE.3 Manage Project Execution

The customer has primary responsibility for the following tasks in this phase:

- TE.027 Update Validation Scripts
- TE.105 Prepare Users for Validation
- TR.080 Prepare for Training (except where requested as an additional service from Oracle)
- TR.095 Conduct Train-the-Trainer Workshops Material (except where requested as an additional service from Oracle)

The Oracle Implementation team and the customer have a shared responsibility for the following task in this phase:

- CV.065.2 Load, Reconcile and Validate Data
- TE.070 Conduct End-to-End Review
- TA.125 Execute Technical Readiness Assessment

MC.070.4 –Setup Applications (Core)

The purpose of this task is to prepare the commercial-off-the-shelf (COTS) application environment for configuration prototyping or validation activities.

In this task, you update the configurations in the non-production environment to reflect any final changes as a result of the configuration validation sessions conducted in the Configure phase. You enter revisions to earlier setup values based on the feedback received during the Configuration Validation Workshops.

Activity/Task Group

C.TG.PR Prepare for End-to-End Review

Work Product

Configured Applications – The Configured Applications is the non-production environment, which has been updated to reflect the adjusted setup values for validation/testing in the Validate phase. It is comparable to a system test environment.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Validated Configuration	The Validated Configuration verifies that all setup data has been entered in accordance with the Functional Design/Setup Documentation and that system behavior is as expected.

Approach

When performing this task, consider the following:

- Identify revised configuration settings that have not previously been applied.
- Update the non-production environment with the revised configurations.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

TE.027 – Update Validation Scripts (Core)

In this task, you revise the validation/test scripts to align them with the final business processes.

Activity/Task Group

C.TG.PR Prepare for End-to-End Review

Work Product

Updated Validation Scripts – The Updated Validation Scripts consist of the set of test scenarios, that each includes a number of test steps, which will be executed during the End-to-End Review.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Configured Applications	The Configured Applications is the non-production environment, which has been updated to reflect the adjusted setup values for validation/testing in the Validate phase. It is comparable to a system test environment.

Approach

When performing this task, consider the following:

- The scope of the validation is described through a number of test types that are performed during the End-to-End Review, the items that should be validated, and the features that should be validated.
- Have validation scripts been updated to reflect revised configuration settings, extensions and extensible items?

Roles and Responsibilities

The customer has primary responsibility for this task.

TE.105 – Prepare Users for Validation (Core)

The purpose of this task is to provide basic training to users participating in testing.

Provide training to users programmed to participate in the End-to-End Review.

Activity/Task Group

C.TG.PR Prepare for End-to-End Review

Work Product

Prepared Users – The Prepared Users have been trained on the new system and are able to conduct the End-to-End Review for their business process area.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Configured Applications	The Configured Applications is the non-production environment, which has been updated to reflect the adjusted setup values for validation/testing in the Validate phase. It is comparable to a system test environment.
Updated Validation Scripts	The Updated Validation Scripts consist of the set of test scenarios, that each includes a number of test steps, which will be executed during the End-to-End Review.

Approach

When performing this task, consider the following:

- The training necessary for users to perform their End-to-End Review tasks.
- Instructions on how to read a validation script and how to perform the End-to-End Review.

Roles and Responsibilities

The customer has primary responsibility for this task.

CV.065.2 – Load, Reconcile and Validate Data (Optional)

The purpose of this task is to load, reconcile and validate data.

Load the extracted customer data into the non-production/test environment. You convert sufficient data in each information category for purposes of conducting the End-to-End Review, at the same time making visible any inconsistencies or inadequacy in the legacy data.

Δ If pre-built data loads, or custom data loads, are in-scope for the project, you should perform this task.

Activity/Task Group

C.TG.DL Validate Data Load - Validate

Work Product

Validated Data – The Validated Data is the customer data that has been loaded to the non-production/test environment via the data load templates or other means and validated to correctly reflect the legacy data in the format required by the new system.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Prepared Data	The Prepared Data includes the customer data that's been obtained from the legacy systems and prepared for loading to the new Oracle system.

Approach

When performing this task, consider the following:

- This task should be repeated until the data load process has been proven.
- Problems with production data are usually invisible until the data load processes have been run.
- It is assumed that data has been cleansed, but you should look for potential data issues as part of this process.

Roles and Responsibilities

The customer and Oracle Implementation team have a shared responsibility for this task.

TE.070 – Conduct End-to-End Review (Core)

The purpose of this task is to perform the system test.

Conduct an End-to-End Review by executing the validation scripts documented earlier in the project using the converted customer data.

Activity/Task Group

C.TG.ER End-to-End Review

Work Product

End-to-End Review Results – The End-to-End Review Results are the findings of the End-to-End Review of the application system. It should validate that the applications work in a way that is consistent with what the users expect.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Validated Configuration	Before the End-to-End Review can start, the configuration of the Prototype/Testing Environment must be validated.
Validated Data	After the data loads have been validated, the data is ready for use in the End-to-End Review.
Updated Validation Scripts	The Updated Validation Scripts are used when performing the End-to-End Review.
User Guide	Users should follow and validate the User Guide during the End-to-End Review, if available.

Approach

When performing this task, consider the following:

- Have final configuration settings been applied and validated?
- Has the necessary customer data been loaded to the non-production/test environment and validated?
- Have required extensions and extensible items been integrated into the non-production /test environment?
- Have validation scripts been updated to reflect revised configuration settings, extensions and extensible items?
- Due to the constraints associated with functional testing in the production environment on a SaaS project, the Conduct End-to-End Review task represents the best opportunity to conduct functional testing of the software system that will be migrated to the production environment.

Roles and Responsibilities

The customer and Oracle Implementation team have a shared responsibility for this task.

DO.070 – Publish User Guide (Job Aid) (Optional)

The purpose of this task is to publish a User Guide (or Job Aid) that defines a set of detailed procedures for using the applications.

Δ If project-specific documentation has been requested as an additional service for your project, you should perform this task.

Activity/Task Group

C.TG.DO Documentation

Work Product

User Guide – The User Guide describes a business procedure and provides detailed instructions for using the applications in response to day-to-day business events.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Future Process Model	The Future Process Model describes the future business process that the business executes in response to triggering events as a set of one or more activities.
Validated Configuration	The Validated Configuration verifies that all setup data has been entered in accordance with the Functional Design/setup documentation and that system behavior is as expected.

Approach

When performing this task, consider the following:

- The User Guide introduces the user to the purpose of procedures and then explains the detailed steps and options needed to perform the business task or transactions.
- Project documentation should be brief and concise.
- The tone of the documentation should be simple and straightforward, rather than academic or technical.
- Anticipate questions that the user may ask regarding a procedure, and answer them. As you document these procedures, compare the current and future approach and add more detailed explanations to the areas that may be confusing to a user.
- Write the documentation to the level of the targeted audience. If you are documenting a technical process, include technical details; if you are

documenting a business process, only include technical details if they are necessary to convey a concept.

- Use diagrams and charts to explain broad or complex concepts. For example, a paragraph containing many conditions may be more easily understood when the information is presented in a table or chart.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

DO.075 – Publish Admin Guide (Optional)

In this task, publish an Administrative Guide that describes administrative tasks and processes specific for the customer's implementation.

Δ If project-specific documentation has been requested as an additional service for your project, you should perform this task.

Activity/Task Group

C.TG.DO Documentation

Work Product

Admin Guide – The Admin Guide is focused at customer administrators, and describes administrative tasks and processes specific to the customer's implementation. It can contain, for example, manual data imports that need to be performed on a regular basis (for data migration) or specific checks that need to be performed in the application when a functional issue occurs on configured functionality. It does not describe standard application administration tasks.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Technical Designs	The Technical Designs contain the detailed technical specifications for custom data loads, integrations and other extensions.

Approach

When performing this task, consider the following:

- Identify the administrative tasks the customer staff will be performing when the system goes live.
- Will the customer need to use data import or export functions?
- Document the procedures and review with customer personnel.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

TR.080 – Prepare for Training (Optional)

The purpose of this task is to develop the end-user training materials.

The training materials are needed to conduct a Train-the-Trainer session for the customer personnel identified to teach the end-user community. You also establish training user accounts in the Training Environment and make other adjustments to the environment required to support training.

Δ If training is in-scope for the project, you should perform this task.

Activity/Task Group

C.TG.TR Prepare for Training

Work Product

Training Preparations – The Training Preparations consist of the materials (PowerPoint slides, UPK scripts, etc.) needed to train a cadre of customer personnel who have been designated to teach the end user community how to use the new system. It also includes system adjustments required to support training, such as the establishment of user accounts, etc.

Prerequisites

You need the following for this task:

Prerequisite	Usage
User Guide	The User Guide describes a business procedure and provides detailed instructions for using the applications in response to day-to-day business events.
Future Process Model	The Future Process Model describes the business processes that the business executes in response to triggering events as a set of one or more activities.

Approach

When performing this task, consider the following:

- The Train-the-Trainer training materials should address all standard functionality in scope for the start up packs included in the project, as well as any additional configurations and extensions.
- Tailor the existing training materials to reflect the new procedures derived from the final business processes and the extensions, if appropriate.
- The Train-the-Trainer materials are used to equip the designated trainers to be successful in training the end user community.
- If necessary, update the Training Environment configuration to include user accounts and other adjustments required to support the training sessions.

- If required, have the customer translate the training materials for each language in scope for the current release.

Roles and Responsibilities

The customer generally has primary responsibility for this task. However, the Oracle Implementation team may take responsibility for this task, if requested as an additional service from Oracle.

TR.095 – Conduct Train-the-Trainer Workshops (Optional)

In this task, you train the customer personnel who will be training the end users.

Δ If training is in-scope for the project, you should perform this task.

Activity/Task Group

C.TG.TR Prepare for Training

Work Product

Trained Trainers – The Trained Trainers have learned what they need to succeed in training the end users. This knowledge covers system literacy, procedural, and business skills.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Training Preparations	Training Preparations consist of the materials (PowerPoint slides, UPK scripts, etc.) needed to train a cadre of customer personnel who have been designated to teach the end user community how to use the new system. It also includes system adjustments required to support training, such as the establishment of user accounts, etc.

Approach

When performing this task, consider the following:

- Monitor the pulse and progress of the train-the-trainer events as they unfold, to make sure that the momentum and quality are maintained.
- Ensure the training content is being absorbed by the students and that the revised business processes are understood.

Roles and Responsibilities

It is advisable that the customer have primary responsibility for this task. However, the Oracle Implementation team may take responsibility for this task, if requested as an additional service from Oracle.

TA.125 – Execute Technical Readiness Assessment (Optional)

In this task, the customer conducts the Technical Readiness Assessment with guidance from the implementation team.

Δ

> If a Technical Readiness Assessment is in-scope for the project, you should perform this task.

Activity/Task Group

C.TG.TA Execute Technical Readiness Assessment

Work Product

Technical Readiness Assessment Recommendations – The Technical Readiness Assessment Recommendations consists of changes that should be made to the customer's network in order to get a better performance from the Oracle applications.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Technical Readiness Assessment Project Plan	The Technical Readiness Assessment Project Plan defines when the assessments will be performed and when you can start reviewing the results.

Approach

When performing this task, consider the following:

- Perform the assessments.
- Capture the result of the assessments.
- Evaluate the results.
- Document the recommendations.
- Share the recommendations with the customer.

Roles and Responsibilities

The customer and Oracle Implementation team have a shared responsibility for this task.

WM.055.3 – Conduct Implementation Checkpoint (Core)

In this task, you review the key work products completed during the phase with the customer, verify that the phase objectives have been met, confirm the next steps to be taken, and obtain approval to proceed with the next phase.

Activity/Task Group

C.TG.IC Implementation Checkpoint

Work Product

Implementation Checkpoint Meeting/Approval to Proceed – The Implementation Checkpoint Meeting/Approval to Proceed provides an opportunity to review the work completed during the phase with the customer, confirm the next steps and obtain the approval to proceed with the next phase of the implementation.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Validated Data	The Validated Data is the customer data that has been loaded to the non-production/test environment via the data load templates or other means and validated to correctly reflect the legacy data in the format required by the new system.
End-to-End Review Results	The End-to-End Review Results is the application system that has been reviewed to verify that the applications work in a way that is consistent with what the users expect.
Trained Trainers	The Trained Trainers have learned what they need to succeed in training the end users. This knowledge covers system literacy, procedural, and business skills.

Approach

When performing this task, consider the following:

- Have the key work products for the phase been completed and reviewed?
- Have the objectives set out for the phase been achieved?
- Have the next steps been determined and confirmed?
- Has the product release schedule been communicated?

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task although they must be supported by the customer at this stage to increase the likelihood of successful production transition.

PEC.MPE.3 – Manage Project Execution (Core)

In this task, the execution of the project is managed. This includes using the policies, standards, and procedures delineated in the Project Start Up phase, performing the necessary reviews and measurements to validate that the project is being executed according to the Project Management Plan.

It also includes comparing actual performance with planned performance, analyzing variances, evaluating possible alternatives, and taking appropriate corrective action as needed.

The Manage Project Execution is made up of many *ongoing* tasks. An ongoing task is defined as a task that occurs continuously throughout a project, rather than at a specific pre-defined time. The ongoing tasks occur as needed and do not include dependencies among the tasks or with the execution method tasks.

Activity/Task Group

C.TG.PM Project Management

Work Product

Managed Project Assets – Reviewed project progress, analyzed variances and updated management plans and policies.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Project Management Plan and Established Project Infrastructure	The Project Management Plan defines the governance approach for managing the project by identifying how the project will be planned, executed, controlled, monitored and reported on. The project infrastructure includes the systems and procedures to support the execution of the project.

Approach

When performing this task, consider the following:

- Adjust Project Workplan, staff and budget as necessary.
- Document lessons learned.
- Track project actuals against the workplan.
- Identify reasons for variations and remedy accordingly.
- Adjust project approach (PMP) as necessary.
- Review the key outputs for the phase with customer and obtain agreement or acceptance (for fixed price projects).
- Verify that phase objectives have been met and confirm next steps.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

CHAPTER

6 Transition (D) Phase

The goal of the Transition phase is to deploy the new system into the organization. All the elements must come together to transition successfully to active production use.

During Transition, the configuration that was validated during the Validate phase is moved to the Production Environment and customer legacy data is loaded, reconciled and validated.

A final validation review is conducted with users and stakeholders to verify that the system is ready for production use, an assessment is made of operational readiness, and the phase culminates with the new system being placed into use.

Transition Phase Objectives

The objectives of the Transition phase follow:

- Configure the Production Environment.
- Migrate integrations and extensions to the Production Environment.
- Load, reconcile and validate data loads in the Production Environment.
- Conduct Final Validation Review.
- Verify Production and Operational Readiness.
- Begin production use of the system.

Transition Phase Task Groups

The Validate phase is comprised of the following Task Groups:

- D.TG.PT Prepare for Transition
- D.TG.FV Final Validation
- D.TG.TR Training
- D.TG.TS Transition to Production
- D.TG.IC Implementation Checkpoint
- D.TG.PM Project Management

Key Work Products

The key work products of the Transition phase are as follows:

Work Product	Description
Validated Production Environment	The Validated Production Environment is the production system which has been through a final review by the customer to ensure its' readiness for production use.
Production Ready System	The Production Ready System consists of checklists and optionally a quality assurance review that allows you to verify production readiness.
System in Production	The System in Production is a system for which you have verified that all aspects of the system are operational and production use is achieved.

Tasks and Work Products

The tasks and work products for this phase are:

ID	Task Name	Work Product	Required When
TS.045	Remove Test Data from Production	Clean Production Environment	Production Environment must be cleansed of test data.
TS.050	Migrate Configuration to Production	Configured Production Environment	Always
TS.051	Migrate Integrations and Extensions to Production	Integrations and Extensions in Production	Integrations and extensions are in-scope for the project.
CV.065.3	Load, Reconcile and Validate Data Loads in Production	Validated Data	Pre-built data loads, or custom data loads, are in-scope for the project.
TE.120	Conduct Final Validation Review with Users & Stakeholders	Validated Production Environment	Always
TR.100	Conduct End-User Training	Skilled Users	Training is in-scope for the project
TS.052	Implement Production Support Infrastructure	Production Support Infrastructure	Always
TS.058	Verify Production and Operational Readiness	Production Ready System	Always
TS.060	Begin Production Use	System in Production	Always
WM.055.4	Conduct Implementation Checkpoint	Implementation Checkpoint Meeting/Approval to Proceed	Always
PEC.MPE.4	Manage Project Execution	Managed Project Assets	Always

Responsibilities

The Oracle Implementation team has primary responsibility for the following tasks in this phase:

- WM.055.4 Conduct Implementation Checkpoint
- PEC.MPE.4 Manage Project Execution

The customer has primary responsibility for the following tasks in this phase:

- TR.100 Conduct End User Training
- TS.052 Implement Production Support Infrastructure
- TS.058 Verify Production and Operational Readiness
- TS.060 Begin Production Use

The Oracle Implementation team and the customer have a shared responsibility for the following tasks in this phase:

- TS.045 Remove Test Data from Production
- TS.050 Migrate Configuration to Production
- TS.051 Migrate Integrations and Extensions to Production
- CV.065.3 Load, Reconcile and Validate Data Loads in Production
- TE.120 Conduct Final Validation Review with Users and Stakeholders

TS.045 – Remove Test Data from Production (Optional)

In this task, you remove test data from the Production Environment.

Δ For Taleo implementations only, if the Production Environment must be cleansed of test data, you should perform this task.

Activity/Task Group

D.TG.PT Prepare for Transition

Work Product

Clean Production Environment – The Clean Production Environment is the Production Environment, which has been cleansed of test data and ready for the customer to use.

Prerequisites

You need the following for this task:

Prerequisite	Usage
End-to-End Review Results	The End-to-End Review Results is the application system that has been reviewed to verify that the applications work in a way that is consistent with what the users expect.

Approach

When performing this task, consider the following:

- This task applies only to Taleo implementations where test data may have been entered into the Production Environment/zone. For all other products, you should refrain from conducting any testing in the Production Environment, as there is no provision for removing it.
- Remove any data or content that is not required in the Production Environment.

Roles and Responsibilities

The customer and Oracle Implementation team have a shared responsibility for this task.

TS.050 – Migrate Configuration to Production (Core)

The purpose of this task is to set up, configure and install the database and application software for the production environment.

Migrate the Validated Configuration to the production environment.

Activity/Task Group

D.TG.PT Prepare for Transition

Work Product

Configured Production Environment – The Configured Production Environment is complete once the application setups are applied to the production environment.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Setup Documentation	The Setup Documentation defines the detailed setup parameters that have been shown to support the future business processes.
End-to-End Review Results	The End-to-End Review Results are the findings of the End-to-End Review of the application system. It should validate that the applications work in a way that is consistent with what the users expect.

Approach

When performing this task, consider the following:

- Use the setup documentation and applicable tools, such as Fusion Functional Setup Manager, as appropriate to configure the production environment with the validated and reviewed configuration values.
- Review the setups in the production environment to ensure that they have been migrated correctly.
- Involve the customer in reviewing the setups in production.

Roles and Responsibilities

The customer and Oracle Implementation team have a shared responsibility for this task.

TS.051 – Migrate Integrations and Extensions to Production (Optional)

In this task, you migrate the validated integrations and extensions to the production environment.

Δ If integrations and extensions are in-scope for the project, you should perform this task.

Activity/Task Group

D.TG.PT Prepare for Transition

Work Product

Integrations and Extensions in Production – The Integrations and Extensions in Production represent the validated integrations and extensions, which have been implemented in the production environment.

Prerequisites

You need the following for this task:

Prerequisite	Usage
End-to-End Review Results	The End-to-End Review Results are the findings of the End-to-End Review of the application system. It should validate that the applications work in a way that is consistent with what the users expect.

Approach

When performing this task, consider the following:

- Enable all validated integrations and extensions in the production environment.

Roles and Responsibilities

The customer and Oracle Implementation team have a shared responsibility for this task.

CV.065.3 – Load, Reconcile and Validate Data Loads in Production (Optional)

The purpose of this task is to load, reconcile and validate data.

Load the extracted customer data into the production environment.

Δ If pre-built data loads, or custom data loads, are in-scope for the project, you should perform this task.

Activity/Task Group

D.TG.PT Prepare for Transition

Work Product

Validated Data – The Validated Data is the customer data that has been loaded to the production environment via the data load templates or other means and validated to correctly reflect the legacy data in the format required by the new system.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Prepared Data	The Prepared Data provide the extracted customer data in the format required by the new system.
Validated Data	The validated data from the Validate phase reflects the successful completion and validation of uploaded customer data from the previous trial data load.

Approach

When performing this task, consider the following:

- During the Transition phase, the initial load of the production database is typically carried out after the production environment is set up.
- A checklist and log of the data loads that were executed on the production database should be provided and the correctness of the loads should be verified.

Roles and Responsibilities

The customer and Oracle Implementation team have a shared responsibility for this task.

TE.120 – Conduct Final Validation Review with Users and Stakeholders (Core)

The purpose of this task is to support the users in reviewing and accepting the system.

Do a final review of the Configured Production Environment with users and stakeholders to validate that the configuration has been migrated correctly, and that all required customer data, integrations and extensions are in place.

Though the purpose of this task is to validate that all of the required functionality is ready for use in the new production system, it does not include a trial production run involving entry of data, or processing of transactions.

Be careful not to enter any test data into the production environment during the final validation review, unless you have previously made provisions for its removal, as may be the case for certain Taleo implementations. Oracle Cloud Operations does not perform backup or restore operations on demand, so backing out test data by restoring a “clean” backup is not an option.

Activity/Task Group

D.TG.FV Final Validation

Work Product

Validated Production Environment – The Validated Production Environment represents the final review of the production environment by the customer to ensure its’ readiness for use.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Configured Production Environment	The Configured Production Environment is complete once the application setups are applied to the production environment.
Integrations and Extensions in Production	The Integrations and Extensions in Production represent the validated integrations and extensions, which have been implemented in the production environment.
Validated Data	The Validated Data is the customer data that has been loaded to the production environment via the data load templates or other means and validated to correctly reflect the legacy data in the format required by the new system.

Approach

When performing this task, consider the following:

- Has the previously validated configuration been migrated to the production environment correctly?

- Have the previously validated integrations and extensions been migrated to the production environment as required?
- Has all required data been migrated to the production environment and validated?
- Have acceptance criteria been established?
- Does the production environment meet the acceptance criteria?

Roles and Responsibilities

The customer and Oracle Implementation team have a shared responsibility for this task.

TR.100 – Conduct End-User Training (Optional)

The purpose of this task is to conduct learning events for the end users.

Customer trainers provide training in the use of the system to the other end users.

Δ If training is in-scope for the project, you should perform this task.

Activity/Task Group

D.TG.TR Training

Work Product

Skilled Users – Users have learned what they need to succeed in their new roles. This knowledge covers system literacy, procedural, and business skills.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Training Preparations	Training Preparations include system adjustments required to support training, such as the establishment of user accounts, etc.
Trained Trainers	The customer Trainers will deliver the training to the end users.

Approach

When performing this task, consider the following:

- What specific tasks each group of users will need to perform on the system?
- Pay special attention to how the users' daily tasks will change, especially if the related business process has been updated.
- Be sensitive to the fact that some users will welcome the change, whilst others may initially be resistant to change.
- Be sensitive to the fact that some users might find being in a Training Environment disconcerting.

Roles and Responsibilities

The customer has primary responsibility for this task.

TS.052 – Implement Production Support Infrastructure (Core)

The purpose of this task is to activate the support personnel and procedures for the new business system and review requirements for support-related services from software suppliers, contractors, help desks, and other support services.

Activity/Task Group

D.TG.TS Transition to Production

Work Product

Production Support Infrastructure - The Production Support Infrastructure addresses call and response tracking, links to external support mechanisms or sources and the understanding of performance metrics by support personnel (response, history retention, follow-up, accuracy, audit, etc.).

Prerequisites

You need the following for this task:

Prerequisite	Usage
Production Support Infrastructure Design	The Production Support Infrastructure Design addresses the operational infrastructure (for example, Helpdesk, Self-Help Q&A's, escalation procedures, etc.) for supporting the production use of the application system.

Approach

When performing this task, consider the following:

- It is important to rehearse the support procedures. You can simulate various types of support calls and evaluate whether the expected response time, accuracy of the resolutions, and the general flow of the process are adequate to support the request volume. This is also a good opportunity to test default support mechanisms, after-business-hours support, and supplier support hotlines.
- The establishment of a robust and capable internal and vendor external support infrastructure is critical to the success of the project.
- The support team needs to be aware of the Oracle Cloud Operations support processes.

Roles and Responsibilities

The customer has primary responsibility for this task.

TS.058 – Verify Production and Operational Readiness (Core)

The purpose of this task is to verify that all users are ready to use the system and all required operational procedures are in place.

Activity/Task Group

D.TG.TS Transition to Production

Work Product

Production Ready System – The Production Ready System consists of checklists and optionally, a quality assurance review that allows you to verify production readiness.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Validated Production Environment	The Validated Production Environment represents the final review of the production environment by the customer to ensure its' readiness for use. It is comparable to a User Acceptance, in that it effectively represents the customer's willingness to proceed with system use.

Approach

When performing this task, consider the following:

- Key users should have gone through the production environment setup and data to confirm that every screen can be accessed and all reports print successfully?
- Have all testing activities been successfully closed?
- Have users been trained and are they ready to use the new system in the execution of their responsibilities?
- Is the necessary support infrastructure in place?
- Has the product release schedule been communicated?

Roles and Responsibilities

The customer has primary responsibility for this task.

TS.060 – Begin Production Use (Core)

Te purpose of this task is to begin production use of the new system.

Activity/Task Group

D.TG.TS Transition to Production

Work Product

System in Production – The System in Production is a system for which you have verified that all aspects of the system are operational and active use is achieved.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Production and Operational Readiness Verification	The Production and Operational Readiness Verification consists of checklists and optionally a quality assurance review that allows you to verify production readiness.
Production Support Infrastructure	The Production Support Infrastructure addresses call and response tracking, links to external support mechanisms or sources and the understanding of performance metrics by support personnel (response, history retention, follow-up, accuracy, audit, etc.).

Approach

When performing this task, consider the following:

- The best way to begin using the new system is to control the initial transactions and entries; in terms of volume and manual integration (for example, it is advisable not to load a large interface file as the first transaction).
- Bring up departments or sets of related transactions in sequence to permit focused attention on limited areas until they are stabilized.

Roles and Responsibilities

The customer has primary responsibility for this task, although it is strongly advised that the Oracle team closely support the customer at this time.

WM.055.4 – Conduct Implementation Checkpoint (Core)

In this task, you review the key work products completed during the phase with the customer, verify that the phase objectives have been met, confirm the next steps to be taken, and obtain approval to proceed with the next phase.

Activity/Task Group

D.TG.IC Implementation Checkpoint

Work Product

Implementation Checkpoint Meeting/Approval to Proceed – The Implementation Checkpoint Meeting/Approval to Proceed provides an opportunity to review the work completed during the phase with the customer, confirm the next steps and obtain the approval to proceed with the next phase of the implementation.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Validated Production Environment	The Validated Production Environment is the production system which has been through a final review by the customer to ensure its' readiness for production use.
Production Ready System	The Production Ready System consists of checklists and optionally a quality assurance review that allows you to verify production readiness.
System in Production	The System in Production is a system for which you have verified that all aspects of the system are operational and production use is achieved.

Approach

When performing this task, consider the following:

- Have the key work products for the phase been completed and reviewed?
- Have the objectives set out for the phase been achieved?
- Have the next steps been determined and confirmed?

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

PEC.MPE.4 – Manage Project Execution (Core)

In this task, the execution of the project is managed. This includes using the policies, standards, and procedures delineated in the Project Start Up phase, performing the necessary reviews and measurements to validate that the project is being executed according to the Project Management Plan.

It also includes comparing actual performance with planned performance, analyzing variances, evaluating possible alternatives, and taking appropriate corrective action as needed.

The Manage Project Execution is made up of many *ongoing* tasks. An ongoing task is defined as a task that occurs continuously throughout a project, rather than at a specific pre-defined time. The ongoing tasks occur as needed and do not include dependencies among the tasks or with the execution method tasks.

Activity/Task Group

D.TG.PM Project Management

Work Product

Managed Project Assets – Reviewed project progress, analyzed variances and updated management plans and policies.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Project Management Plan and Established Project Infrastructure	The Project Management Plan defines the governance approach for managing the project by identifying how the project will be planned, executed, controlled, monitored and reported on. The project infrastructure includes the systems and procedures to support the execution of the project.

Approach

When performing this task, consider the following:

- Adjust Project Workplan, staff and budget as necessary.
- Document lessons learned.
- Track project actual against the workplan.
- Identify any variations and respond accordingly.
- Adjust project approach (PMP) as necessary.
- Review the key outputs for the phase with customer and obtain agreement or acceptance (for fixed price projects).
- Verify that phase objectives have been met and confirm next steps.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

CHAPTER

7 Realization (E) Phase

The goal of the Realization phase is to effectively manage the transition to steady-state operations, close the project from an administrative and contractual standpoint and plan for the next release.

The Realization phase marks the last phase of the implementation and the beginning of the system support cycle. During this phase, system use is monitored, necessary actions taken in response to issues raised by users, and a hand off conducted to the team responsible for the ongoing customer relationship.

The phase culminates with acceptance of the new system by the customer and closing out of the contract and project management processes by the project manager.

Realization Phase Objectives

The objectives of the Realization phase follow:

- Manage transition to Steady-State Operations.
- Provide Post Go-Live Support.
- Conduct a handoff to the ongoing Customer Relationship Management Team.
- Validate that the project work products are complete.
- Gain final sign-off.
- Collect documents for reuse and retention.
- Document lessons learned.
- Close contract and processes.

Realization Phase Task Groups

The Realization phase is comprised of the following Task Groups:

- E.TG.SP Stabilization
- E.TG.TC Transition to Customer Relationship Manager
- E.TG.PM Project Management
- E.TG.PC Project Closure

Key Work Products

The key work products of the Realization phase are as follows:

Work Product	Description
Steady-State Operations	Steady-State Operations exist when the system has achieved a stable state. Daily use of the system has become routine and disruptions that may have characterized the initial stage of operation have receded.
Customer Relationship Manager Handoff	The Customer Relationship Manager Handoff begins the process of assisting the customer in taking full advantage of the investment in Oracle technology and building the trust that is key to a long term association.
Final Acceptance Certificate	The Final Acceptance Certificate verifies that the contracted project scope was delivered.
Closed Processes and Contract	The Closed Processes and Contract closes the contract and the project processes for each of the project management processes.

Tasks and Work Products

The tasks and work products for this phase are:

ID	Task Name	Work Product	Required
PS.005	Manage Transition to Steady-State Operations	Steady-State Operations	Always
PS.065	Post Go-Live Support	Post Go-Live Support	Always
PS.070	Execute Handoff to Customer Relationship Manager	Customer Relationship Manager Handoff	A Customer Relationship Manager (for example, Customer Success Specialist) or comparable resource is assigned to the customer.
PEC.MPE.5	Manage Project Execution	Managed Project Assets	Always
PC.GA	Gain Acceptance	Final Acceptance Certificate	Always
PC.CPC	Closer Processes and Contract	Closed Processes and Contract	Always

Responsibilities

The Oracle Implementation team has primary responsibility for the following tasks in this phase:

- PS.065 Post Go-Live Support
- PS.070 Execute Handoff to Customer Relationship Manager
- PEC.MPE.5 Manage Project Execution
- PC.GA Gain Acceptance
- PC.CPC Close Processes and Contract

The Oracle Implementation team and the customer have a shared responsibility for the following tasks in this phase:

- PS.005 Manage Transition to Steady-State Operations

PS.005 – Manage Transition to Steady-State Operations (Core)

In this task, you monitor the customer's transition to routine operations and assist as necessary to achieve steady-state operations.

Activity/Task Group

E.TG.SP Stabilization

Work Product

Steady-State Operations – Steady-State Operations exist when the system has achieved a stable state. Daily use of the system has become routine and disruptions that may have characterized the initial stage of operation have receded.

Prerequisites

You need the following for this task:

Prerequisite	Usage
System in Production	The System in Production is the system, which has been placed into active operation.

Approach

When performing this task, consider the following:

- Have users been adequately trained on the use of the new system to perform their functions?
- Is there a clearly communicated process for reporting issues and escalating them, if necessary?
- Are follow-on releases planned, or are there enhancements that would contribute to improved operations?

Roles and Responsibilities

The customer and Oracle Implementation team have a shared responsibility for this task.

PS.065 – Post Go-Live Support (Core)

In this task, you provide Post Go-Live Support as specified in the contract.

Activity/Task Group

E.TG.SP Stabilization

Work Product

Post Go-Live Support – Post Go-Live Support consists of monitoring and responding to problems and issues throughout the post-production support period, as specified in the contract.

Prerequisites

You need the following for this task:

Prerequisite	Usage
System in Production	The System in Production is the system, which has been placed into active operation.

Approach

When performing this task, consider the following:

- Create a system or process to effectively maintain the production system and respond to users' requests.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

PS.070 – Execute Handoff to Customer Relationship Manager (Optional)

In this task, you conduct a meeting with the customer relationship manager (aka customer success specialist), or comparable resource, who will be assuming responsibility for the customer relationship following completion of the implementation.

Δ If a customer relationship manager (aka, customer success specialist) or comparable resource is assigned to the customer, you should perform this task.

Activity/Task Group

E.TG.TC Transition to Customer Relationship Manager

Work Product

Customer Relationship Manager Handoff – The Customer Relationship Manager Handoff begins the process of assisting the customer in taking full advantage of the investment in Oracle technology and building the trust that is key to a long term association.

Prerequisites

You need the following for this task:

Prerequisite	Usage
System in Production	The System in Production is the system, which has been placed into active operation.

Approach

When performing this task, consider the following:

- Has the customer relationship manager (for example, customer success specialist or managed services representative) been introduced to the key stakeholders for the project?
- Has the customer relationship manager been provided with the background on the company and an overview of the project?
- Have you communicated possible enhancements the customer might be interested in to the customer relationship manager?

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

PEC.MPE.5 – Manage Project Execution (Core)

In this task, the execution of the project is managed. This includes using the policies, standards, and procedures delineated in the Project Start Up phase, performing the necessary reviews and measurements to validate that the project is being executed according to the Project Management Plan.

It also includes comparing actual performance with planned performance, analyzing variances, evaluating possible alternatives, and taking appropriate corrective action as needed.

The Manage Project Execution is made up of many *ongoing* tasks. An ongoing task is defined as a task that occurs continuously throughout a project, rather than at a specific pre-defined time. The ongoing tasks occur as needed and do not include dependencies among the tasks or with the execution method tasks.

Activity/Task Group

E.TG.PM Project Management

Work Product

Managed Project Assets – Reviewed project progress, analyzed variances and updated management plans and policies.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Project Management Plan and Established Project Infrastructure	The Project Management Plan defines the governance approach for managing the project by identifying how the project will be planned, executed, controlled, monitored and reported on. The project infrastructure includes the systems and procedures to support the execution of the project.

Approach

When performing this task, consider the following:

- Document lessons learned.
- Track project actual.
- Adjust Project Workplan, staff and budget as necessary.
- Adjust project approach (PMP) as necessary.
- Review the key outputs for the phase with customer and obtain agreement or acceptance (for fixed price projects).
- Verify that phase objectives have been met and confirm next steps.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

PC.GA – Gain Acceptance (Core)

In this task, you validate the project scope was delivered per the contract.

Activity/Task Group

E.TG.PC Project Closure

Work Product

Final Acceptance Certificate – The Final Acceptance Certificate verifies that the contracted project scope was delivered.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Contract and associated documentation	Review the contract for the contract scope in order to validate that the contractual scope was delivered in the course of the project.

Approach

When performing this task, consider the following:

- Validate with customer that project scope was delivered.
- If Fixed Price, gain acceptance from the customer on the overall project. (Note: Make sure that customer acceptance is documented on all outstanding project work products.)

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

PC.CPC – Close Processes and Contract (Core)

In this task, the contract and the project processes for each of the project management processes are closed.

Before the processes are closed**,** the project manager should review them for potential future enhancements. This information is valuable to plan for future system enhancements and to begin this dialog with the customer.

During this task, the project is archived following specified procedures.

The project manager is also responsible for performing a retrospective of the project and documenting lessons learned.

Additionally, it is important for the project manager to identify customer reference opportunities and ask for the customer reference before closing the project.

Activity/Task Group

E.TG.PC Project Closure

Work Product

Closed Processes and Contract – The Closed Processes and Contract closes the contract and the project processes for each of the project management processes.

Prerequisites

You need the following for this task:

Prerequisite	Usage
Final Acceptance Certificate	The Final Acceptance Certificate verifying that the contracted project scope was delivered.

Approach

When performing this task, consider the following:

- Release staff.
- Close Project Processes (Project Financials, Issue, Risk, and Problem logs, and other infrastructure-related processes).
- Close Contract.
- Document Lessons Learned.
- Archive project documentation following project archiving standards and guidelines.
- Submit final reports such as the Project Summary or similar documents such as the Customer Summary or Customer Results documents.
- Submit Good News Database Submission.
- Receive customer reference.

- Plan for the next release.

Roles and Responsibilities

The Oracle Implementation team has primary responsibility for this task.

APPENDIX

A Work Breakdown Structure

This appendix provides the work breakdown structure (WBS) for the Cloud Application Services OUM approach.

How to Read the Work Breakdown Structure

The CAS OUM WBS is comprised of three elements: phases, activities/task groups, and tasks. Each element is indicated graphically as shown in the following legend:

A	**Design**	Phase
A.TG.TR	**Prepare Project Team**	Activity/Task Group
STM.050	♦Conduct Customer Kickoff Meeting	Task

Cloud Application Services OUM WBS

The following is a work breakdown structure for the CAS OUM approach.

Phase	Activity/Task Group	Task ID	Task Name	Work Product	Core/Optional

Phase	Activity/Task Group	Task ID	Task Name	Work Product	Core/Optional
Project Design [A]					
	(A.TG.PSU) Project Start Up				
		PSU.RCSWB	Review Contract, Scope, Workplan and Budget	Reviewed Contract, Scope, Workplan and Budget	Core
		PSU.RPAC	Review Project Approach with Customer and confirm Customer Readiness	Confirmed Customer Readiness	Core
		PSU.EGSI	Establish Governance and Supporting Infrastructure	Project Management Plan and Established Project Infrastructure	Core
	(A.TG.TR) Prepare Project Team				
		STM.050	Conduct Customer Kickoff Meeting	Kickoff Meeting	Core
		TR.050	Train Project Team	Trained Project Team	Optional
		WM.070	Schedule Workshops	Workshop Schedule	Core
	(A.TG.FT) Conduct Functional and Technical Design Workshops				
		MC.040	Conduct Functional Design Workshops	Functional Design	Core
		DS.145	Conduct Technical Design Workshops	Technical Designs	Optional
		DS.160	Conduct Design Reviews	Approved Designs	Core
	(A.TG.SP) Security Planning				
		MC.060	Develop Security Strategy and Plan	Security Strategy and Plan	Core
	(A.TG.VP) Validation Planning				
		TE.010	Define Validation Strategy and Plan	Validation Strategy and Plan	Core
	(A.TG.DO) Documentation				
		DO.010	Define Documentation Requirements and Strategy	Documentation Requirements and Strategy	Optional
	(A.TG.TA) Technical Readiness Assessment Kickoff				
		TA.010	Conduct Technical Readiness Assessment Kickoff Meeting	Technical Readiness Assessment Project Plan	Optional

Phase	Activity/Task Group	Task ID	Task Name	Work Product	Core/Optional
	(A.TG.IC) Implementation Checkpoint				
		WM.055.1	Conduct Implementation Checkpoint	Implementation Checkpoint Meeting/Approval to Proceed	Core
	(A.TG.PM) Project Management				
		PEC.MPE.1	Manage Project Execution	Managed Project Assets	Core
Configure [B]					
	(B.TG.IF) Initial Configuration				
		MC.070.1	Setup Applications	Configured Applications	Core
		TE.025	Prepare Validation Scripts	Validation Scripts	Core
		MC.080	Conduct Configuration Validation Workshops	Validated Configuration	Core
		MC.050	Update Setup Documentation	Setup Documentation	Core
		RD.011	Update Business Process Model	Future Process Model	Core
	(B.TG.FC) Configuration Familiarization and Coaching				
		MC.063	Conduct Configuration Familiarization/Coaching Sessions	Configuration Familiarization/Coaching Sessions	Core
	(B.TG.DL) Load and Validate Data - Configure				
		CV.027	Perform Data Mapping	Data Mapping	Optional
		CV.053	Prepare Data for Loading	Prepared Data	Optional
		CV.065.1	Load, Reconcile and Validate Data	Validated Data	Optional
	(B.TG.CL) Prepare and Load Content				
		CV.026	Conduct Content Strategy Session	Content Strategy	Optional
		CV.066	Prepare and Load Content	Loaded Content	Optional
	(B.TG.IP) Implement Integration Packages				
		IM.050.1	Implement Integration Packages - Oracle	Integration Components - Oracle	Optional
		IM.050.2	Implement Integration Packages - Customer Systems	Integration Components – Customer Systems	Optional

Phase	Activity/Task Group	Task ID	Task Name	Work Product	Core/Optional
		TE.045	Validate Integration Packages	Validated Integrations	Optional
	(B.TG.IE) Implement Extensions				
		IM.050.3	Implement Extensions	Implemented Extensions	Optional
		MC.070.2	Implement Extensible Items	Configured Extensible Items	Optional
		MC.085	Prepare Reports	Developed Reports	Optional
		TE.030	Validate Extensions (QA Testing)	QA Tested Extensions	Optional
	(B.TG.PC) Prepare for Cutover				
		TS.020	Define Cutover Strategy	Cutover Strategy	Core
		TS.040	Design Production Support Infrastructure	Production Support Infrastructure Design	Core
	(B.TG.IS) Implement Security Plan				
		MC.070.3	Implement Security	Implemented Security	Core
	(B.TG.IC) Implementation Checkpoint				
		WM.055.2	Conduct Implementation Checkpoint	Implementation Checkpoint Meeting/Approval to Proceed	Core
	(B.TG.PM) Project Management				
		PEC.MPE.2	Manage Project Execution	Managed Project Assets	Core
Validate [C]					
	(C.TG.PR) Prepare for End-to-End Review				
		MC.070.4	Setup Applications	Configured Applications	Core
		TE.027	Update Validation Scripts	Updated Validation Scripts	Core
		TE.105	Prepare Users for Validation	Prepared Users	Core
	(C.TG.DL) Validate Data Load – Validate				
		CV.065.2	Load, Reconcile & Validate Data	Validated Data	Optional
	(C.TG.ER) End-to-End Review				
		TE.070	Conduct End-to-End Review	End-to-End Review Results	Core

Phase	Activity/Task Group	Task ID	Task Name	Work Product	Core/Optional
	(C.TG.DO) Documentation				
		DO.070	Publish User Guide (Job Aid)	User Guide	Optional
		DO.075	Publish Admin Guide	Admin Guide	Optional
	(C.TG.TR) Prepare for Training				
		TR.080	Prepare for Training	Training Preparations	Optional
		TR.095	Conduct Train-the-Trainer Workshops	Trained Trainers	Optional
	(C.TG.TA) Execute Technical Readiness Assessment				
		TA.125	Execute Technical Readiness Assessment	Technical Readiness Assessment Recommendations	Optional
	(C.TG.IC) Implementation Checkpoint				
		WM.055.3	Conduct Implementation Checkpoint	Implementation Checkpoint Meeting/Approval to Proceed	Core
	(C.TG.PM) Project Management				
		PEC.MPE.3	Manage Project Execution	Managed Project Assets	Core
Transition [D]					
	(D.TG.PT) Prepare for Transition				
		TS.045	Remove Test Data from Production	Clean Production Environment	Optional
		TS.050	Migrate Configuration to Production	Configured Production Environment	Core
		TS.051	Migrate Integrations and Extensions to Production	Migrate Integrations and Extensions in Production	Optional
		CV.065.3	Load, Reconcile & Validate Data Loads in Production	Validated Data	Optional
	(D.TG.FV) Final Validation				
		TE.120	Conduct Final Validation Review with Users & Stakeholders	Validated Production Environment	Core
	(D.TG.TR) Training				
		TR.100	Conduct End-User Training	Skilled Users	Optional
	(D.TG.TS) Transition to Production				

Phase	Activity/Task Group	Task ID	Task Name	Work Product	Core/Optional
		TS.052	Implement Production Support Infrastructure	Production Support Infrastructure	Core
		TS.058	Verify Production & Operational Readiness	Production Ready System	Core
		TS.060	Begin Production Use	System in Production	Core
	(D.TG.IC) Implementation Checkpoint				
		WM.055.4	Conduct Implementation Checkpoint	Implementation Checkpoint Meeting/Approval to Proceed	Core
	(D.TG.PM) Project Management				
		PEC.MPE.4	Manage Project Execution	Managed Project Assets	Core
Realization [E]					
	(E.TG.SP) Stabilization				
		PS.005	Manage Transition to Steady-State Operations	Steady-State Operations	Core
		PS.065	Post Go-Live Support	Post Go-Live Support	Core
	(E.TG.TC) Transition to Customer Relationship Manager				
		PS.070	Execute Handoff to Customer Relationship Manager	Customer Relationship Manager Handoff	Optional
	(E.TG.PM) Project Management				
		PEC.MPE.5	Manage Project Execution	Managed Project Assets	Core
	(E.TG.PC) Project Closure				
		PC.GA	Gain Acceptance	Final Acceptance Certificate	Core
		PC.CPC	Close Processes and Contract	Closed Processes and Contract	Core
